


Task Critical Task Milestone Summary

ID	Task Name	Duration	Start	Finish	Qtr 2, 2021 Apr May Jun	Qtr 3, 2021 Jul Aug Sep	Qtr 4, 2021 Oct Nov Dec	Qtr 1, 2022 Jan Feb Mar	Qtr 2, 2022 Apr May Jun	Qtr 3, 2022 Jul Aug Sep	Qtr 4, 2022 Oct Nov Dec	Qtr 1, 2023 Jan Feb Mar	Qtr 2, 2023 Apr May Jun	Qtr 3, 2023 Jul Aug Sep	Qtr 4, 2023 Oct Nov Dec	Qtr 1, 2024 Jan Feb Mar	Qtr 2, 2024 Apr May Jun	Qtr 3, 2024 Jul Aug Sep	Qtr 4, 2024 Oct Nov Dec	Qtr 1, 2025 Jan Feb Mar	Qtr 2, 2025 Apr May Jun	Qtr 3, 2025 Jul Aug Sep	Qtr 4, 2025 Oct Nov Dec	Qtr 1, 2026 Jan Feb Mar	Qtr 2, 2026 Apr May Jun	
53	Proposal of Security System (PS1.53A)	14 days	Tue 20/4/21	Mon 3/5/21																						
54	Professional photographer and use of aircraft (PS1.55S)	1 day	Thu 29/4/21	Thu 29/4/21																						
55	Procedures for selecting Subcontractors (ACC C9)	21 days	Tue 20/4/21	Mon 10/5/21																						
56	Competitive process for selection of supplier of plant and materials, equipment and insurance (ACC C11)	21 days	Tue 20/4/21	Mon 10/5/21																						
57	Designated bank and payment of wages to all the site personnel (PS29.05)	14 days	Tue 20/4/21	Mon 3/5/21																						
58	Hygiene and Welfare facilities (PS1.50A)	14 days	Thu 29/4/21	Wed 12/5/21																						
59	Necessary Arrangement with Bank to implement the arrangement on payment of wages to Workers (ACC E6)	14 days	Thu 29/4/21	Wed 12/5/21																						
60	Professional video production company and a competent video director (PS1.119)	14 days	Thu 29/4/21	Wed 12/5/21																						
61	Details of ESIS and DRIS System (PS1.129)	14 days	Thu 29/4/21	Wed 12/5/21																						
62	Hoarding Plan (PS1.48)	14 days	Thu 29/4/21	Wed 12/5/21																						
63	Transport for PM and Supervisor (PS1.52)	14 days	Thu 29/4/21	Wed 12/5/21																						
64	Sub-contractor Management Plan (ACC C5)	30 days	Tue 20/4/21	Wed 19/5/21																						
65	Weather Protection Scheme against inclement weather (PS1.86)	30 days	Thu 29/4/21	Fri 28/5/21																						
66	Temp Drainage Management Plan	30 days	Thu 29/4/21	Fri 28/5/21																						
67	Contingency Plan to deal with Flooding	30 days	Thu 29/4/21	Fri 28/5/21																						
68	Supply of Brand New Survey Equipment (PS Appendix 1.17)	30 days	Thu 29/4/21	Fri 28/5/21																						
69	Site Uniform (PS1.88)	30 days	Thu 29/4/21	Fri 28/5/21																						
70	PII insurance Policy	60 days	Tue 20/4/21	Fri 18/6/21																						
71	Book with a certification body acceptable to the Employer the date of audit for the ISO 9001:2015 certification	90 days	Thu 29/4/21	Tue 27/7/21																						
72	Completion of Initial General Submission	0 days	Fri 28/5/21	Fri 28/5/21																						
73	Programme	104 days	Tue 20/4/21	Sun 1/8/21																						
74	First Programme (CDP1 3)	14 days	Tue 20/4/21	Mon 3/5/21																						
75	Acceptance of the First Programme	30 days	Tue 4/5/21	Wed 2/6/21																						
76	Expanded and more detailed version of the first programme (PSA 1.3)	60 days	Thu 3/6/21	Sun 1/8/21																						
77	First Monthly Progress Report (PS1.08A)	30 days	Tue 4/5/21	Wed 2/6/21																						
78	Completion of Initial Programme Submission	0 days	Wed 2/6/21	Wed 2/6/21																						
79	Appointment of Personnel	99 days	Tue 20/4/21	Tue 27/7/21																						
80	Contractor's Labour Officer (PS29.09)	7 days	Tue 20/4/21	Mon 26/4/21																						
81	Contractor's Surveyor (PS1.09)	7 days	Thu 29/4/21	Wed 5/5/21																						
82	List of Staff for Construction Management Team (ACC D1)	14 days	Thu 29/4/21	Wed 12/5/21																						
83	RSO and SS (ACC D1)	14 days	Thu 29/4/21	Wed 12/5/21																						
84	EO and ES (ACC D1)	14 days	Thu 29/4/21	Wed 12/5/21																						
85	Site Agents and Employees (PS1.12)	14 days	Thu 29/4/21	Wed 12/5/21																						
86	Construction Manager (PS1.12A)	14 days	Thu 29/4/21	Wed 12/5/21																						
87	Construction, Landscape and Land Decontamination Leader (PS1.12B)	14 days	Thu 29/4/21	Wed 12/5/21																						
88	Geotechnical Engineer, Geologist, Geotechnical Supervisor and GFT (1.12C)	14 days	Thu 29/4/21	Wed 12/5/21																						
89	Foreman for Road and Drainage Works	14 days	Thu 29/4/21	Wed 12/5/21																						
90	Particulars of Emergency Unit (PS1.99)	14 days	Thu 29/4/21	Wed 12/5/21																						
91	Tree Supervisor (PS26.02)	30 days	Tue 20/4/21	Wed 19/5/21																						
92	Public Relocation Officer (PS 1.12F)	28 days	Thu 29/4/21	Wed 26/5/21																						
93	Quantity Suretying Clerk (PS1.49)	28 days	Thu 29/4/21	Wed 26/5/21																						
94	Field and Drafting assistant (PS1.49C)	28 days	Thu 29/4/21	Wed 26/5/21																						
95	Independent Checking Engineer (PS1.105)	30 days	Thu 29/4/21	Fri 28/5/21																						
96	Employ CEG and TA (PS1.83)	90 days	Thu 29/4/21	Tue 27/7/21																						
97	BIM Team Leader (PS1.108)	90 days	Thu 29/4/21	Tue 27/7/21																						
98	Completion of Construction Management Team Submission	0 days	Fri 28/5/21	Fri 28/5/21																						
99	Safety	42 days	Tue 20/4/21	Mon 31/5/21																						
100	Draft Construction Health and Safety Plan (ACC D6)	14 days	Tue 20/4/21	Mon 3/5/21																						
101	Ad-hoc meeting with Supervisor to discuss the draft Safety Plan (ACC D6)	7 days	Tue 4/5/21	Mon 10/5/21																						
102	Monthly Reports on Safety Performance (ACC D28)	30 days	Tue 20/4/21	Wed 19/5/21																						
103	Monthly Safety Report	30 days	Tue 20/4/21	Wed 19/5/21																						


Task █ Critical Task █ Milestone ◆ Summary ▬

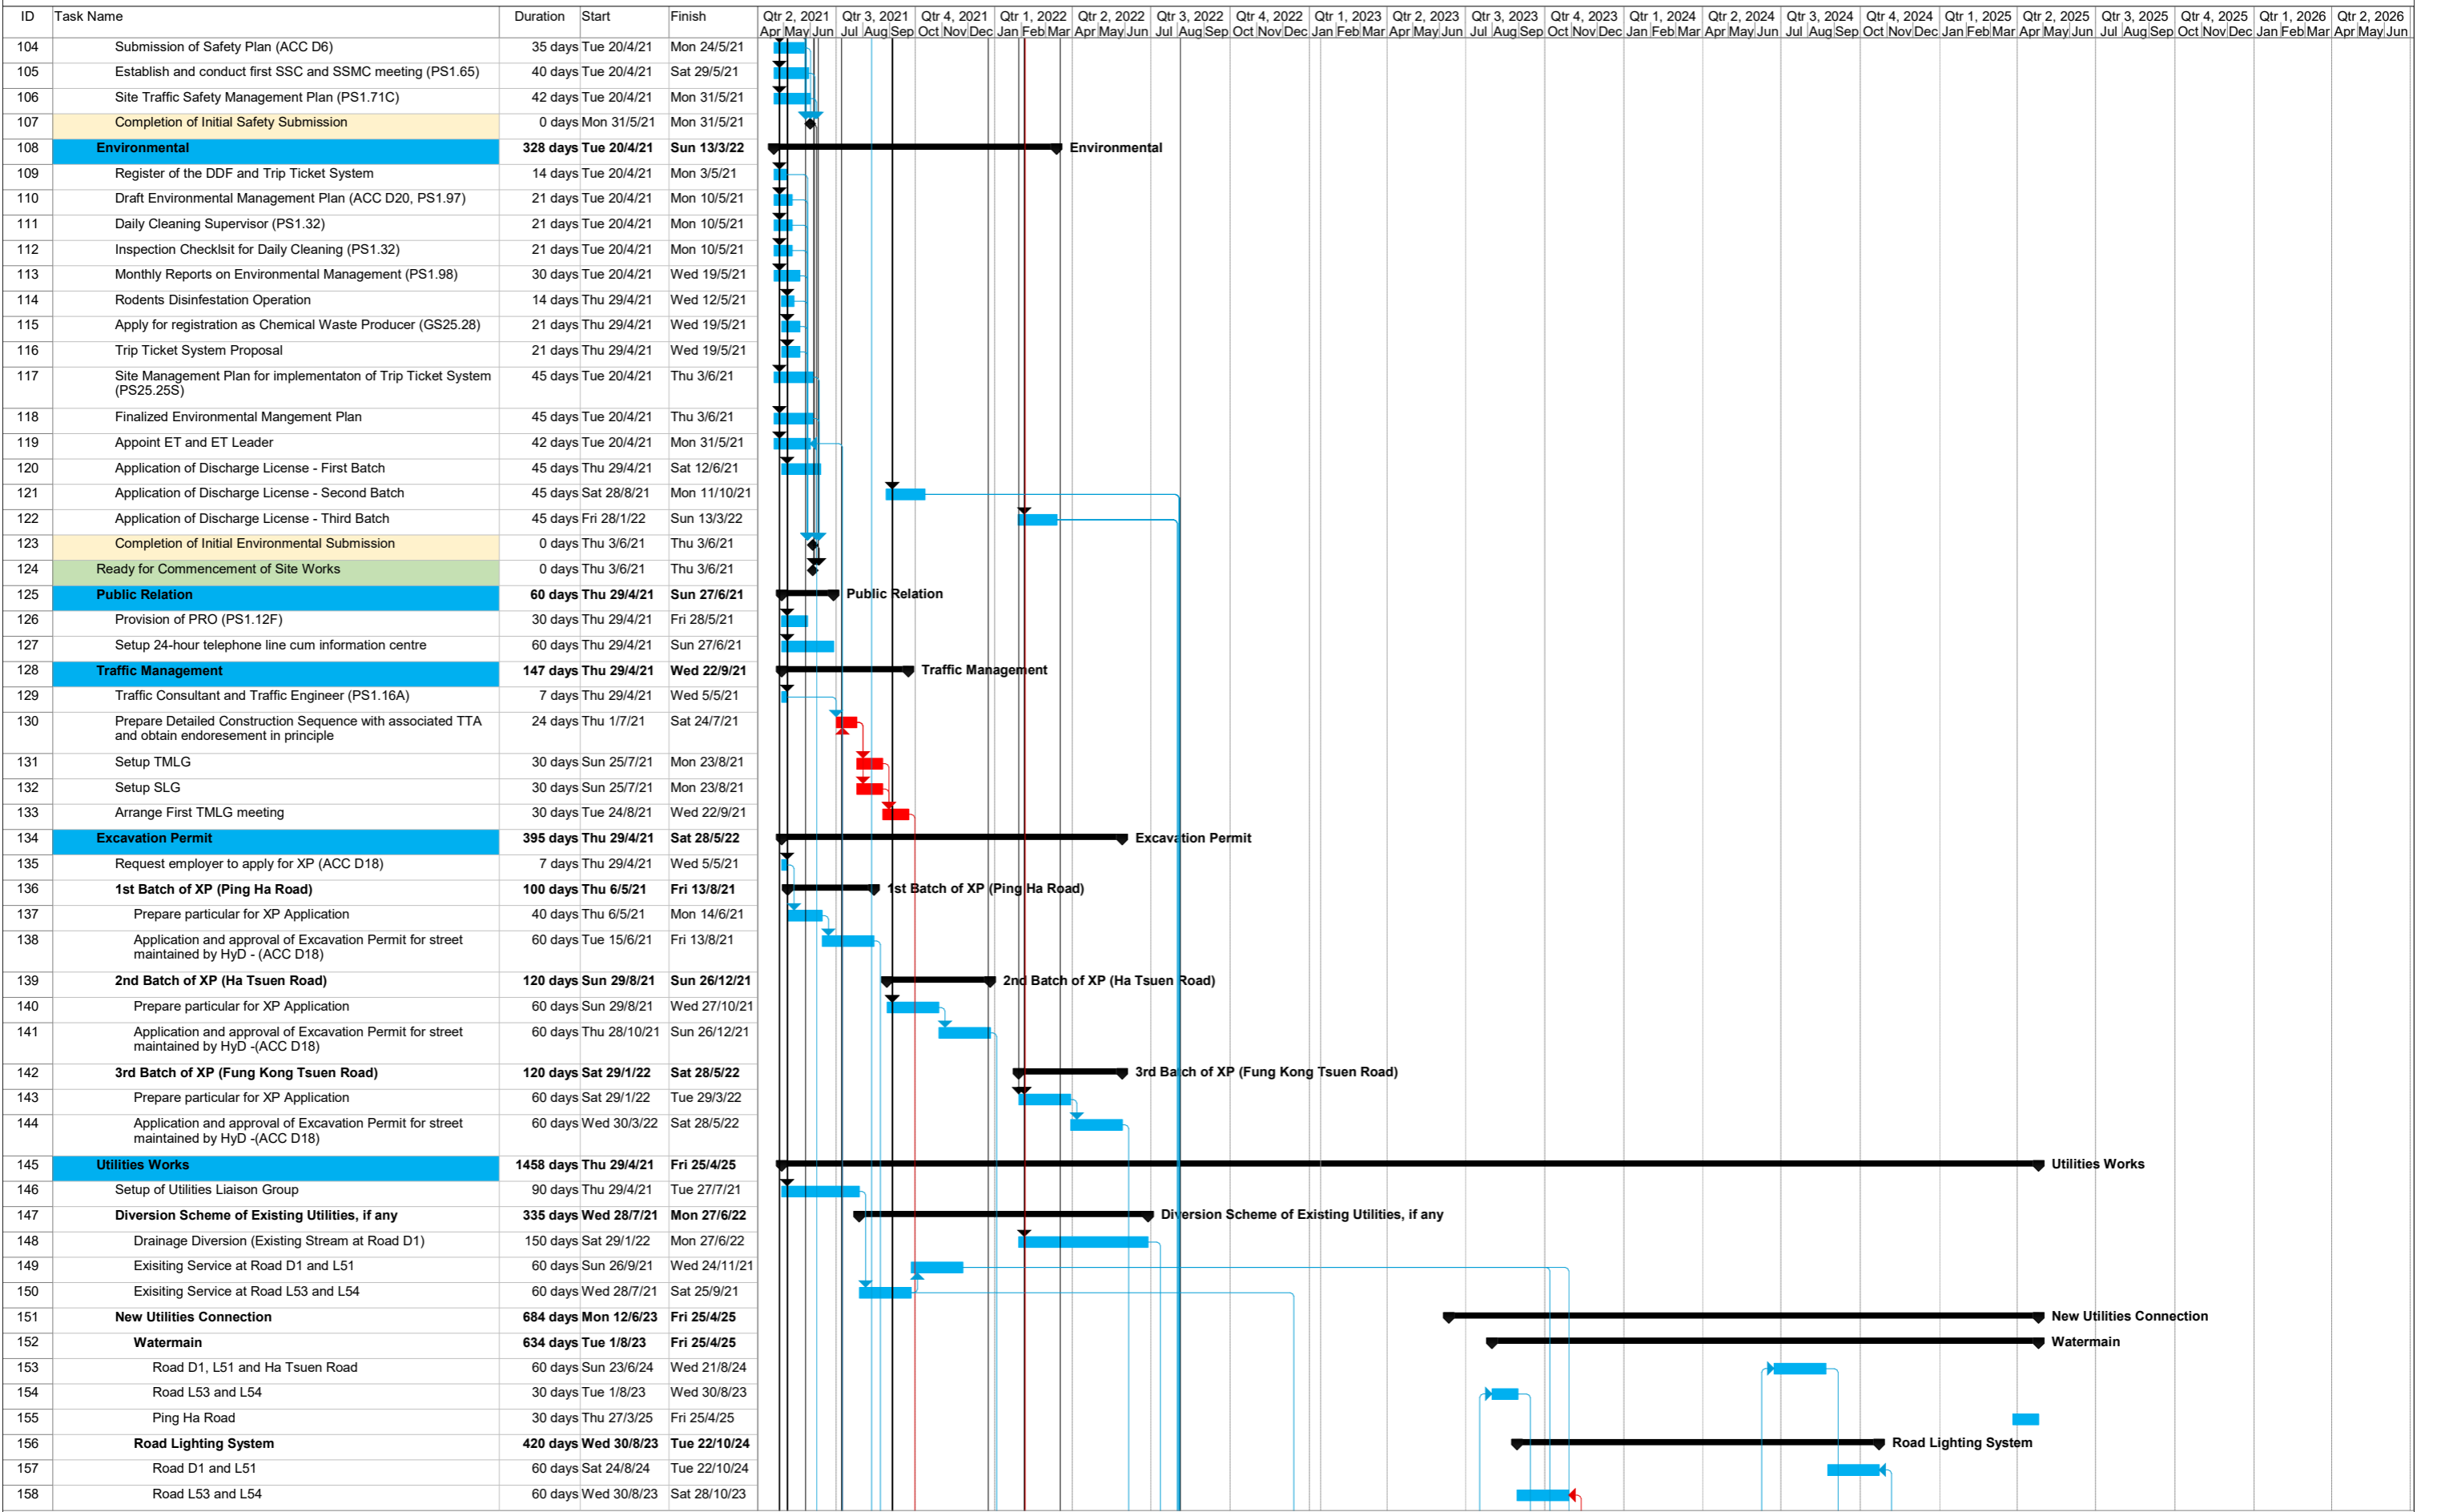

Task [Blue Bar] Critical Task [Red Bar] Milestone [Diamond] Summary [Arrow]

ID	Task Name	Duration	Start	Finish	Qtr 2, 2021 Apr May Jun	Qtr 3, 2021 Jul Aug Sep	Qtr 4, 2021 Oct Nov Dec	Qtr 1, 2022 Jan Feb Mar	Qtr 2, 2022 Apr May Jun	Qtr 3, 2022 Jul Aug Sep	Qtr 4, 2022 Oct Nov Dec	Qtr 1, 2023 Jan Feb Mar	Qtr 2, 2023 Apr May Jun	Qtr 3, 2023 Jul Aug Sep	Qtr 4, 2023 Oct Nov Dec	Qtr 1, 2024 Jan Feb Mar	Qtr 2, 2024 Apr May Jun	Qtr 3, 2024 Jul Aug Sep	Qtr 4, 2024 Oct Nov Dec	Qtr 1, 2025 Jan Feb Mar	Qtr 2, 2025 Apr May Jun	Qtr 3, 2025 Jul Aug Sep	Qtr 4, 2025 Oct Nov Dec	Qtr 1, 2026 Jan Feb Mar	Qtr 2, 2026 Apr May Jun
159	CLP	379 days	Mon 12/6/23	Mon 24/6/24																					
160	Road D1 and L51	60 days	Fri 26/4/24	Mon 24/6/24																					
161	Road L53 and L54	60 days	Mon 12/6/23	Thu 10/8/23																					
162	Telecom (HKT, HGC, HKBN)	379 days	Mon 12/6/23	Mon 24/6/24																					
163	Road D1 and L51	60 days	Fri 26/4/24	Mon 24/6/24																					
164	Road L53 and L54	60 days	Mon 12/6/23	Thu 10/8/23																					
165	Procurement	300 days	Wed 28/4/21	Mon 21/2/22																					
166	Subcontracting / Procurement	132 days	Thu 29/4/21	Tue 7/9/21																					
167	Traffic Consultant	63 days	Thu 29/4/21	Wed 30/6/21																					
168	Subletting	28 days	Thu 29/4/21	Wed 26/5/21																					
169	Submission and Approval	35 days	Thu 27/5/21	Wed 30/6/21																					
170	Independent Checking Engineer	63 days	Thu 29/4/21	Wed 30/6/21																					
171	Subletting	28 days	Thu 29/4/21	Wed 26/5/21																					
172	Submission and Approval	35 days	Thu 27/5/21	Wed 30/6/21																					
173	PM's Accomodation (MiC Method)	63 days	Thu 29/4/21	Wed 30/6/21																					
174	Subletting	28 days	Thu 29/4/21	Wed 26/5/21																					
175	Submission and Approval	35 days	Thu 27/5/21	Wed 30/6/21																					
176	Environmental Team and Team Leader	63 days	Thu 29/4/21	Wed 30/6/21																					
177	Subletting	28 days	Thu 29/4/21	Wed 26/5/21																					
178	Submission and Approval	35 days	Thu 27/5/21	Wed 30/6/21																					
179	Tree Survey and Treatment	63 days	Thu 29/4/21	Wed 30/6/21																					
180	Subletting	28 days	Thu 29/4/21	Wed 26/5/21																					
181	Submission and Approval	35 days	Thu 27/5/21	Wed 30/6/21																					
182	Specialist for Decontamination Works	63 days	Thu 29/4/21	Wed 30/6/21																					
183	Subletting	28 days	Thu 29/4/21	Wed 26/5/21																					
184	Submission and Approval	35 days	Thu 27/5/21	Wed 30/6/21																					
185	BIM Service	63 days	Thu 29/4/21	Wed 30/6/21																					
186	Subletting	28 days	Thu 29/4/21	Wed 26/5/21																					
187	Submission and Approval	35 days	Thu 27/5/21	Wed 30/6/21																					
188	Rebar Supply	63 days	Wed 7/7/21	Tue 7/9/21																					
189	Subletting	28 days	Wed 7/7/21	Tue 3/8/21																					
190	Submission and Approval	35 days	Wed 4/8/21	Tue 7/9/21																					
191	Concrete Supply	63 days	Wed 7/7/21	Tue 7/9/21																					
192	Subletting	28 days	Wed 7/7/21	Tue 3/8/21																					
193	Submission and Approval	35 days	Wed 4/8/21	Tue 7/9/21																					
194	Bitumen Supply and Paving	63 days	Wed 7/7/21	Tue 7/9/21																					
195	Subletting	28 days	Wed 7/7/21	Tue 3/8/21																					
196	Submission and Approval	35 days	Wed 4/8/21	Tue 7/9/21																					
197	Ground Investigation Works	63 days	Wed 7/7/21	Tue 7/9/21																					
198	Subletting	28 days	Wed 7/7/21	Tue 3/8/21																					
199	Submission and Approval	35 days	Wed 4/8/21	Tue 7/9/21																					
200	Demolition Works	63 days	Wed 7/7/21	Tue 7/9/21																					
201	Subletting	28 days	Wed 7/7/21	Tue 3/8/21																					
202	Submission and Approval	35 days	Wed 4/8/21	Tue 7/9/21																					
203	Pipe Jacking Works	63 days	Thu 29/4/21	Wed 30/6/21																					
204	Subletting	28 days	Thu 29/4/21	Wed 26/5/21																					
205	Submission and Approval	35 days	Thu 27/5/21	Wed 30/6/21																					
206	Road Marking	63 days	Wed 7/7/21	Tue 7/9/21																					
207	Subletting	28 days	Wed 7/7/21	Tue 3/8/21																					
208	Submission and Approval	35 days	Wed 4/8/21	Tue 7/9/21																					
209	Road Lighting System (Design and Install)	63 days	Wed 7/7/21	Tue 7/9/21																					
210	Subletting	28 days	Wed 7/7/21	Tue 3/8/21																					
211	Submission and Approval	35 days	Wed 4/8/21	Tue 7/9/21																					
212	Landscaping Works	63 days	Wed 7/7/21	Tue 7/9/21																					
213	Subletting	28 days	Wed 7/7/21	Tue 3/8/21																					
214	Submission and Approval	35 days	Wed 4/8/21	Tue 7/9/21																					
215	E&M Works	63 days	Wed 7/7/21	Tue 7/9/21																					
216	Subletting	28 days	Wed 7/7/21	Tue 3/8/21																					


Task Critical Task Milestone Summary

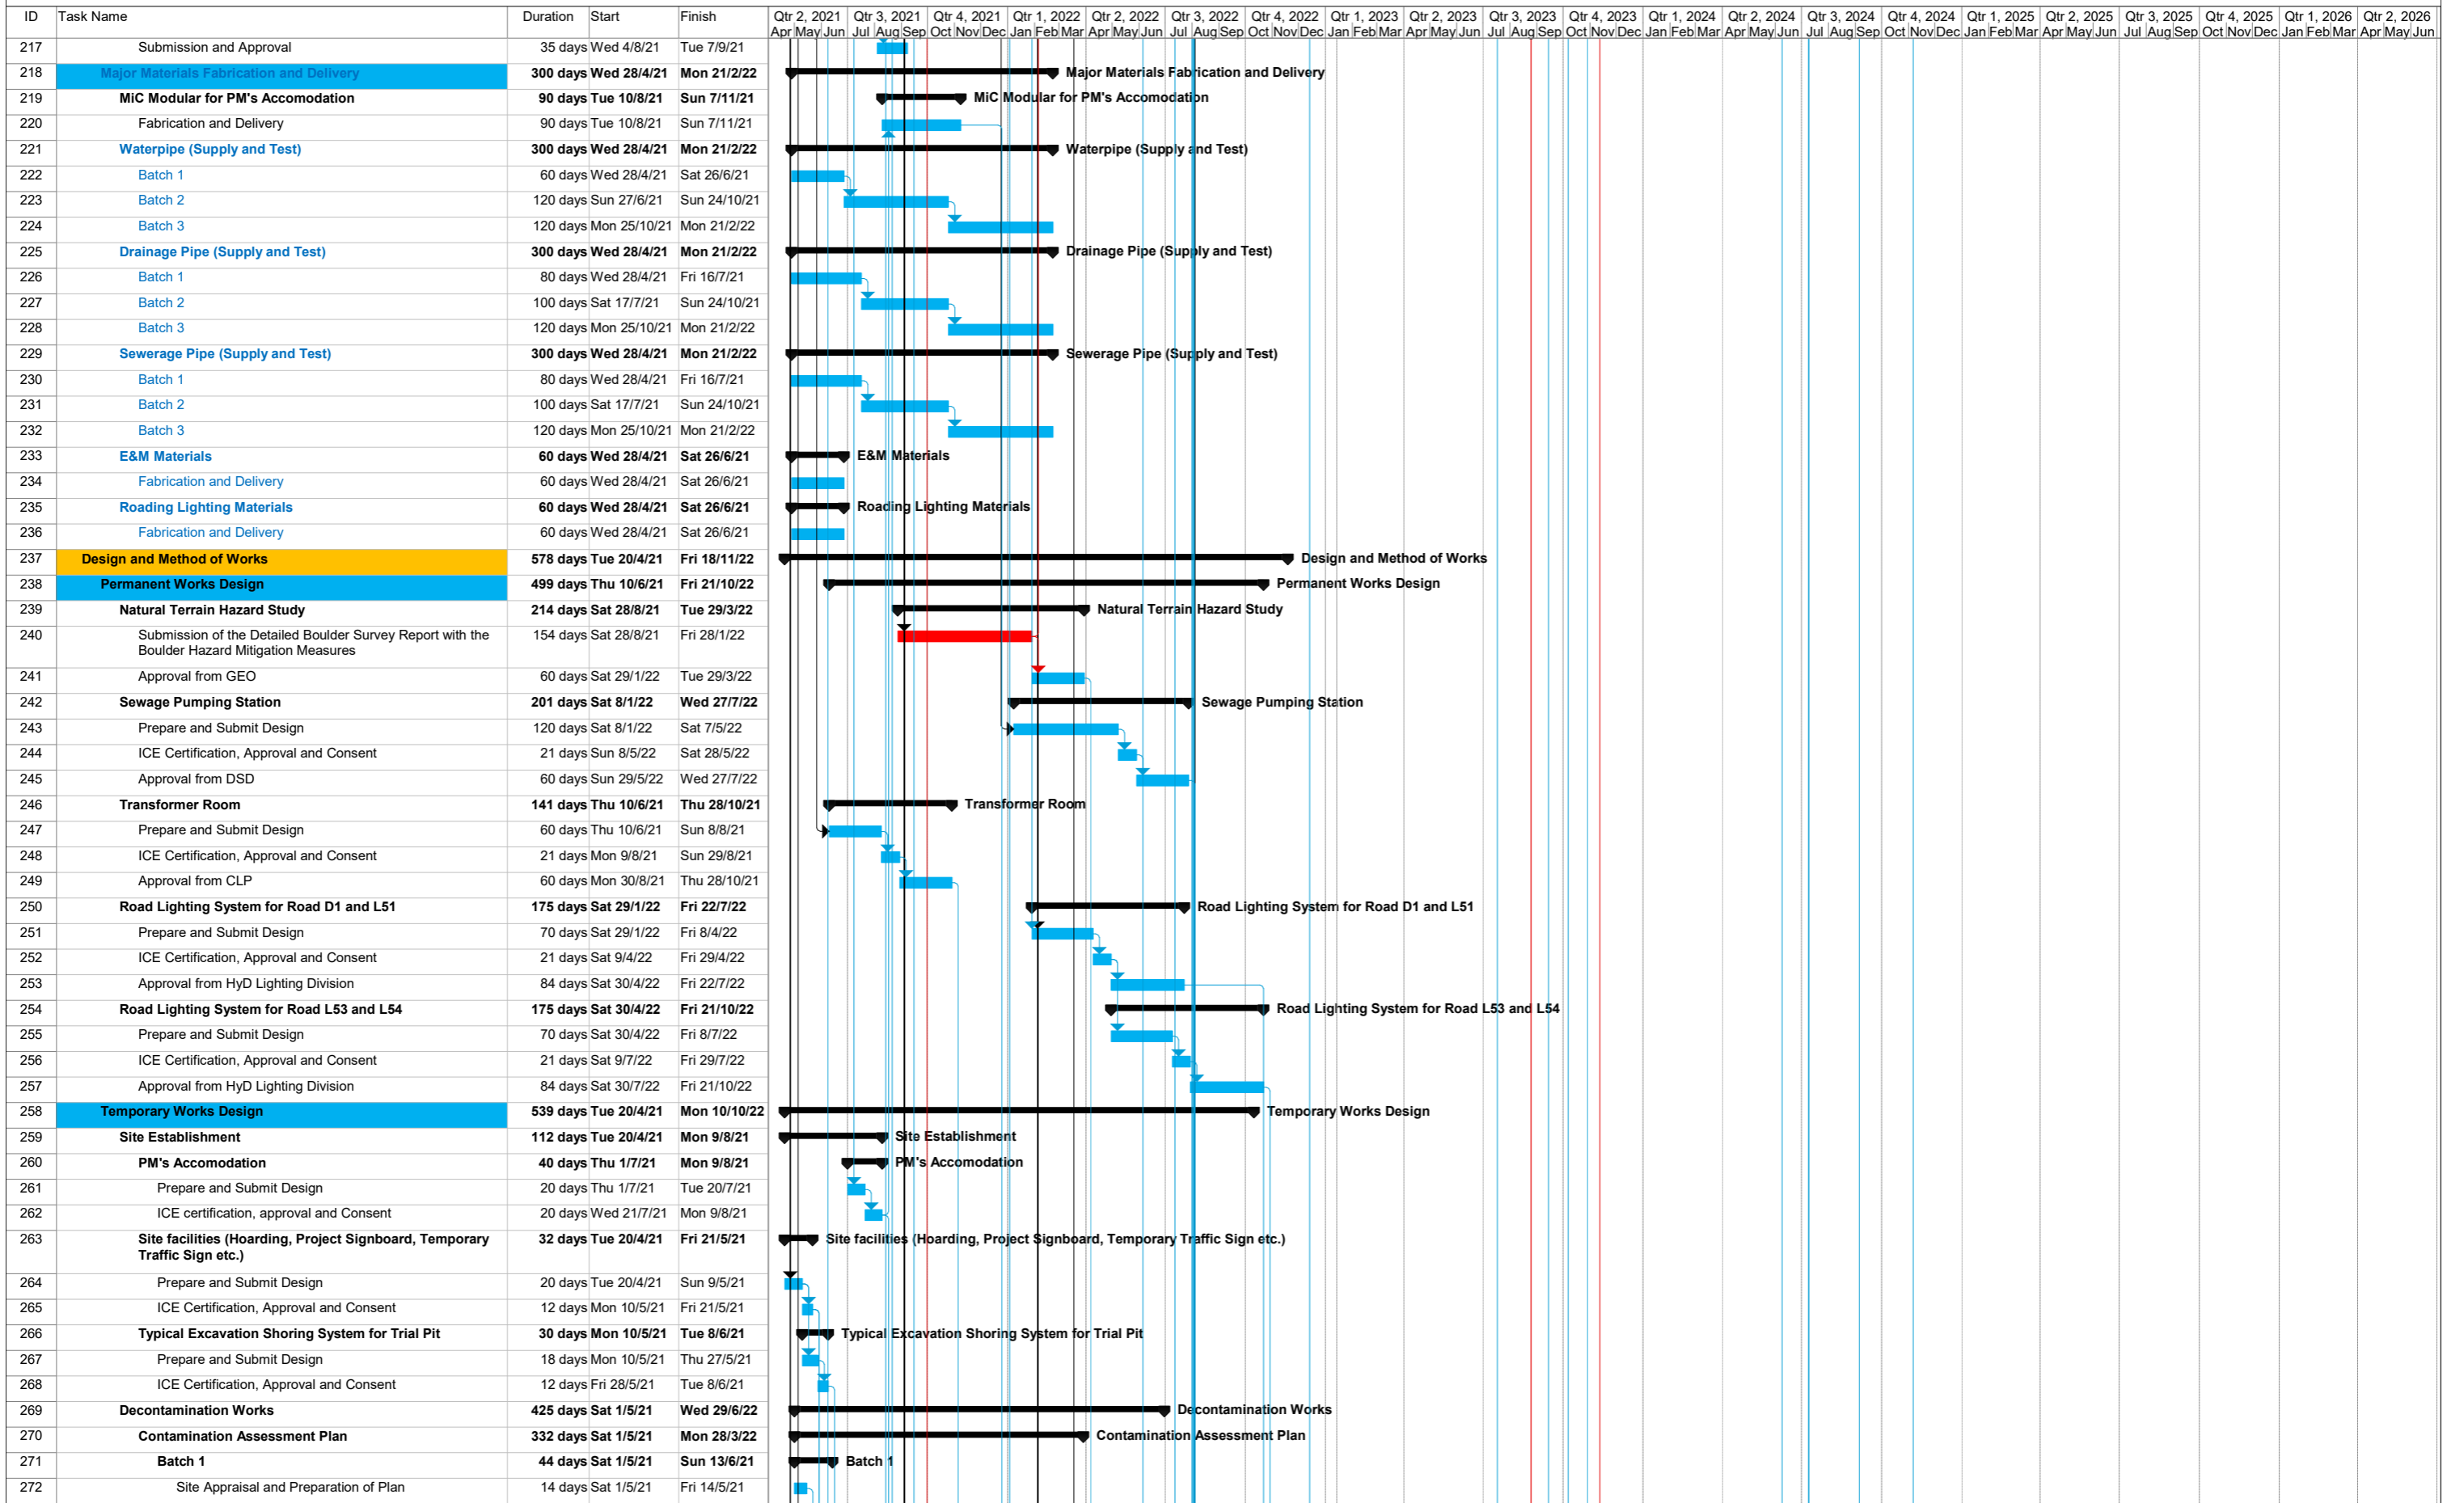


Task Critical Task Milestone Summary

ID	Task Name	Duration	Start	Finish	Qtr 2, 2021	Qtr 3, 2021	Qtr 4, 2021	Qtr 1, 2022	Qtr 2, 2022	Qtr 3, 2022	Qtr 4, 2022	Qtr 1, 2023	Qtr 2, 2023	Qtr 3, 2023	Qtr 4, 2023	Qtr 1, 2024	Qtr 2, 2024	Qtr 3, 2024	Qtr 4, 2024	Qtr 1, 2025	Qtr 2, 2025	Qtr 3, 2025	Qtr 4, 2025	Qtr 1, 2026	Qtr 2, 2026			
273	Submission and Endorsement by EPD	30 days	Sat 15/5/21	Sun 13/6/21																								
274	Batch 2	55 days	Mon 31/1/22	Sat 26/3/22																								
275	Site Appraisal and Preparation of Plan	25 days	Mon 31/1/22	Thu 24/2/22																								
276	Submission and Endorsement by EPD	30 days	Fri 25/2/22	Sat 26/3/22																								
277	Batch 3	55 days	Wed 2/2/22	Mon 28/3/22																								
278	Site Appraisal and Preparation of Plan	25 days	Wed 2/2/22	Sat 26/2/22																								
279	Submission and Endorsement by EPD	30 days	Sun 27/2/22	Mon 28/3/22																								
280	Cement Solidification System	48 days	Fri 13/5/22	Wed 29/6/22																								
281	Prepare and Submit Design	24 days	Fri 13/5/22	Sun 5/6/22																								
282	ICE Certification, Approval and Consent	24 days	Mon 6/6/22	Wed 29/6/22																								
283	Biopile System	48 days	Fri 13/5/22	Wed 29/6/22																								
284	Prepare and Submit Design	24 days	Fri 13/5/22	Sun 5/6/22																								
285	ICE Certification, Approval and Consent	24 days	Mon 6/6/22	Wed 29/6/22																								
286	Demolition Works	84 days	Sun 29/8/21	Sat 20/11/21																								
287	Demolition of RC Structures less than 2-storey	48 days	Sun 29/8/21	Fri 15/10/21																								
288	Prepare and Submit Design	24 days	Sun 29/8/21	Tue 21/9/21																								
289	ICE Certification, Approval and Consent	24 days	Wed 22/9/21	Fri 15/10/21																								
290	Demolition of Steel Frame Structures	60 days	Wed 22/9/21	Sat 20/11/21																								
291	Prepare and Submit Design	36 days	Wed 22/9/21	Wed 27/10/21																								
292	ICE Certification, Approval and Consent	24 days	Thu 28/10/21	Sat 20/11/21																								
293	Drainage, Sewerage and Water Works	60 days	Sun 29/8/21	Wed 27/10/21																								
294	ELS Design (By Shoring Method)	36 days	Sun 29/8/21	Sun 3/10/21																								
295	Prepare and Submit Design	12 days	Sun 29/8/21	Thu 9/9/21																								
296	ICE Certification, Approval and Consent	24 days	Fri 10/9/21	Sun 3/10/21																								
297	Temporary Utility Support	36 days	Fri 10/9/21	Fri 15/10/21																								
298	Prepare and Submit Design	12 days	Fri 10/9/21	Tue 21/9/21																								
299	ICE Certification, Approval and Consent	24 days	Wed 22/9/21	Fri 15/10/21																								
300	Formwork Design for Manhole Construction	36 days	Wed 22/9/21	Wed 27/10/21																								
301	Prepare and Submit Design	12 days	Wed 22/9/21	Sun 3/10/21																								
302	ICE Certification, Approval and Consent	24 days	Mon 4/10/21	Wed 27/10/21																								
303	Geotechnical Works	48 days	Wed 30/3/22	Mon 16/5/22																								
304	Working Platform	36 days	Wed 30/3/22	Wed 4/5/22																								
305	Prepare and Submit Design	12 days	Wed 30/3/22	Sun 10/4/22																								
306	ICE Certification, Approval and Consent	24 days	Mon 11/4/22	Wed 4/5/22																								
307	Formwork Design for RC Structures	36 days	Mon 11/4/22	Mon 16/5/22																								
308	Prepare and Submit Design	12 days	Mon 11/4/22	Fri 22/4/22																								
309	ICE Certification, Approval and Consent	24 days	Mon 11/4/22	Mon 16/5/22																								
310	Pipe Jacking	60 days	Sat 14/8/21	Tue 12/10/21																								
311	ELS Design (By Shoring Method)	60 days	Sat 14/8/21	Tue 12/10/21																								
312	Prepare and Submit Design	30 days	Sat 14/8/21	Sun 12/9/21																								
313	ICE Certification, Approval and Consent	30 days	Mon 13/9/21	Tue 12/10/21																								
314	Retaining Wall	214 days	Sat 28/8/21	Tue 29/3/22																								
315	Formwork Design for Lagging Wall Construction (Soldier Pile Wall)	36 days	Sat 29/1/22	Sat 5/3/22																								
316	Prepare and Submit Design	12 days	Sat 29/1/22	Wed 9/2/22																								
317	ICE Certification, Approval and Consent	24 days	Thu 10/2/22	Sat 5/3/22																								
318	Formwork Design for Lagging Wall Construction (Bored Pile Wall)	36 days	Thu 10/2/22	Thu 17/3/22																								
319	Prepare and Submit Design	12 days	Thu 10/2/22	Mon 21/2/22																								
320	ICE Certification, Approval and Consent	24 days	Tue 22/2/22	Thu 17/3/22																								
321	Formwork Design for RC Capping Beam Construction	36 days	Tue 22/2/22	Tue 29/3/22																								
322	Prepare and Submit Design	12 days	Tue 22/2/22	Sat 5/3/22																								
323	ICE Certification, Approval and Consent	24 days	Sun 6/3/22	Tue 29/3/22																								
324	Formwork Design for RC Retaining Wall Construction	36 days	Sat 28/8/21	Sat 2/10/21																								
325	Prepare and Submit Design	12 days	Sat 28/8/21	Wed 8/9/21																								
326	ICE Certification, Approval and Consent	24 days	Thu 9/9/21	Sat 2/10/21																								
327	Detention Pond	36 days	Sat 29/1/22	Sat 5/3/22																								


Task █ Critical Task █ Milestone ◆ Summary ▬

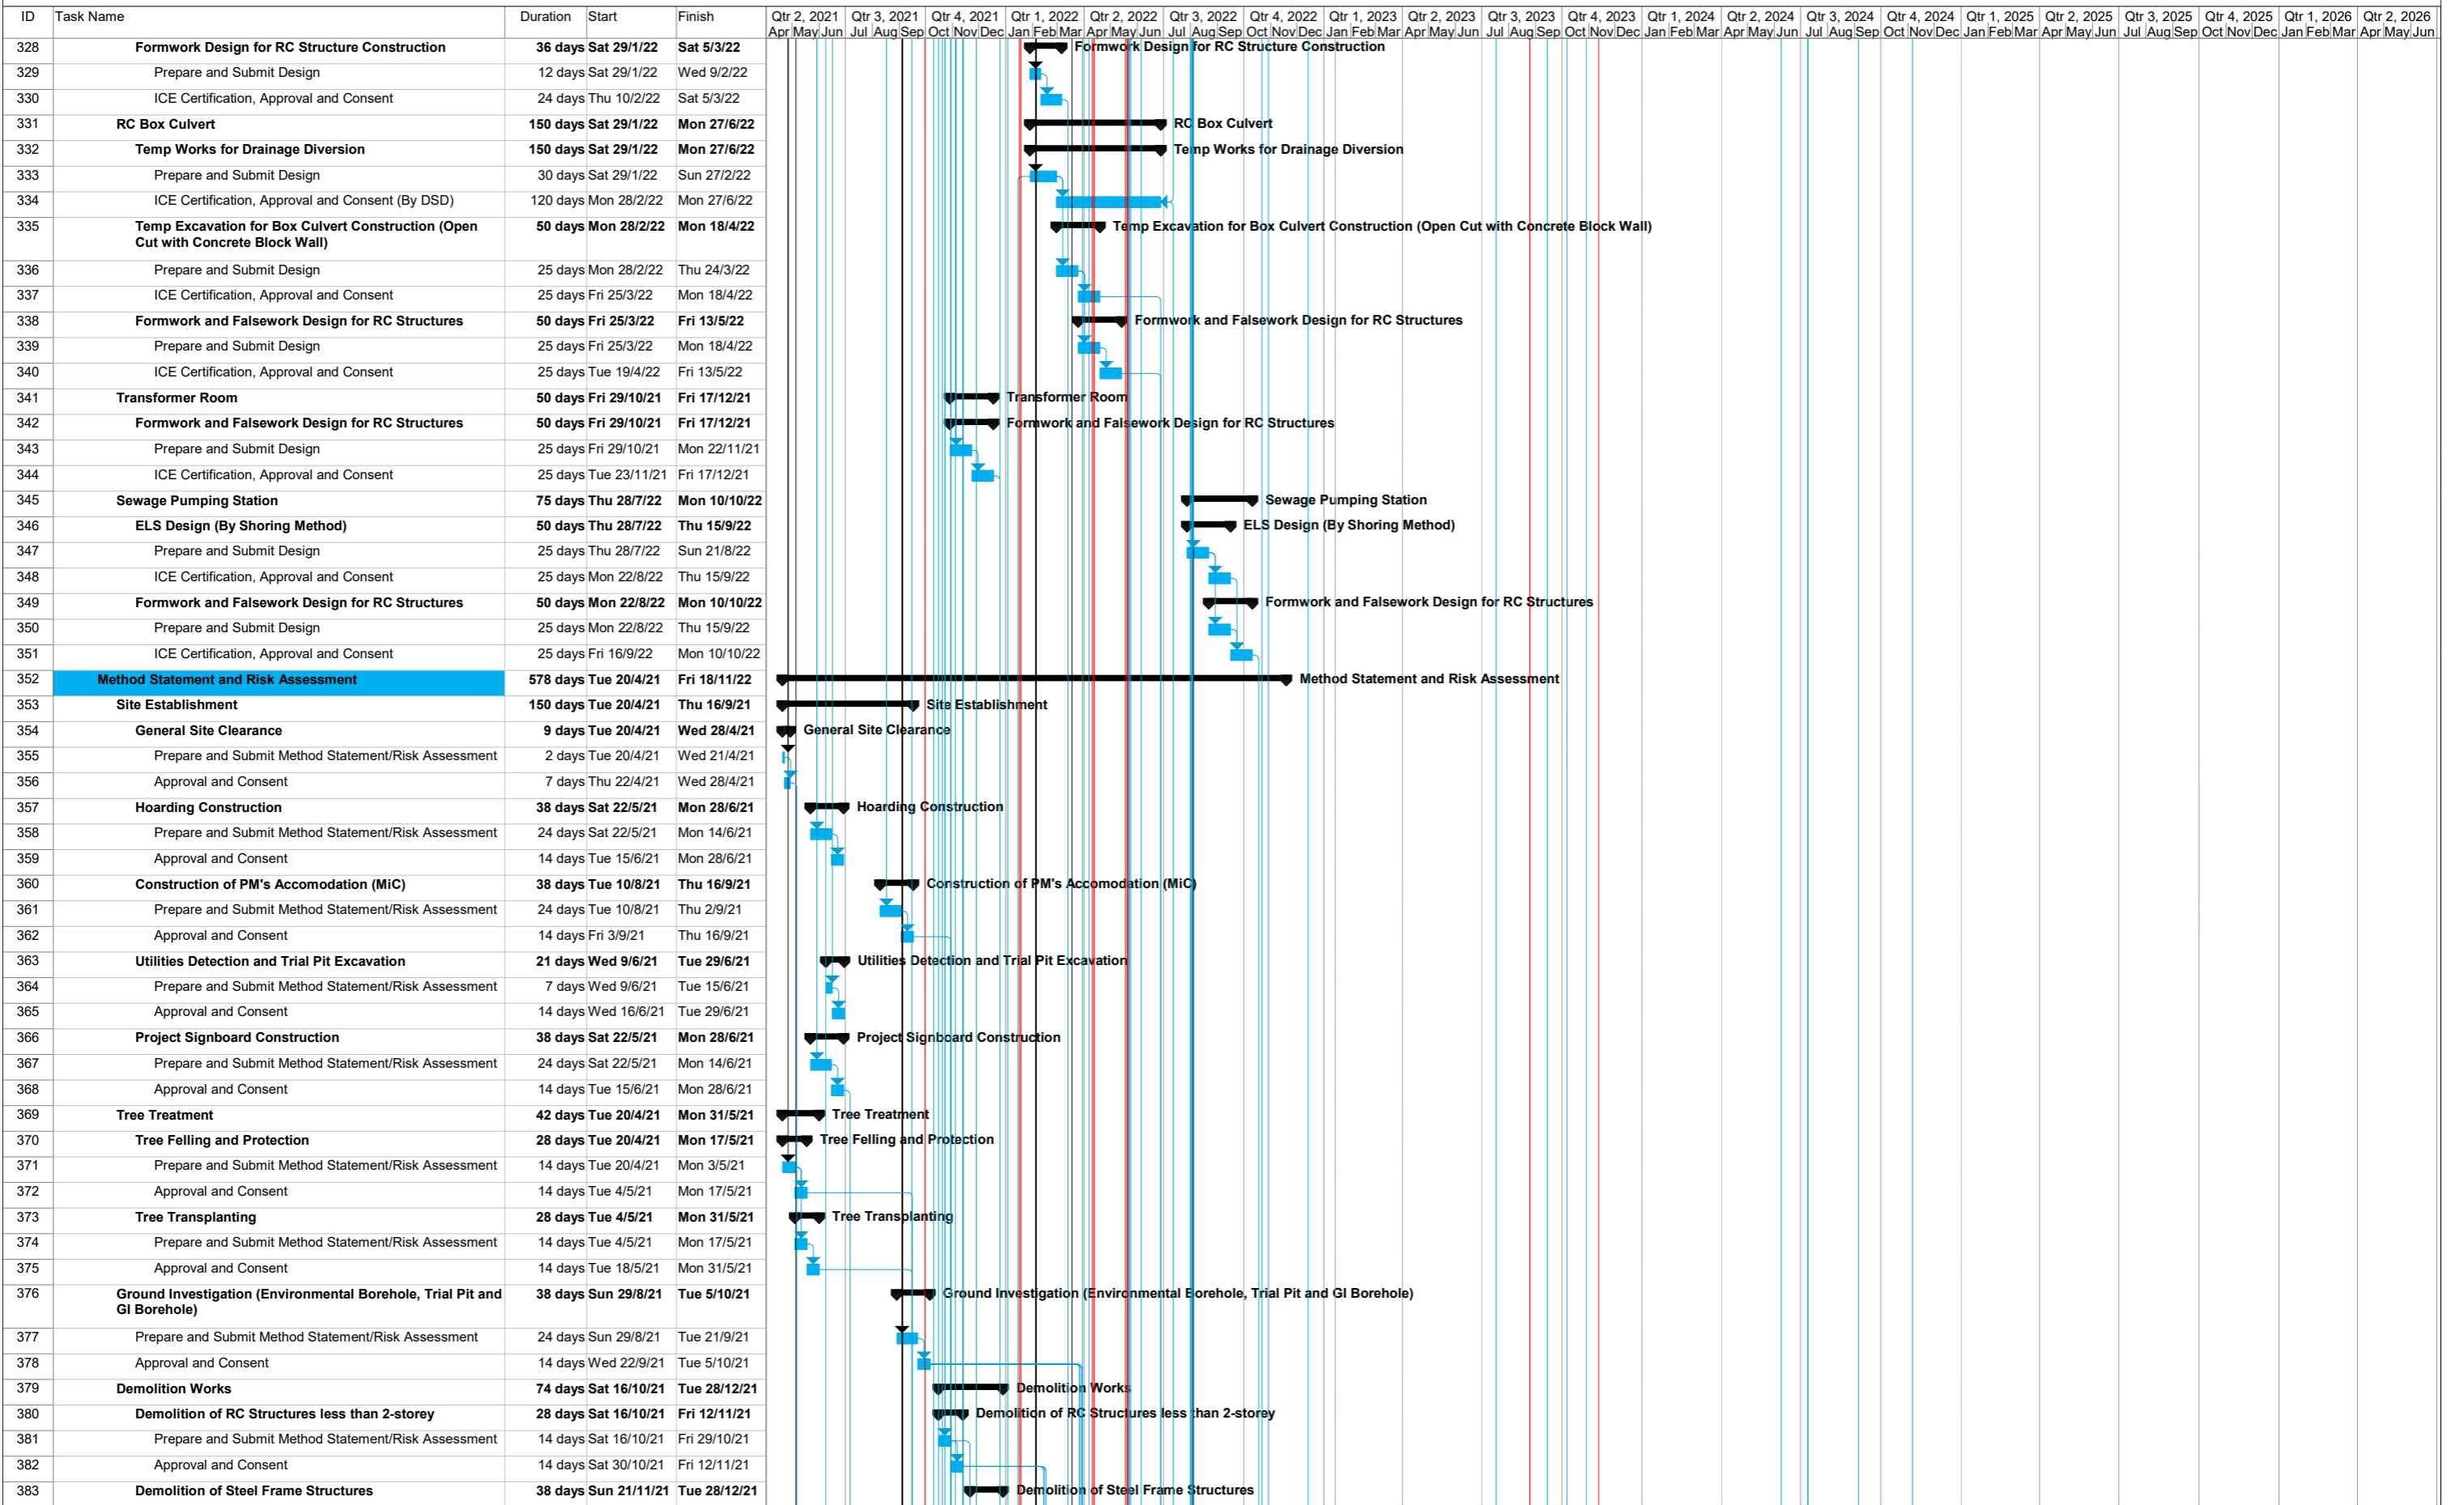


Task █ Critical Task █ Milestone ◆ Summary ▬

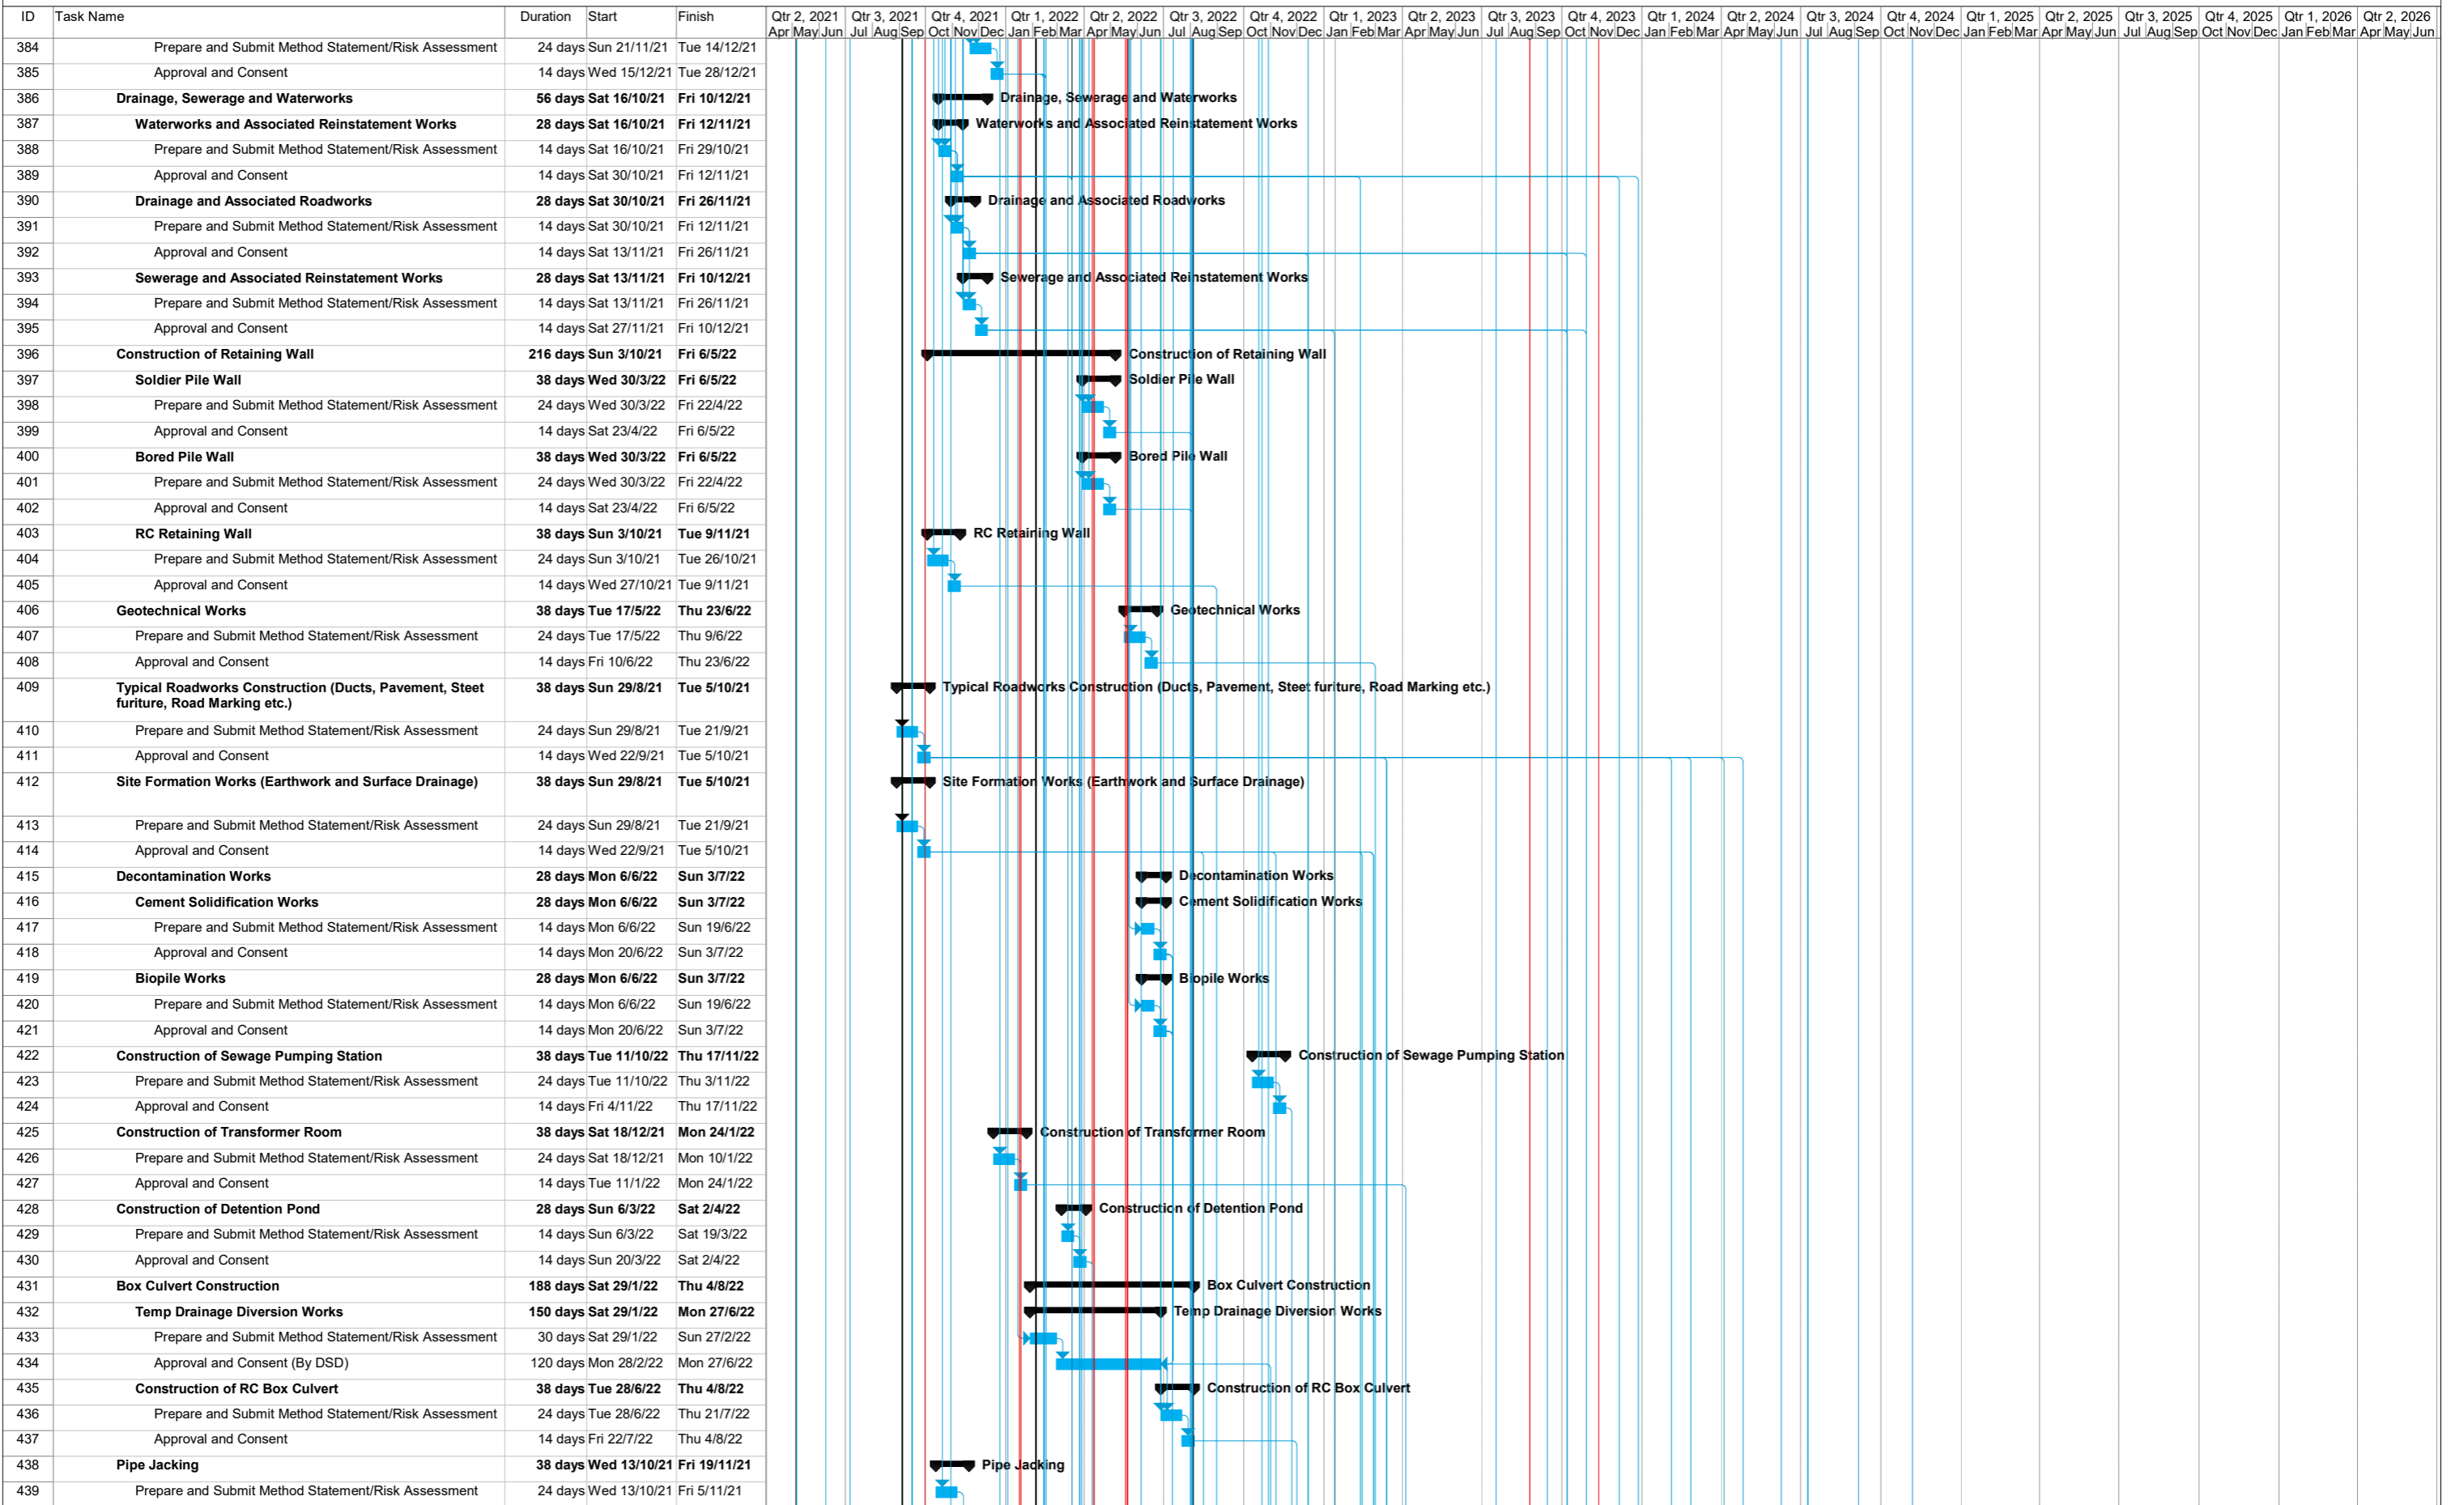


Task █ Critical Task █ Milestone ◆ Summary ▬

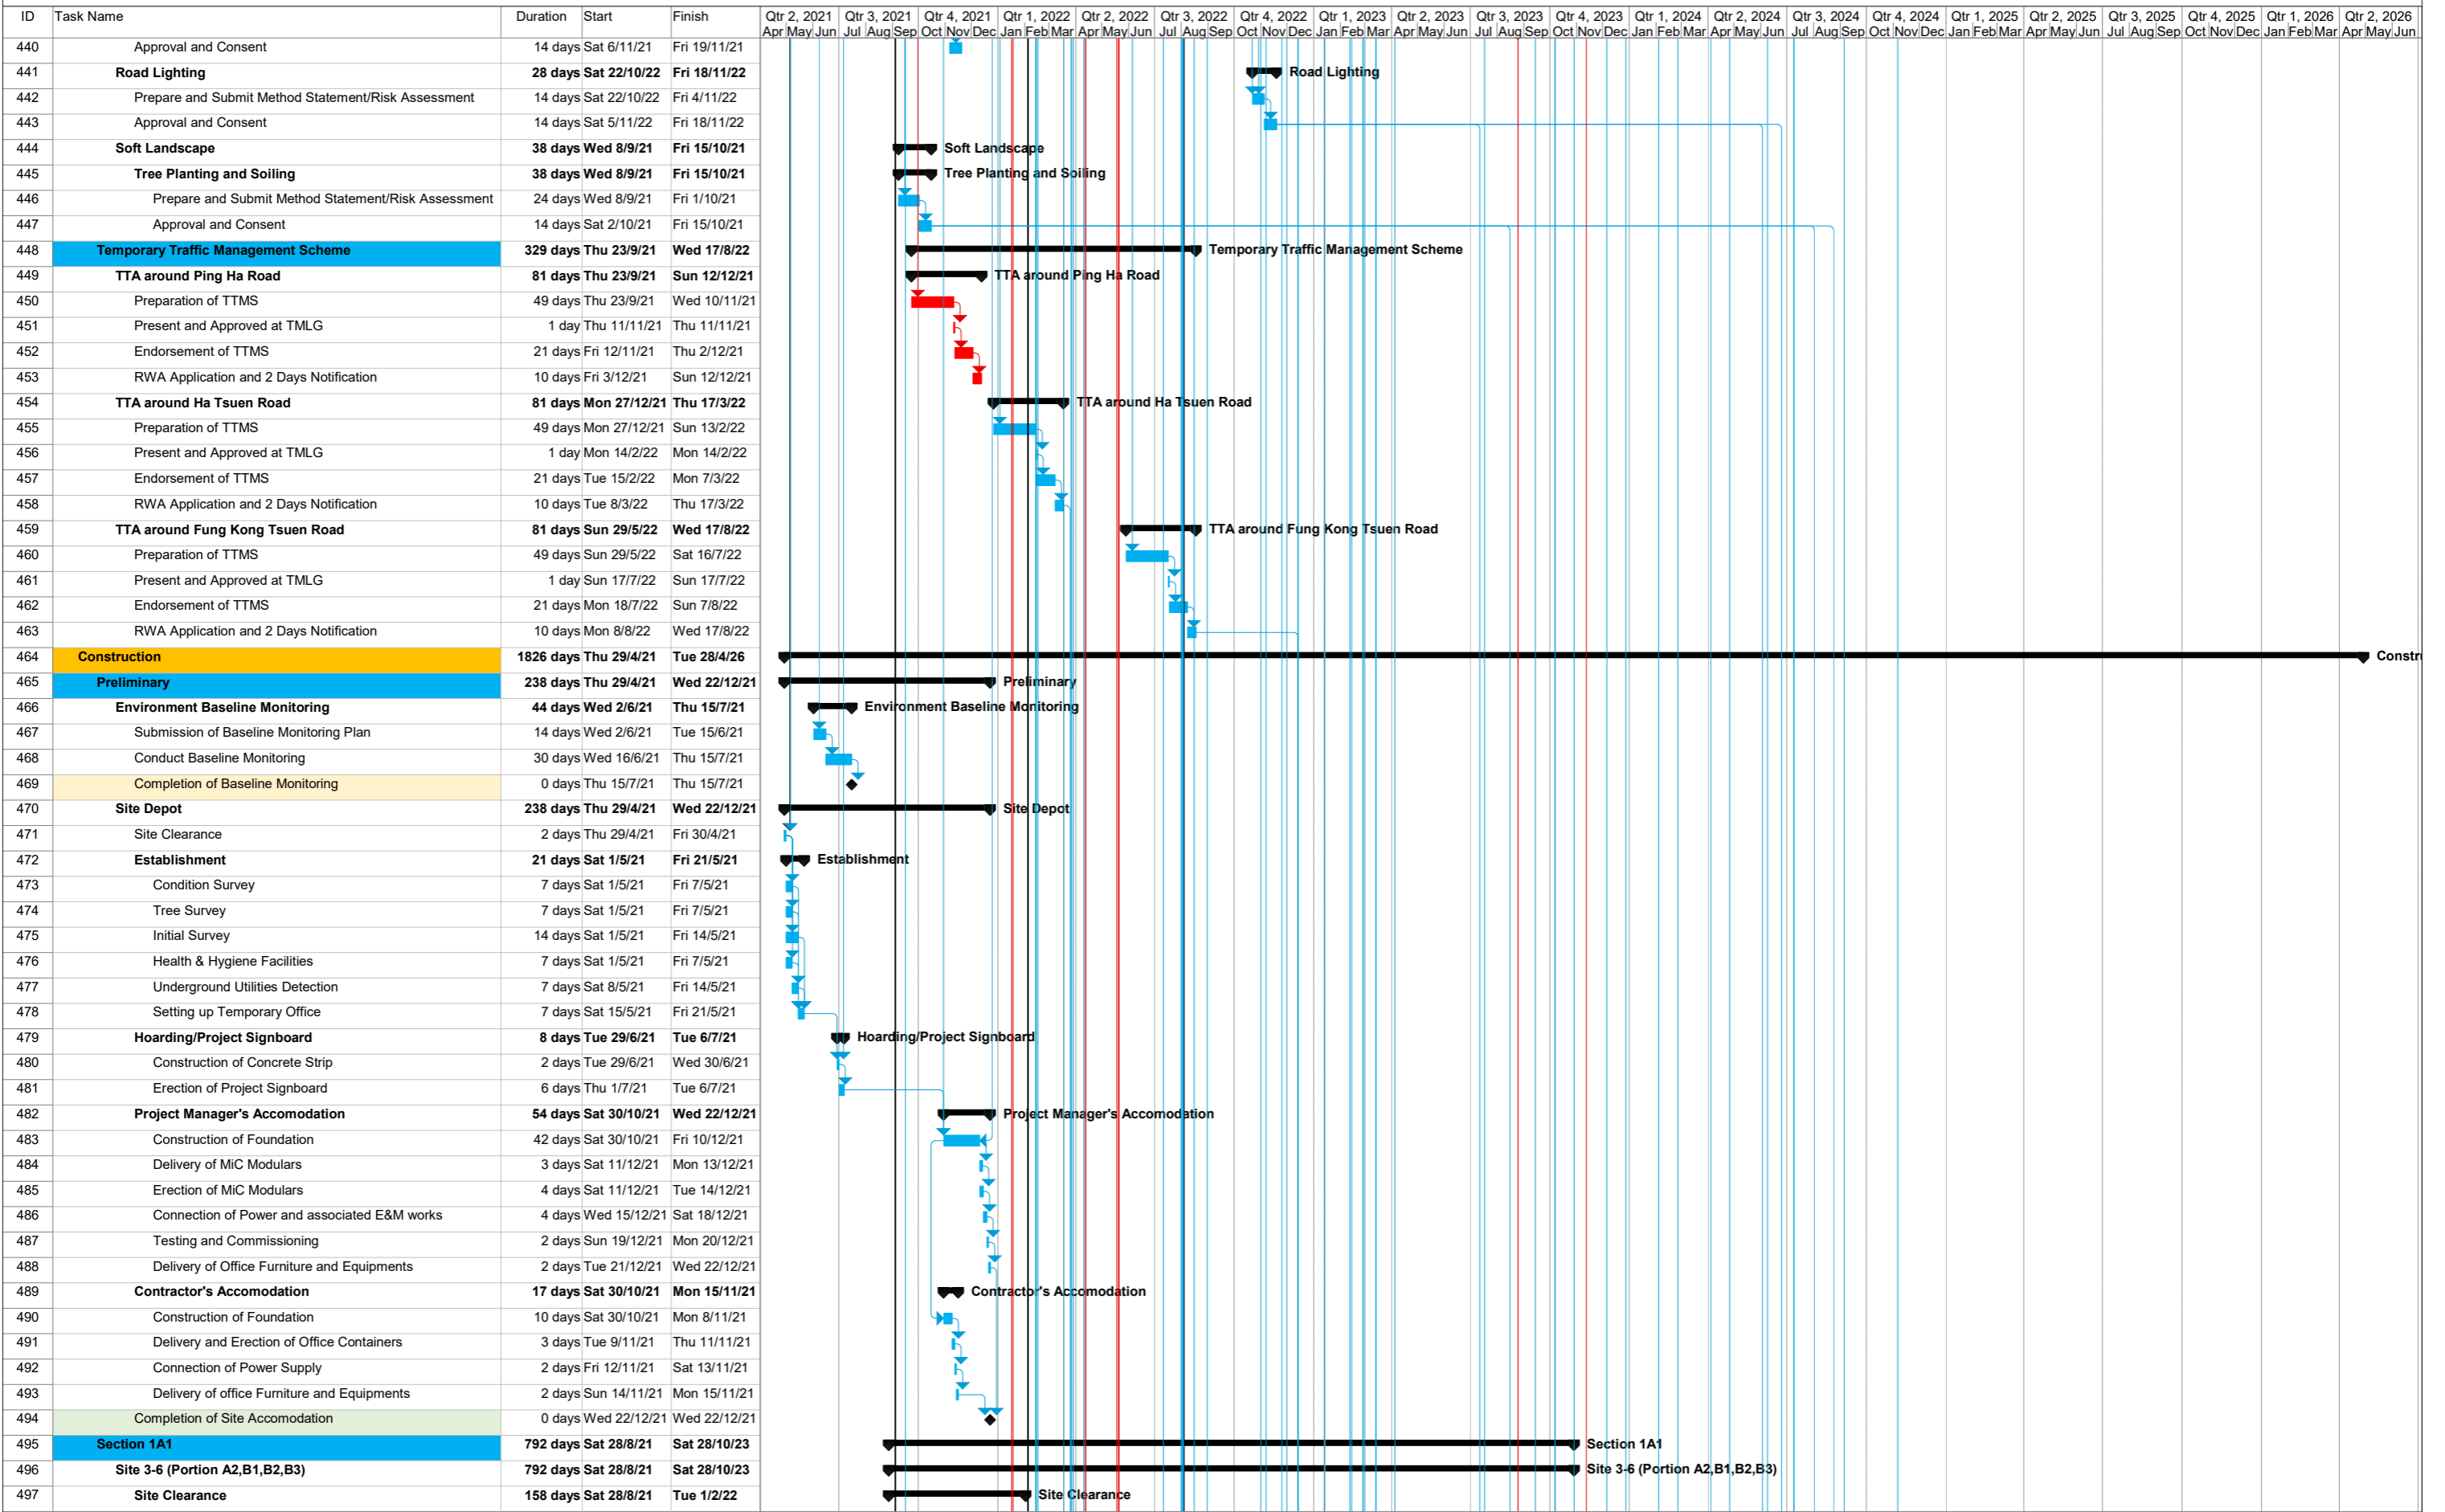


Task █ Critical Task █ Milestone ◆ Summary ▬

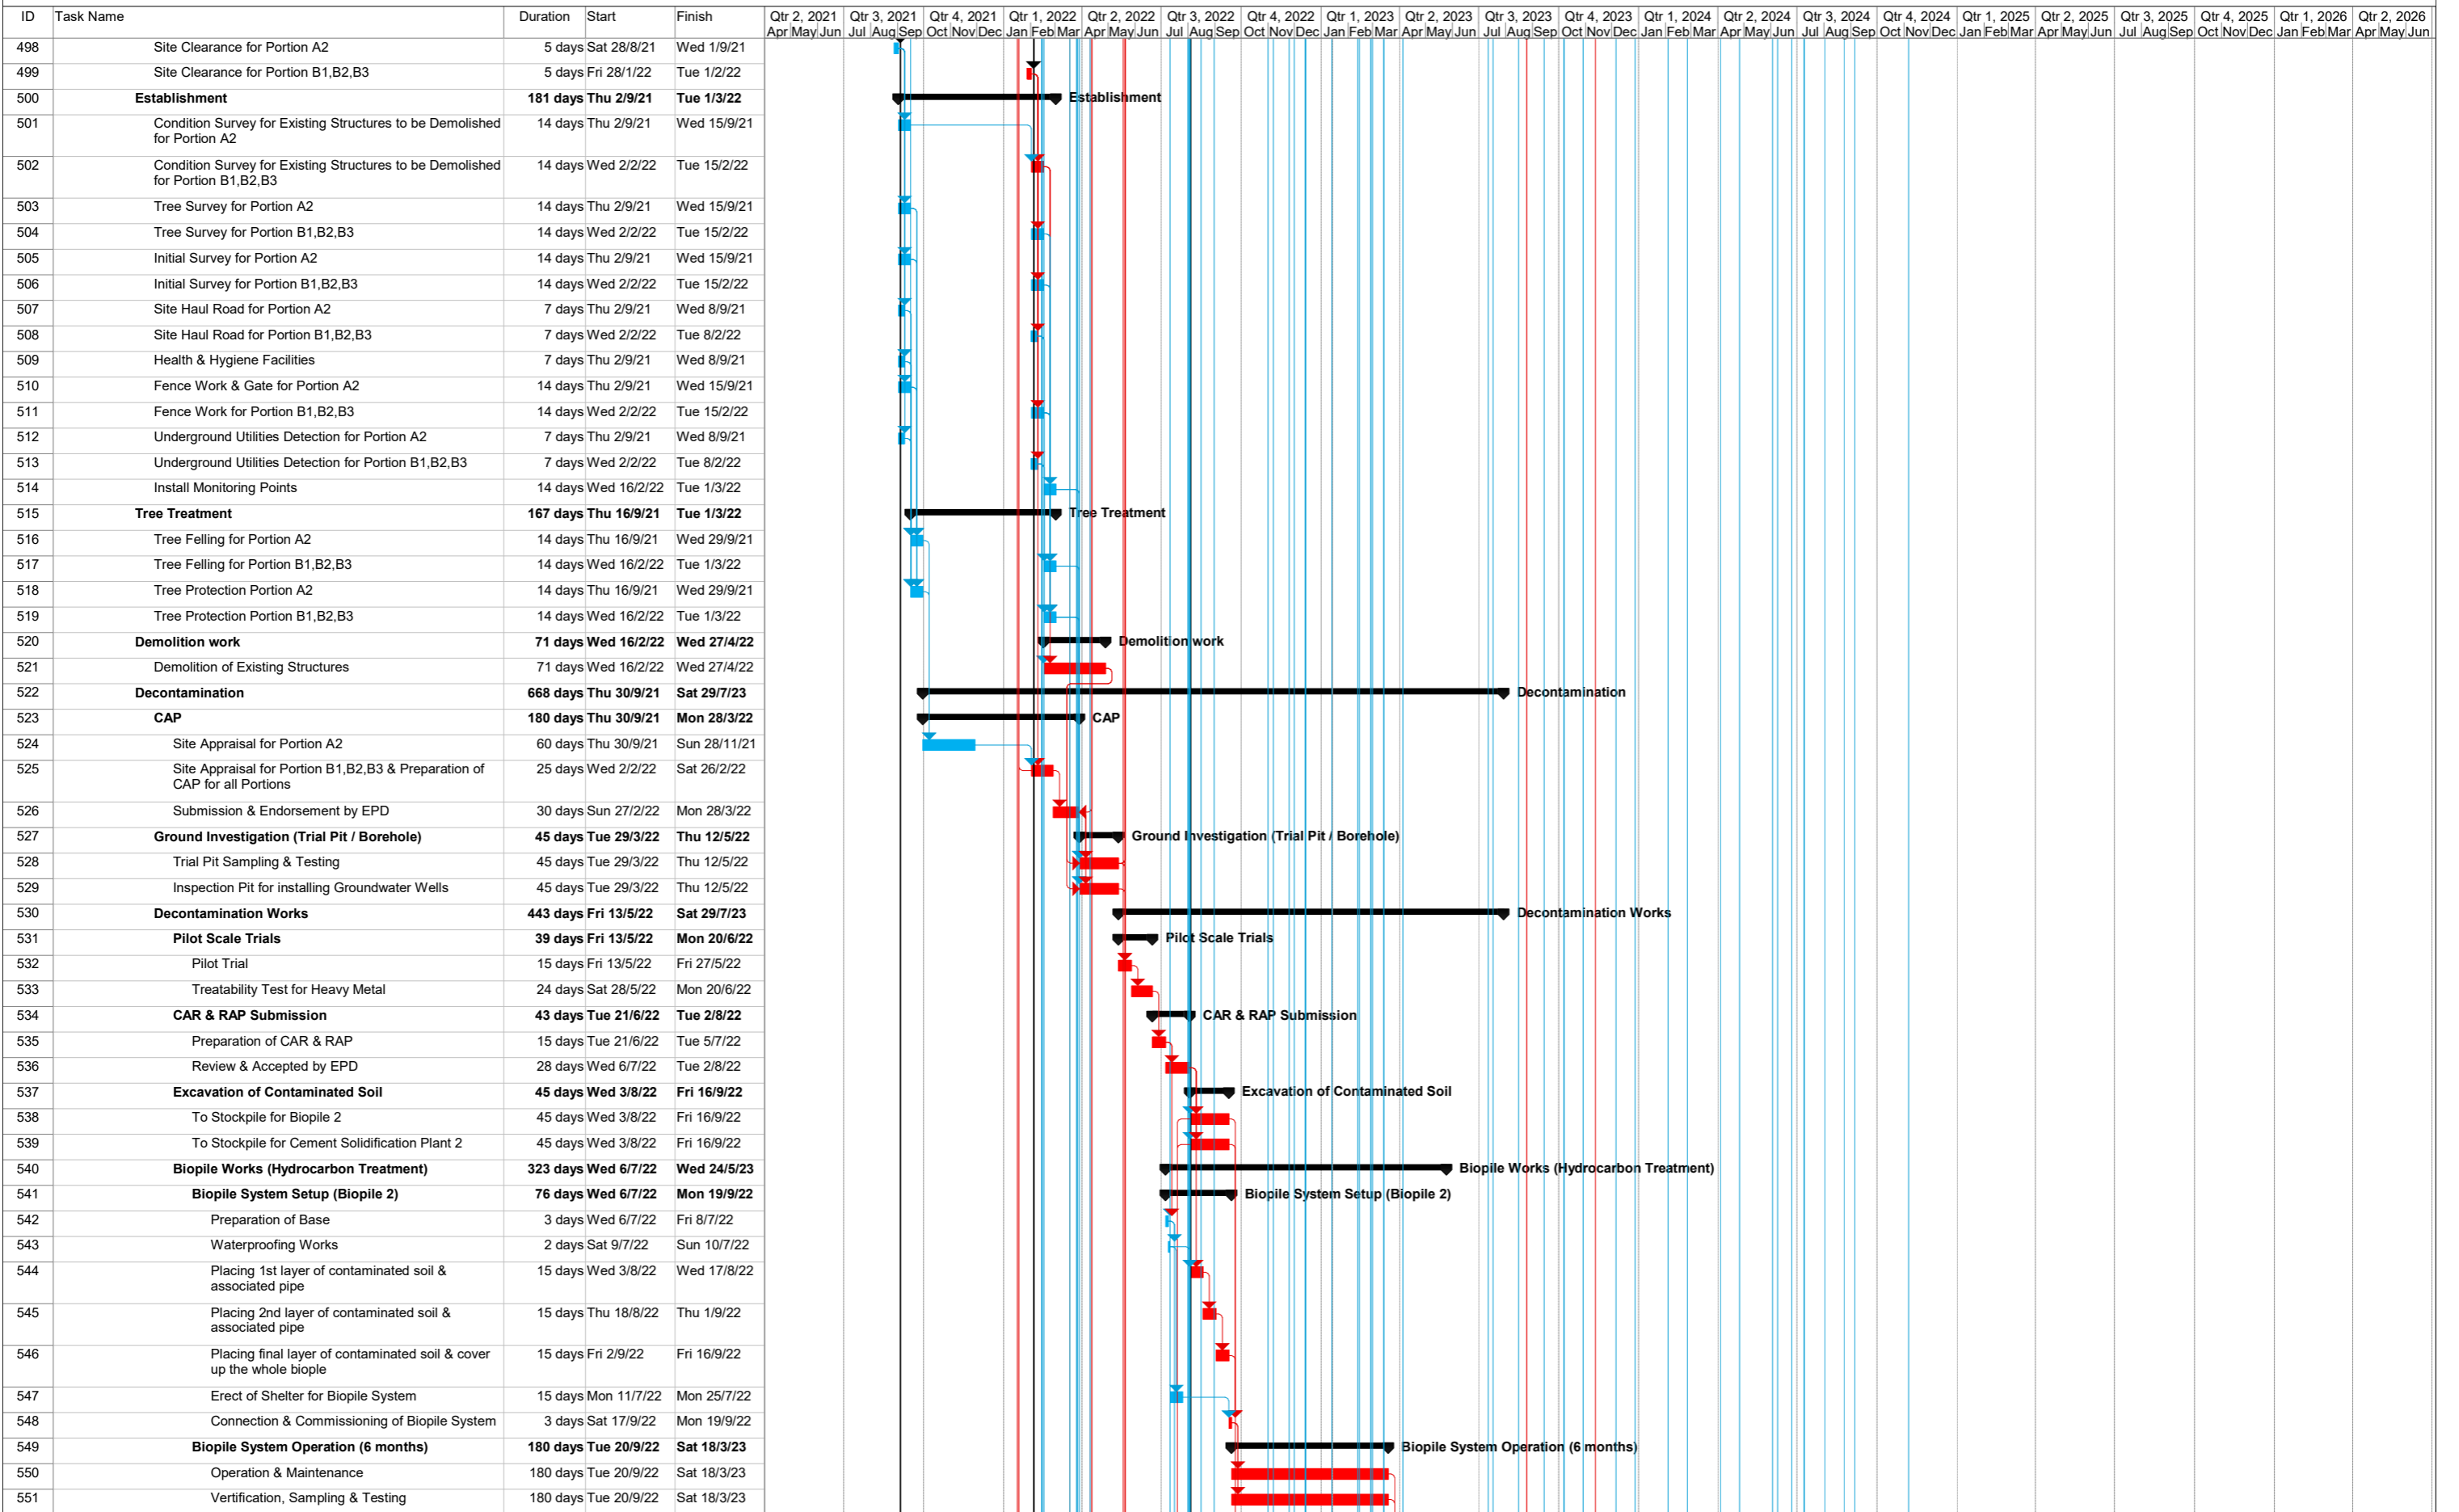


Task ■ Critical Task ■ Milestone ◆ Summary ▬

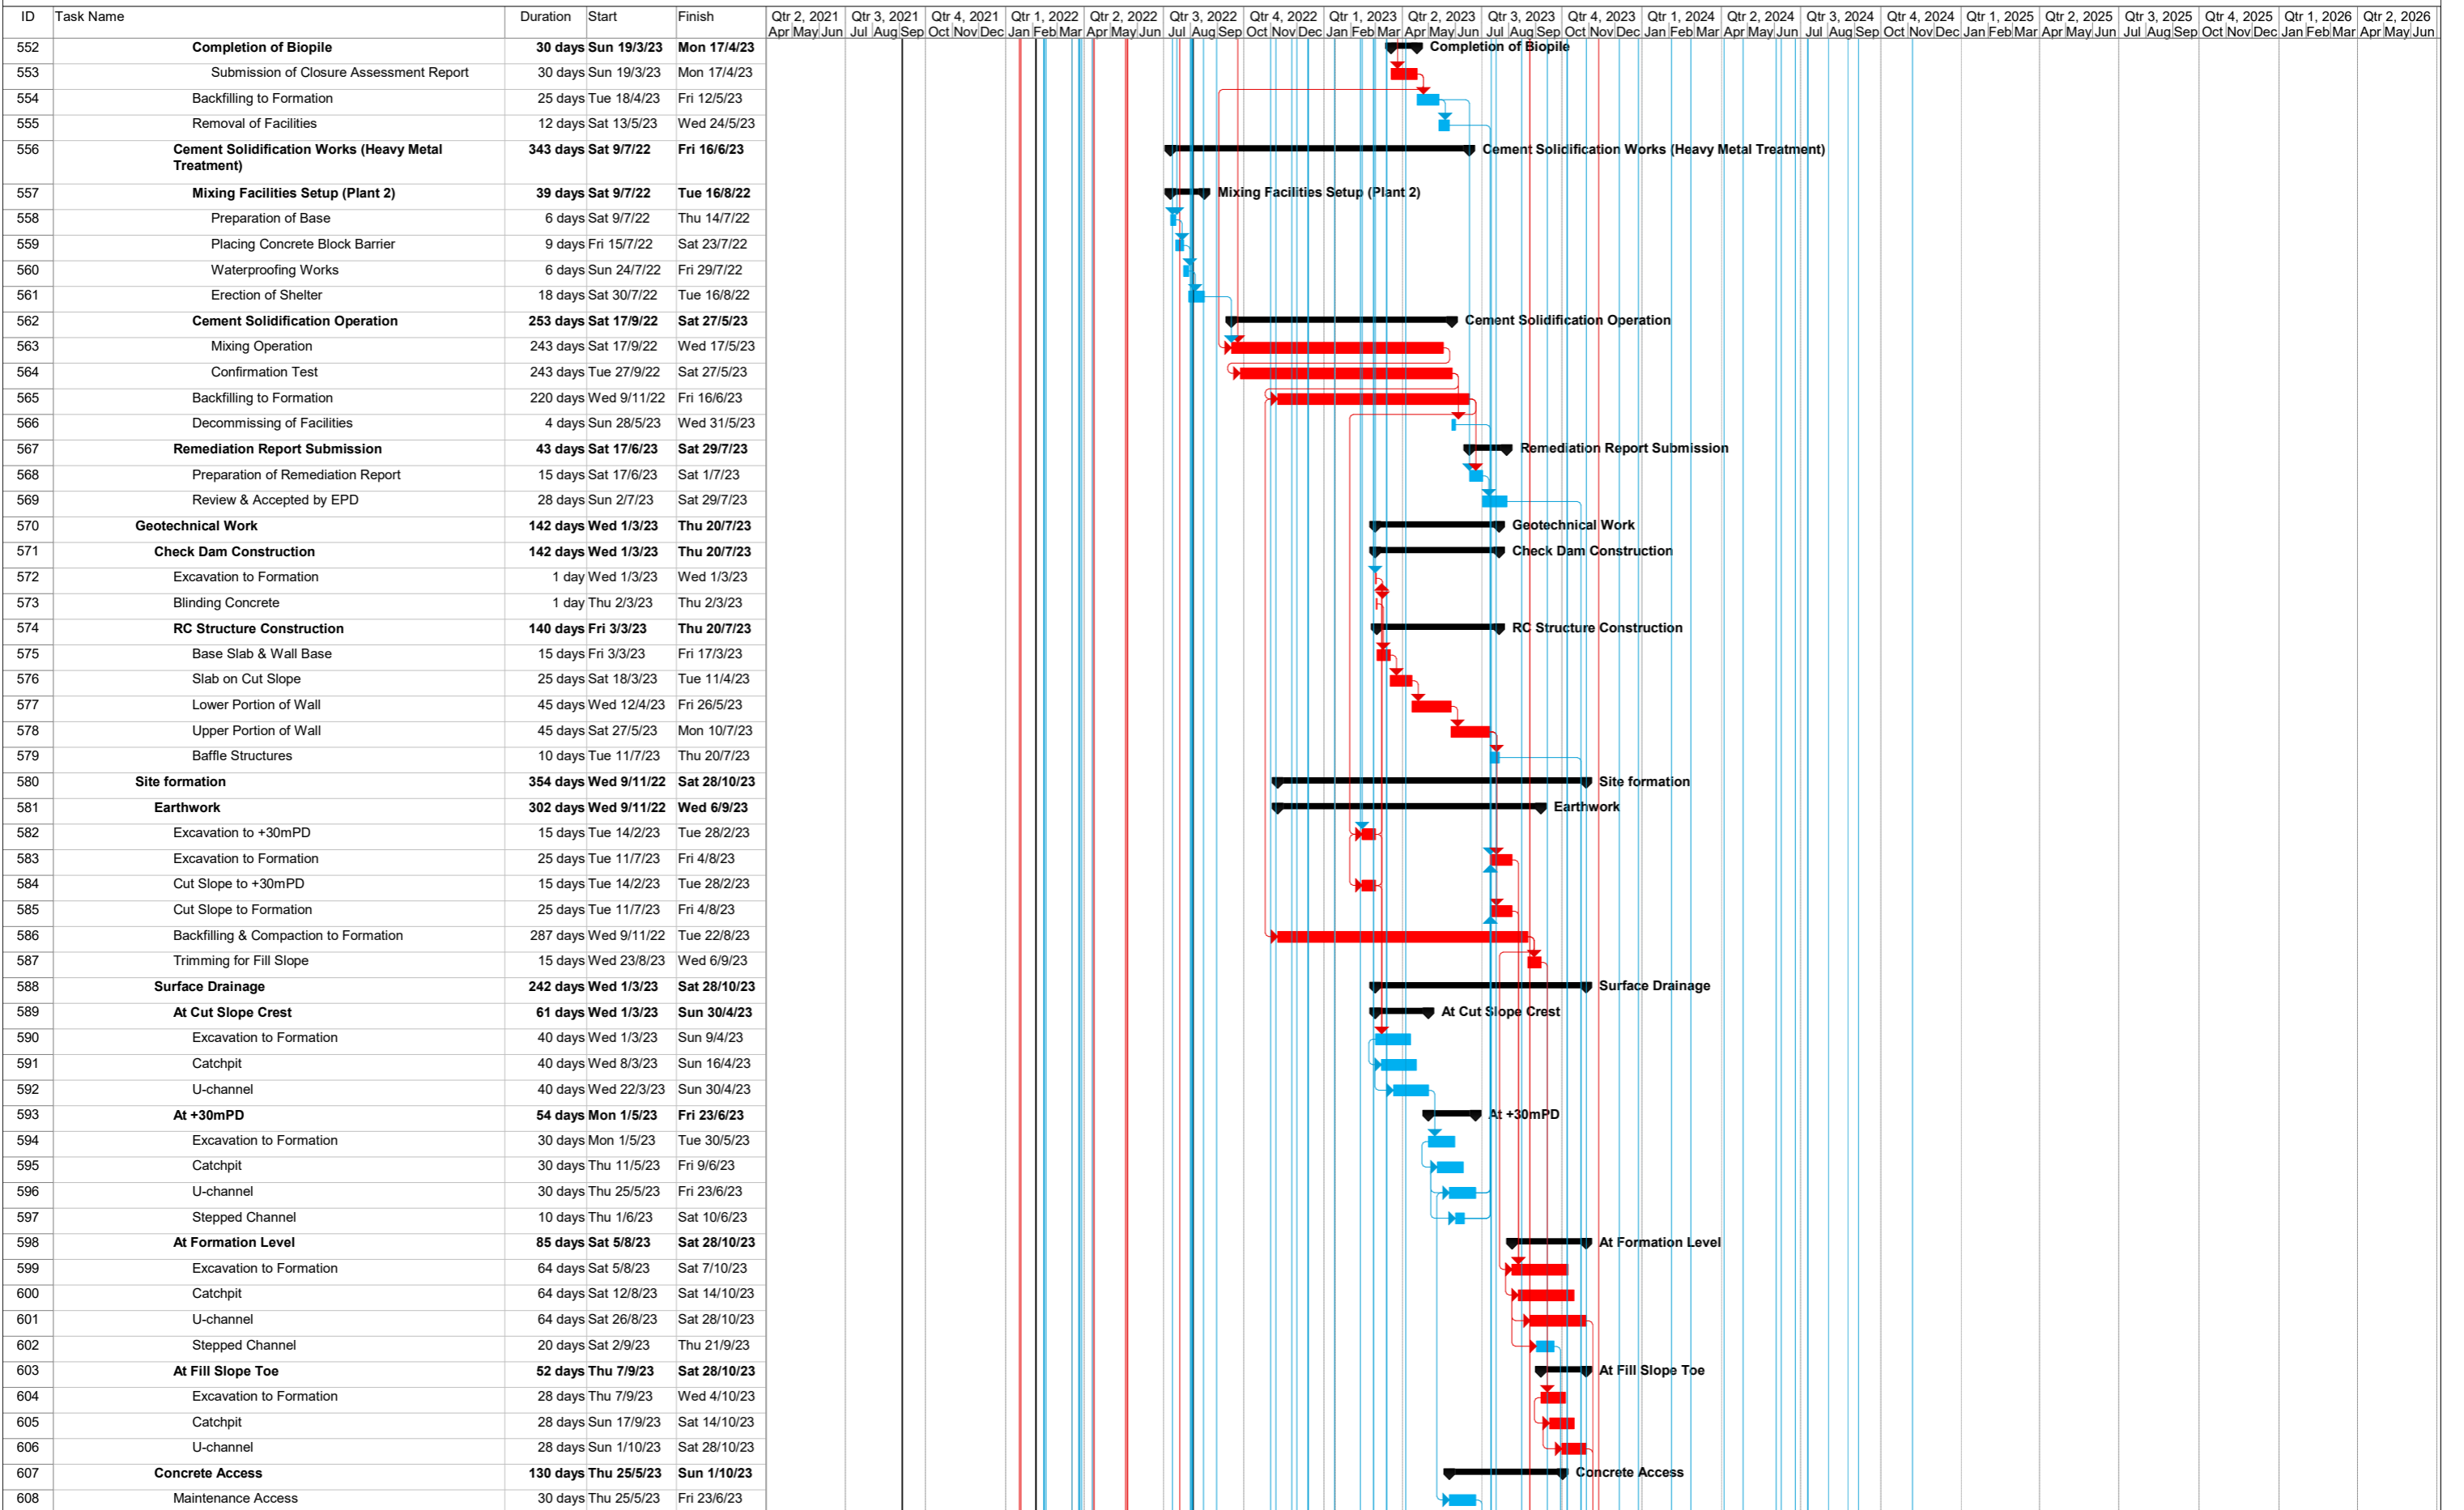


Task █ Critical Task █ Milestone ◆ Summary ▬

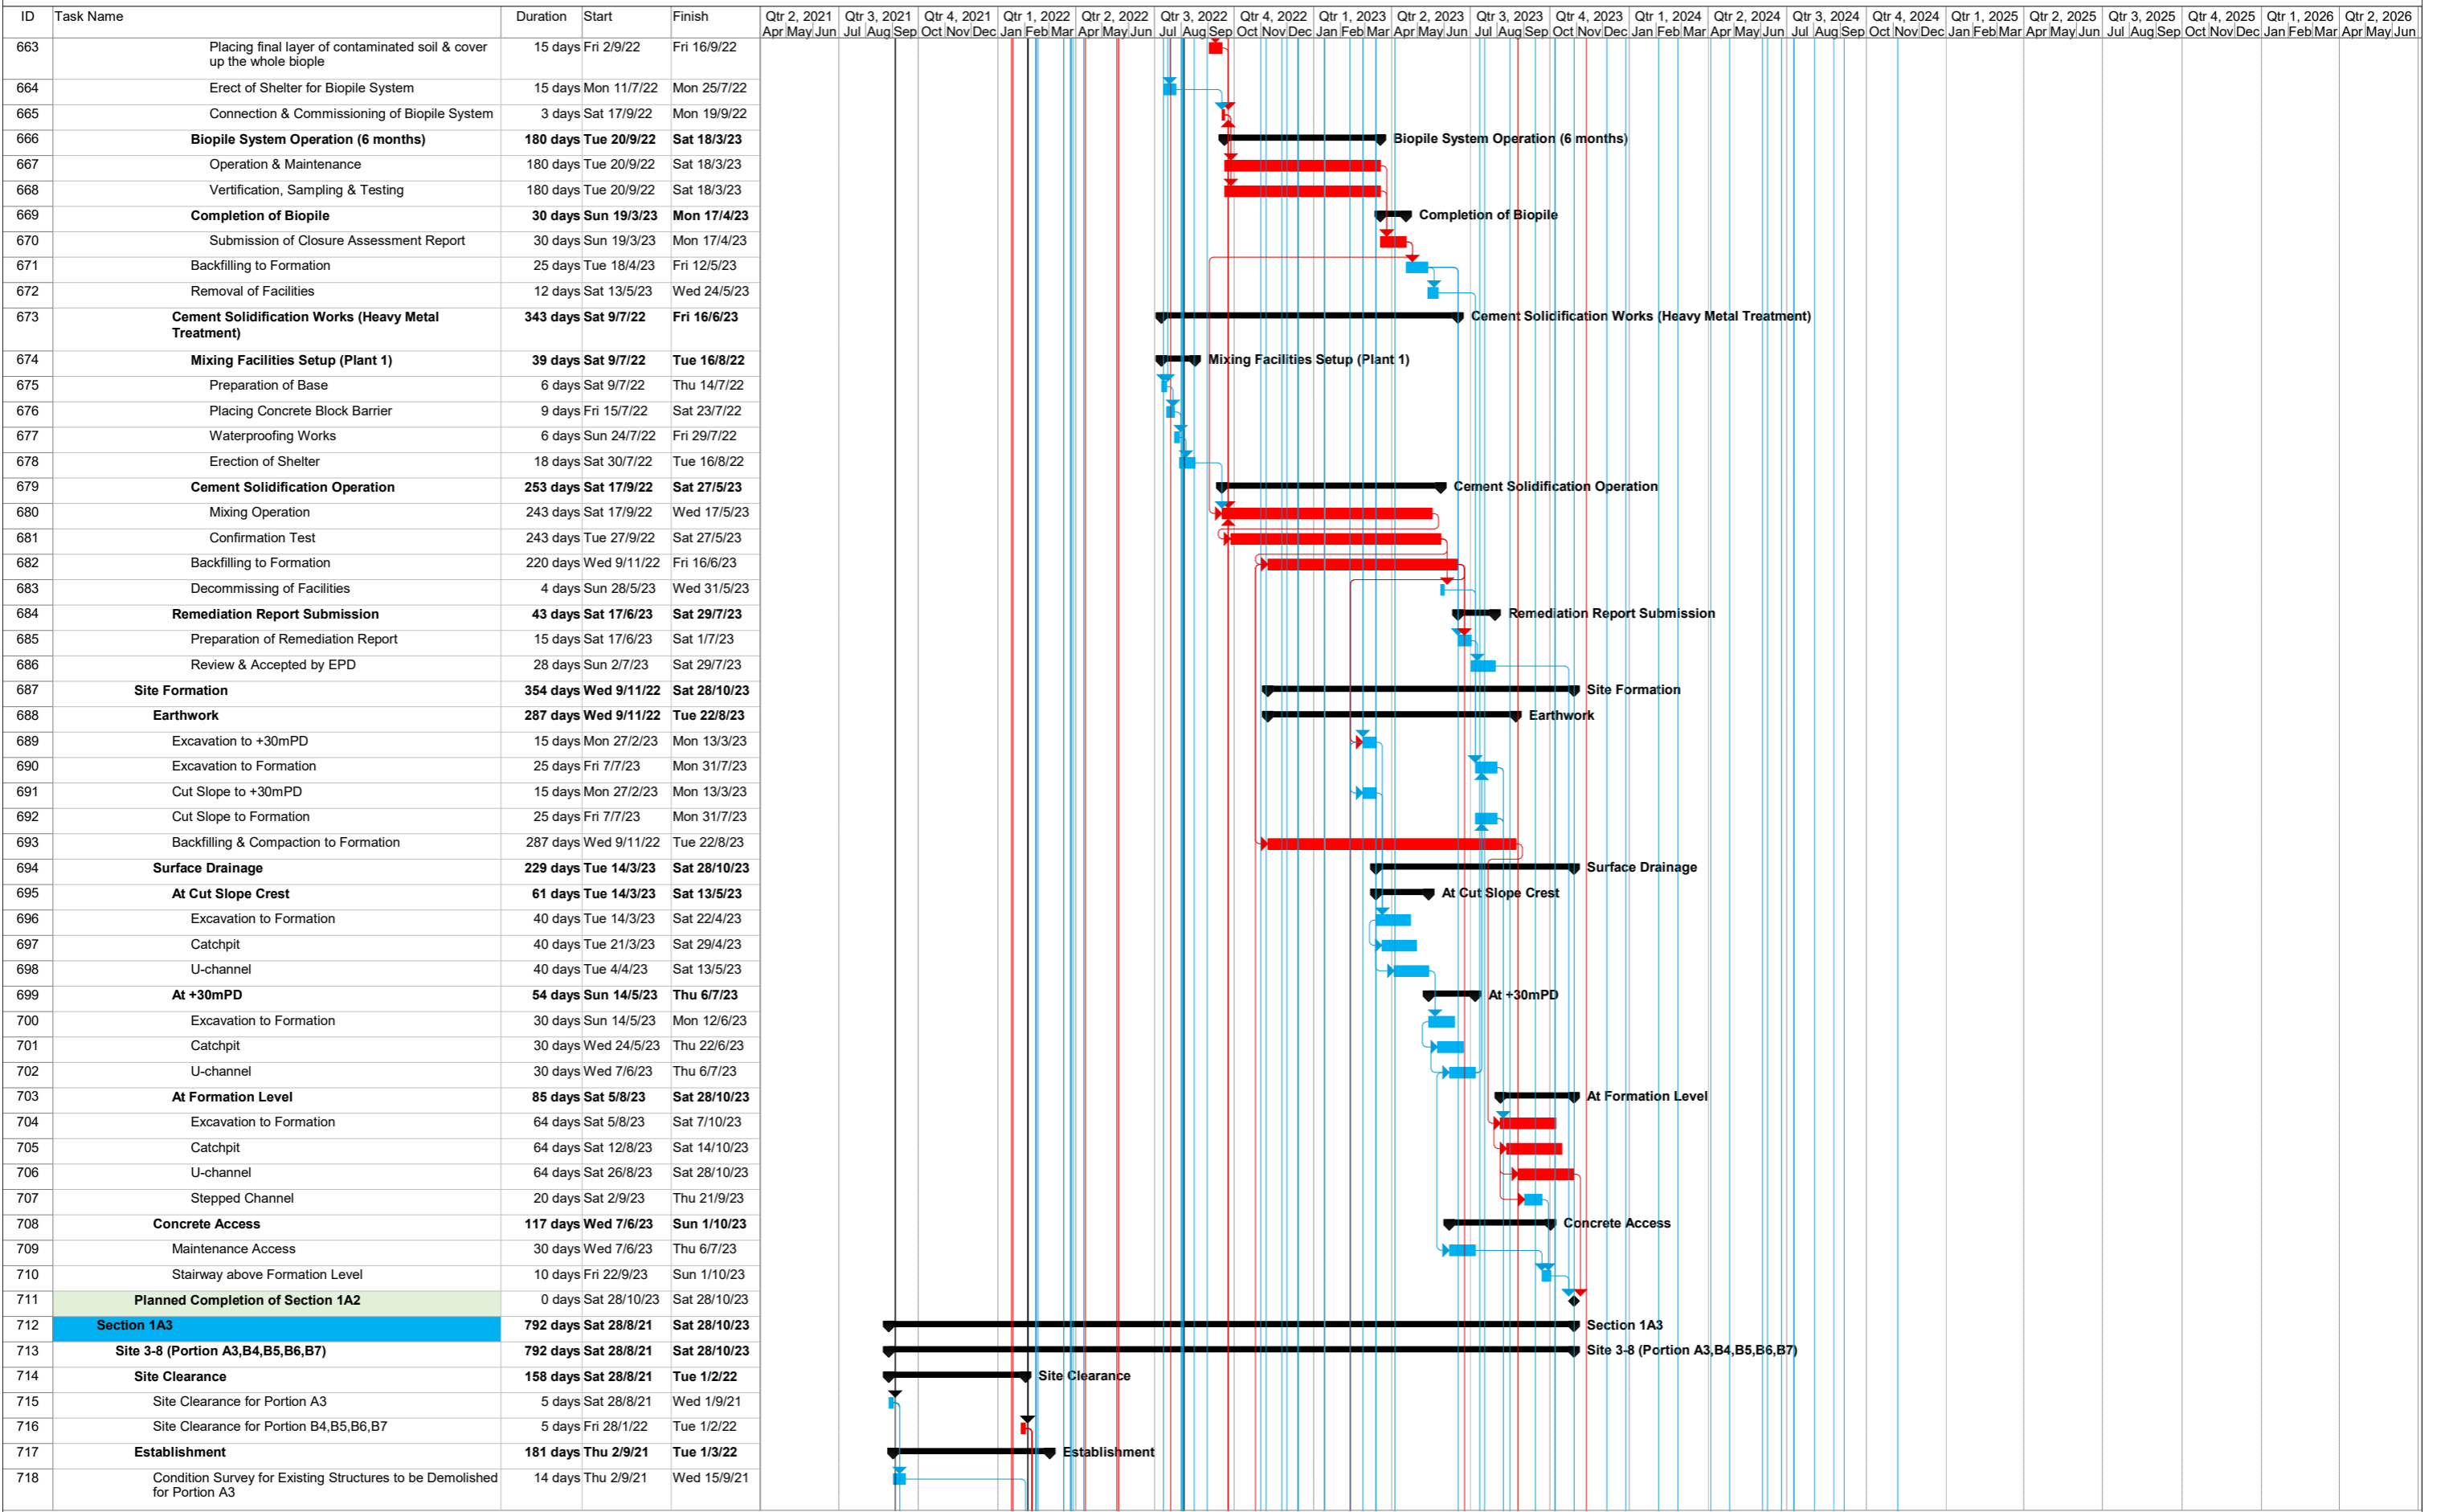

Task ■ Critical Task ■ Milestone ◆ Summary ▬

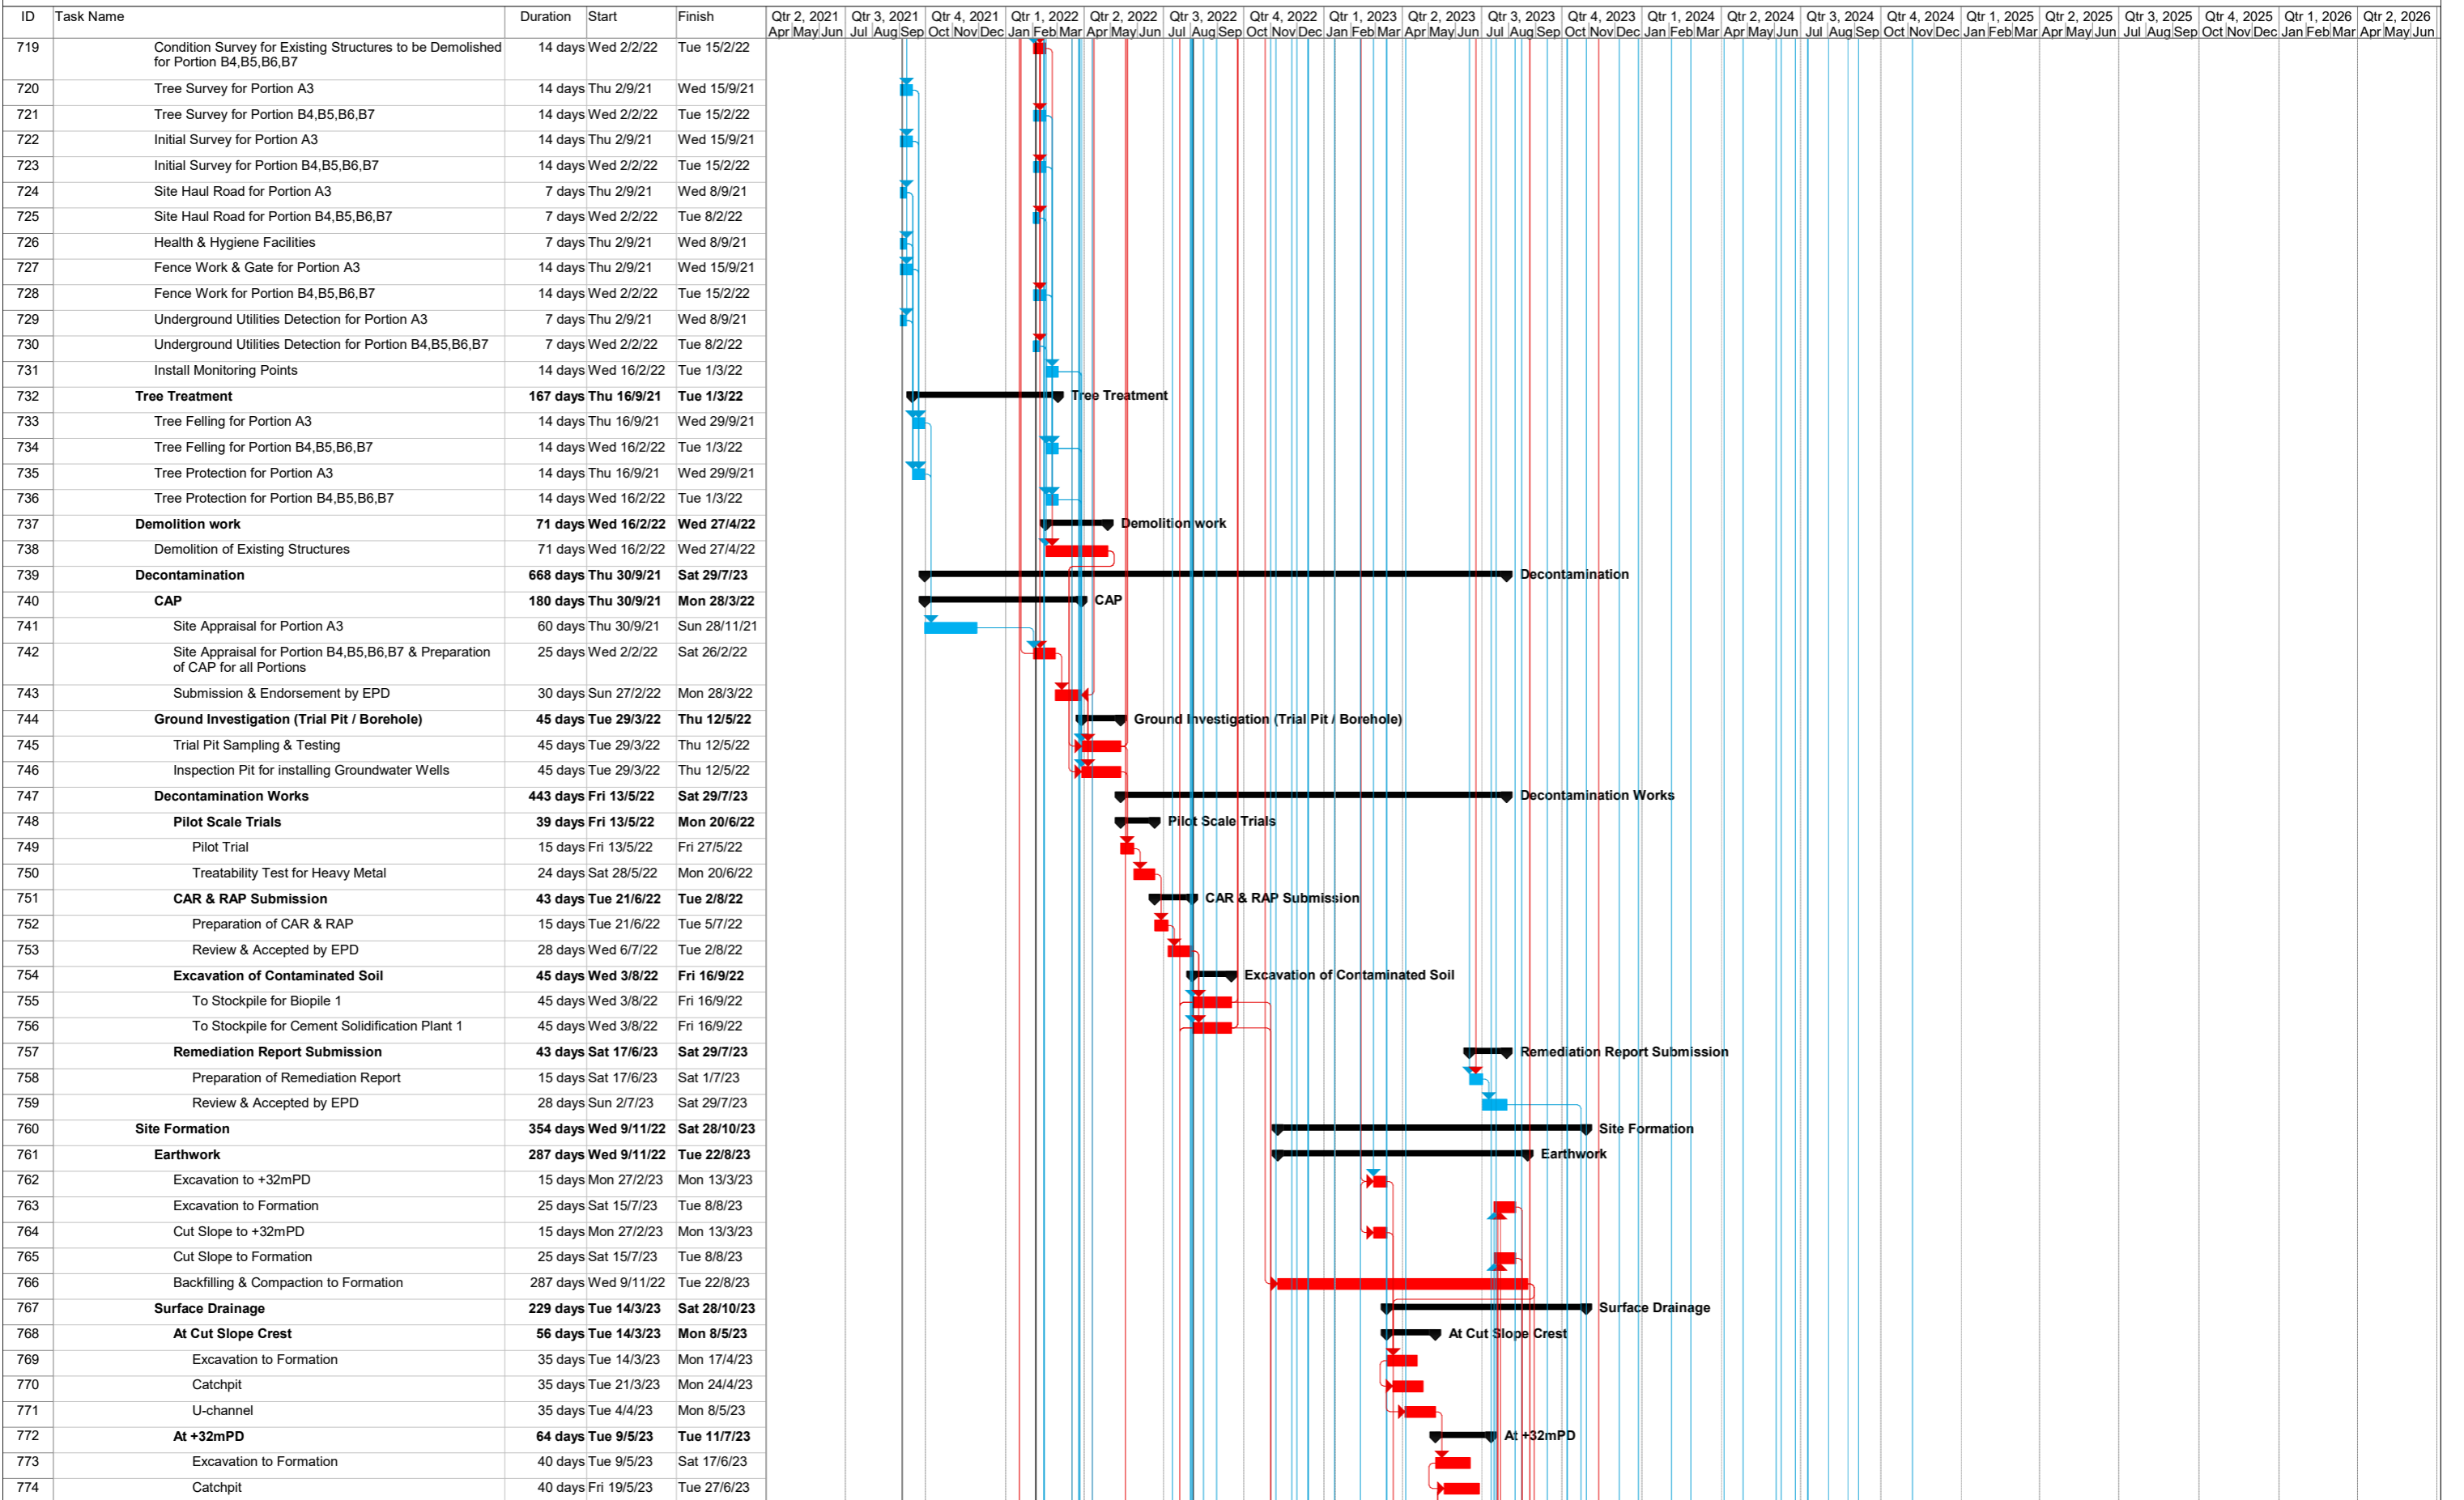


Task █ Critical Task █ Milestone ◆ Summary ▬

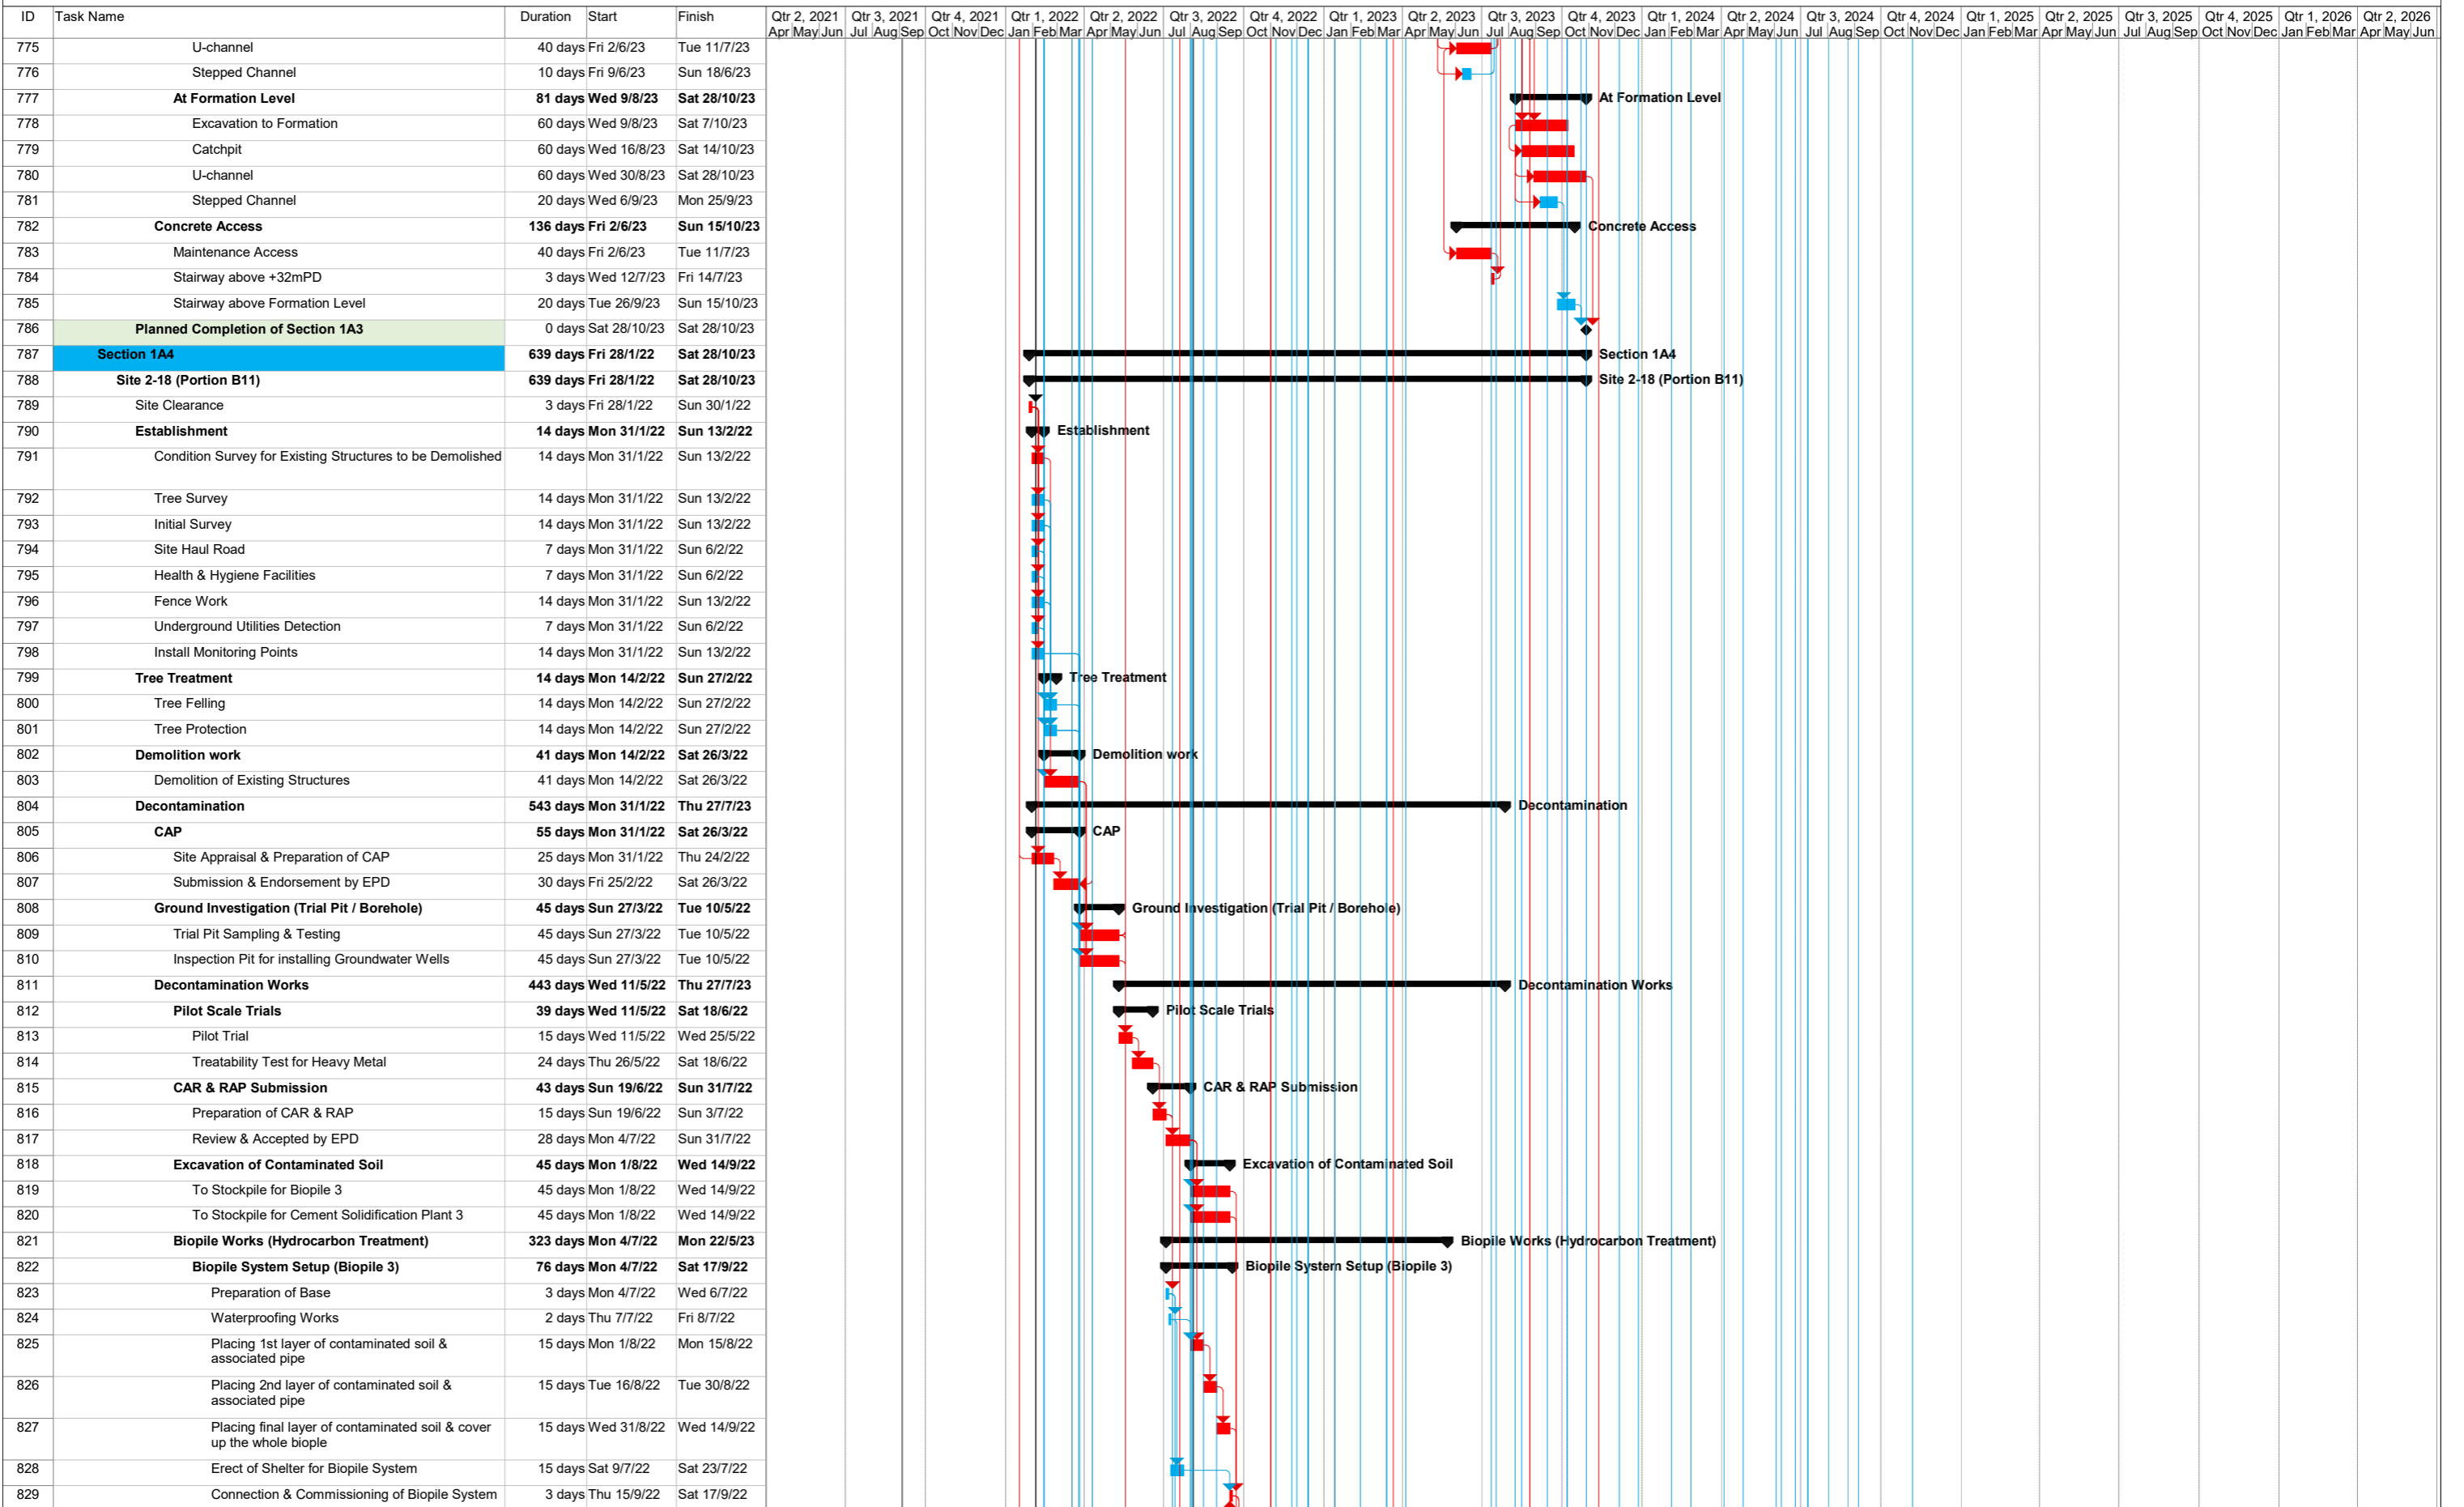

Task █ Critical Task █ Milestone ◆ Summary ▬

Hung Shui Kiu/Ha Tsuen New Development Area Stage 1 Works - Site Formation and Engineering Infrastructure

ID	Task Name	Duration	Start	Finish	Qtr 2, 2021 Apr May Jun	Qtr 3, 2021 Jul Aug Sep	Qtr 4, 2021 Oct Nov Dec	Qtr 1, 2022 Jan Feb Mar	Qtr 2, 2022 Apr May Jun	Qtr 3, 2022 Jul Aug Sep	Qtr 4, 2022 Oct Nov Dec	Qtr 1, 2023 Jan Feb Mar	Qtr 2, 2023 Apr May Jun	Qtr 3, 2023 Jul Aug Sep	Qtr 4, 2023 Oct Nov Dec	Qtr 1, 2024 Jan Feb Mar	Qtr 2, 2024 Apr May Jun	Qtr 3, 2024 Jul Aug Sep	Qtr 4, 2024 Oct Nov Dec	Qtr 1, 2025 Jan Feb Mar	Qtr 2, 2025 Apr May Jun	Qtr 3, 2025 Jul Aug Sep	Qtr 4, 2025 Oct Nov Dec	Qtr 1, 2026 Jan Feb Mar	Qtr 2, 2026 Apr May Jun
830	Biopile System Operation (6 months)	180 days	Sun 18/9/22	Thu 16/3/23																					
831	Operation & Maintenance	180 days	Sun 18/9/22	Thu 16/3/23																					
832	Verification, Sampling & Testing	180 days	Sun 18/9/22	Thu 16/3/23																					
833	Completion of Biopile	30 days	Fri 17/3/23	Sat 15/4/23																					
834	Submission of Closure Assessment Report	30 days	Fri 17/3/23	Sat 15/4/23																					
835	Backfilling to Formation	25 days	Sun 16/4/23	Wed 10/5/23																					
836	Removal of Facilities	12 days	Thu 11/5/23	Mon 22/5/23																					
837	Cement Solidification Works (Heavy Metal Treatment)	343 days	Thu 7/7/22	Wed 14/6/23																					
838	Mixing Facilities Setup (Plant 3)	39 days	Thu 7/7/22	Sun 14/8/22																					
839	Preparation of Base	6 days	Thu 7/7/22	Tue 12/7/22																					
840	Placing Concrete Block Barrier	9 days	Wed 13/7/22	Thu 21/7/22																					
841	Waterproofing Works	6 days	Fri 22/7/22	Wed 27/7/22																					
842	Erection of Shelter	18 days	Thu 28/7/22	Sun 14/8/22																					
843	Cement Solidification Operation	253 days	Thu 15/9/22	Thu 25/5/23																					
844	Mixing Operation	243 days	Thu 15/9/22	Mon 15/5/23																					
845	Confirmation Test	243 days	Sun 25/9/22	Thu 25/5/23																					
846	Backfilling to Formation	220 days	Mon 7/11/22	Wed 14/6/23																					
847	Decommissioning of Facilities	4 days	Fri 26/5/23	Mon 29/5/23																					
848	Remediation Report Submission	43 days	Thu 15/6/23	Thu 27/7/23																					
849	Preparation of Remediation Report	15 days	Thu 15/6/23	Thu 29/6/23																					
850	Review & Accepted by EPD	28 days	Fri 30/6/23	Thu 27/7/23																					
851	Site formation	356 days	Mon 7/11/22	Sat 28/10/23																					
852	Earthwork	305 days	Mon 7/11/22	Thu 7/9/23																					
853	Backfilling & Compaction to Formation	290 days	Mon 7/11/22	Wed 23/8/23																					
854	Trimming for Fill Slope	15 days	Thu 24/8/23	Thu 7/9/23																					
855	Surface Drainage	51 days	Fri 8/9/23	Sat 28/10/23																					
856	At Formation Level	51 days	Fri 8/9/23	Sat 28/10/23																					
857	Excavation to Formation	30 days	Fri 8/9/23	Sat 7/10/23																					
858	Catchpit	30 days	Fri 15/9/23	Sat 14/10/23																					
859	U-channel	30 days	Fri 29/9/23	Sat 28/10/23																					
860	Planned Completion of Section 1A4	0 days	Sat 28/10/23	Sat 28/10/23																					
861	Section 1A5	792 days	Sat 28/8/21	Sat 28/10/23																					
862	Site 2-19 (Portion A5,B10)	792 days	Sat 28/8/21	Sat 28/10/23																					
863	Site Clearance	156 days	Sat 28/8/21	Sun 30/1/22																					
864	Site Clearance for Portion A5	3 days	Sat 28/8/21	Mon 30/8/21																					
865	Site Clearance for Portion B10	3 days	Fri 28/1/22	Sun 30/1/22																					
866	Establishment	181 days	Tue 31/8/21	Sun 27/2/22																					
867	Condition Survey for Existing Structures to be Demolished for Portion A5	14 days	Tue 31/8/21	Mon 13/9/21																					
868	Condition Survey for Existing Structures to be Demolished for Portion B10	14 days	Mon 31/1/22	Sun 13/2/22																					
869	Tree Survey for Portion A5	14 days	Tue 31/8/21	Mon 13/9/21																					
870	Tree Survey for Portion B10	14 days	Mon 31/1/22	Sun 13/2/22																					
871	Initial Survey for Portion A5	14 days	Tue 31/8/21	Mon 13/9/21																					
872	Initial Survey for Portion B10	14 days	Mon 31/1/22	Sun 13/2/22																					
873	Site Haul Road for Portion A5	7 days	Tue 31/8/21	Mon 6/9/21																					
874	Site Haul Road for Portion B10	7 days	Mon 31/1/22	Sun 6/2/22																					
875	Health & Hygiene Facilities	7 days	Tue 31/8/21	Mon 6/9/21																					
876	Fence Work & Gate for Portion A5	14 days	Tue 31/8/21	Mon 13/9/21																					
877	Fence Work for Portion B10	14 days	Mon 31/1/22	Sun 13/2/22																					
878	Underground Utilities Detection for Portion A5	7 days	Tue 31/8/21	Mon 6/9/21																					
879	Underground Utilities Detection for Portion B10	7 days	Mon 31/1/22	Sun 6/2/22																					
880	Install Monitoring Points	14 days	Mon 14/2/22	Sun 27/2/22																					
881	Tree Treatment	167 days	Tue 14/9/21	Sun 27/2/22																					
882	Tree Felling for Portion A5	14 days	Tue 14/9/21	Mon 27/9/21																					
883	Tree Felling for Portion B10	14 days	Mon 14/2/22	Sun 27/2/22																					
884	Tree Protection for Portion A5	14 days	Tue 14/9/21	Mon 27/9/21																					
885	Tree Protection for Portion B10	14 days	Mon 14/2/22	Sun 27/2/22																					

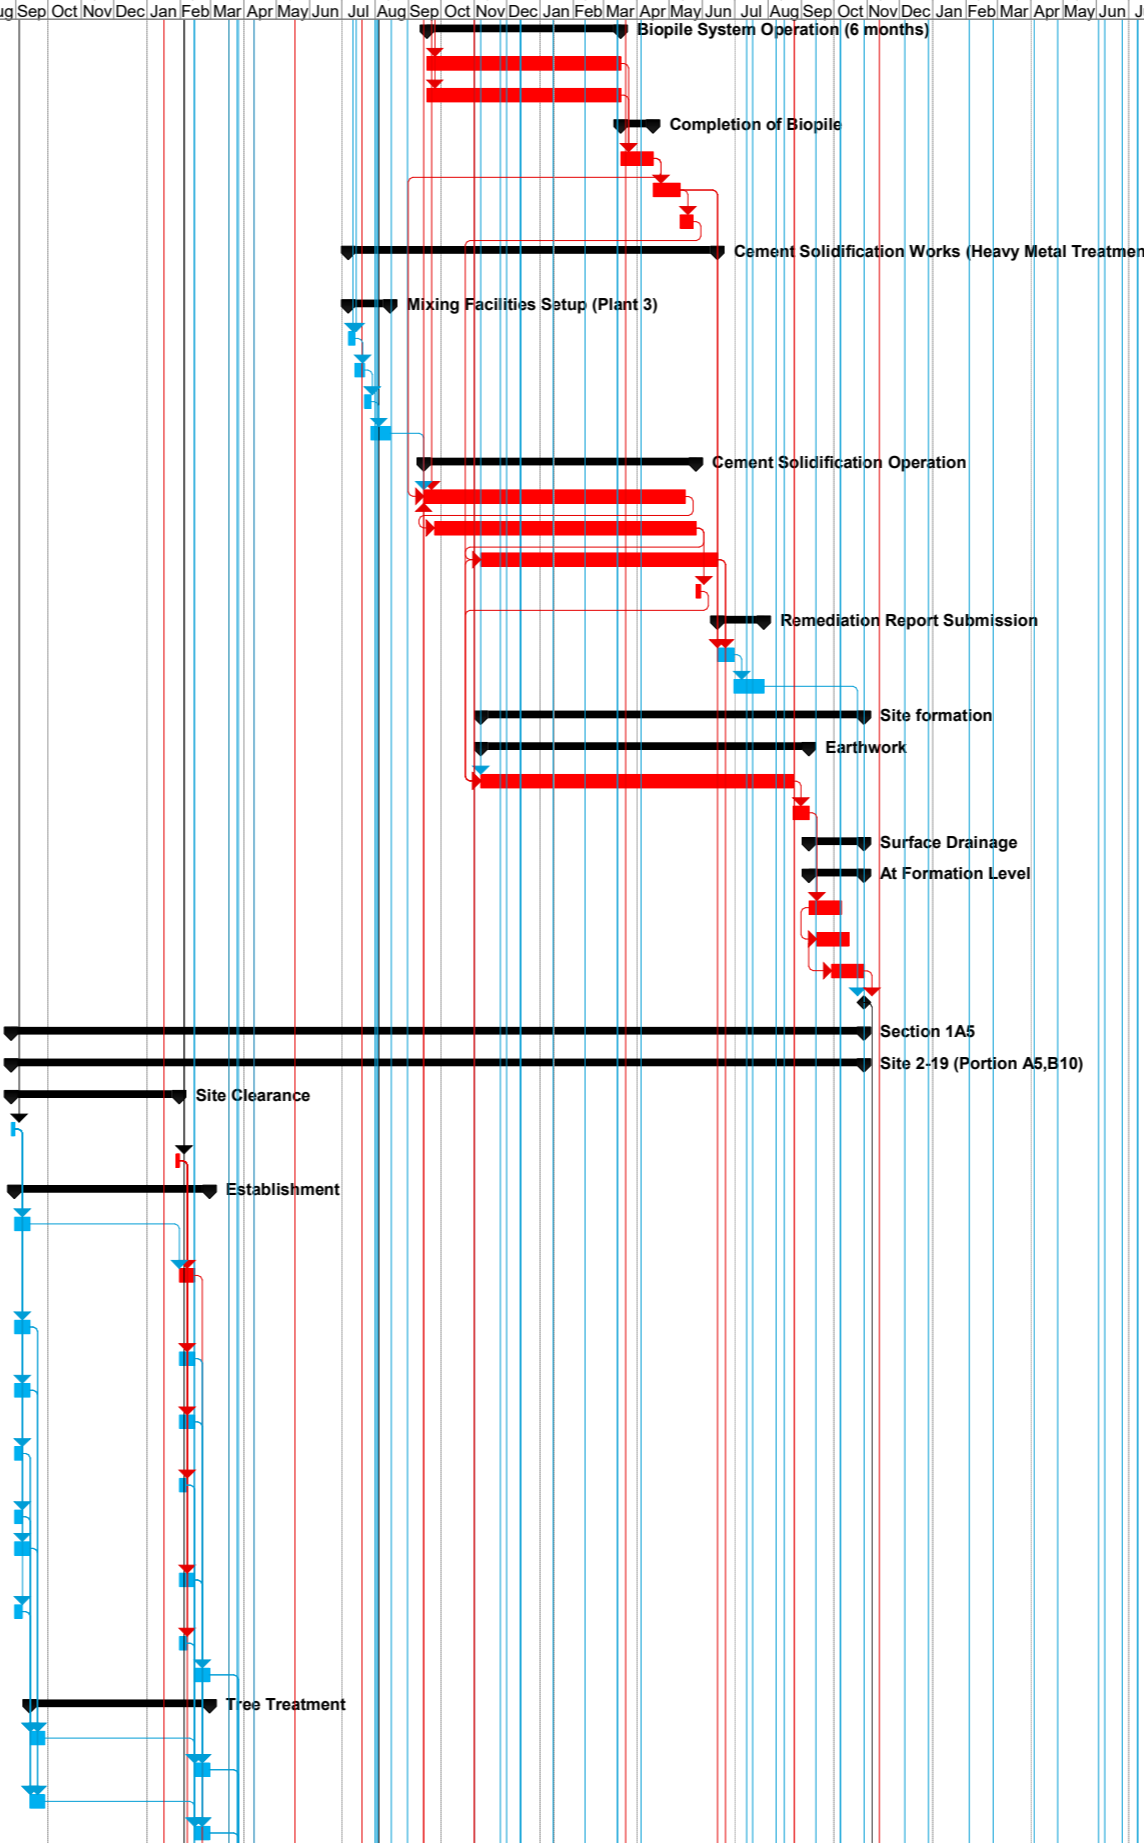


Task █ Critical Task █ Milestone ◆ Summary ▬


*E=Excavator L=Lorry W=Worker D=Drill plant C=Crane Lorry R=Rotter




Task █ Critical Task █ Milestone ◆ Summary ▬

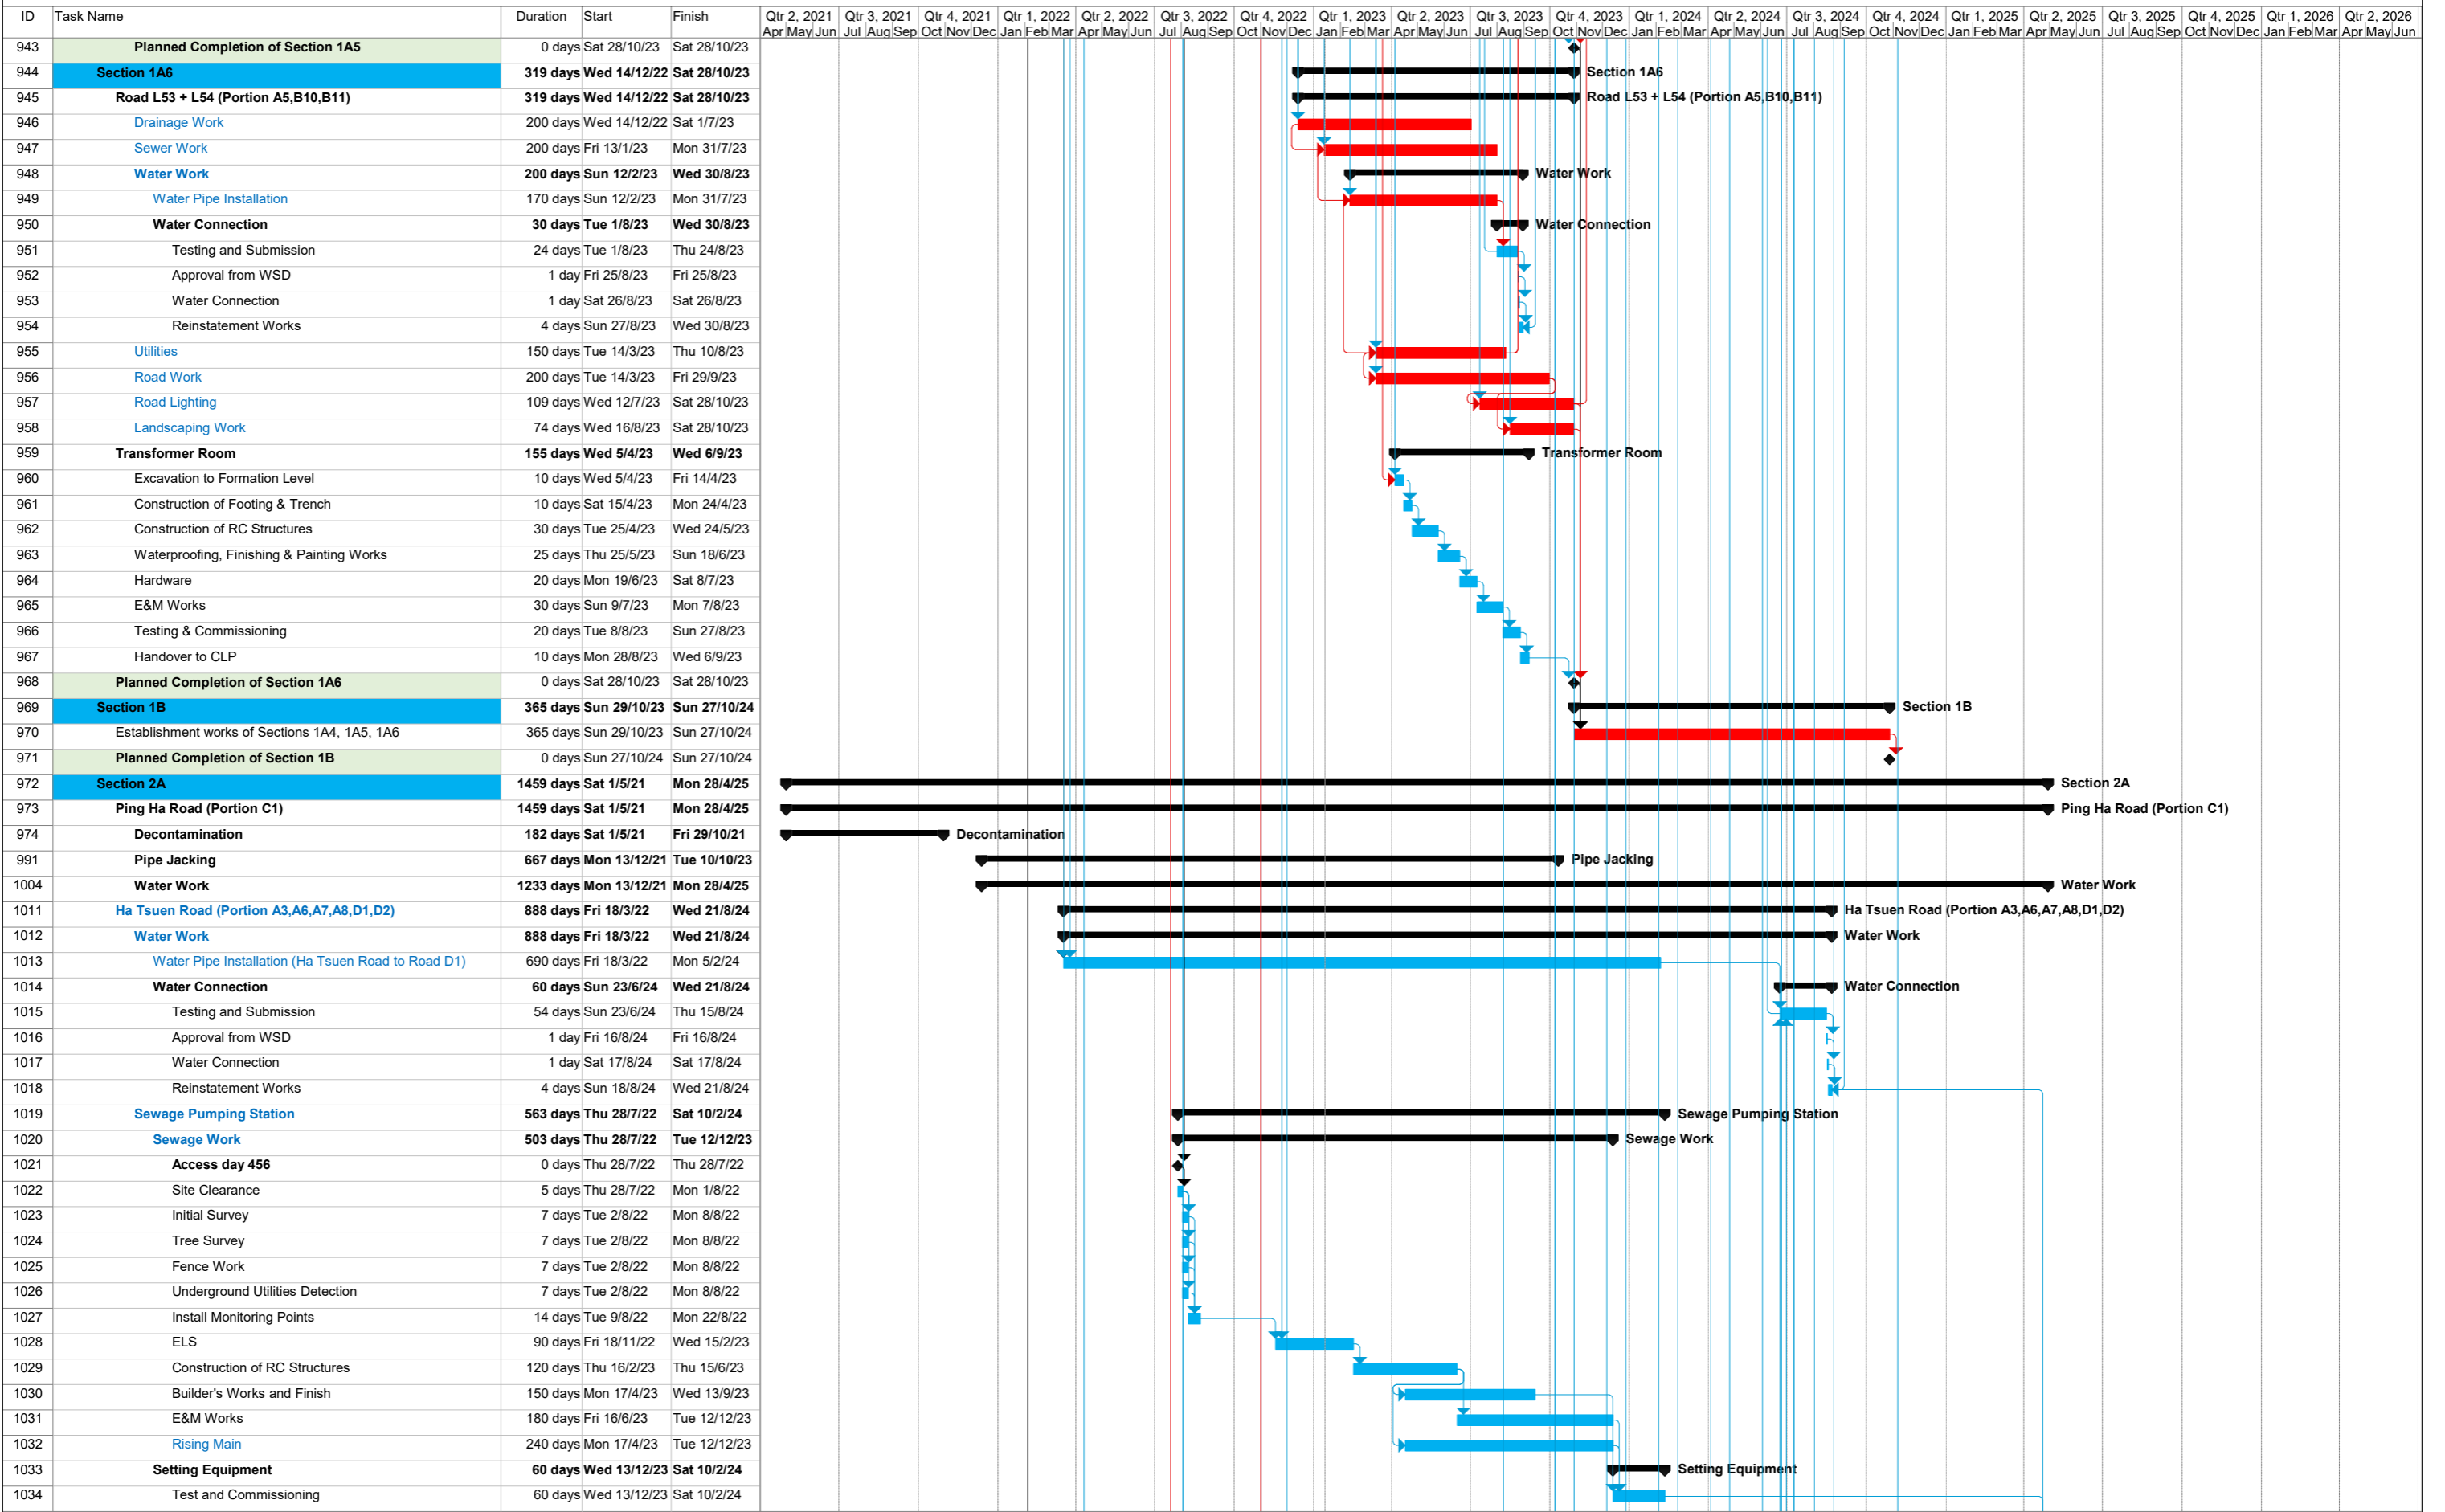

Task █ Critical Task █ Milestone ◆ Summary ▬

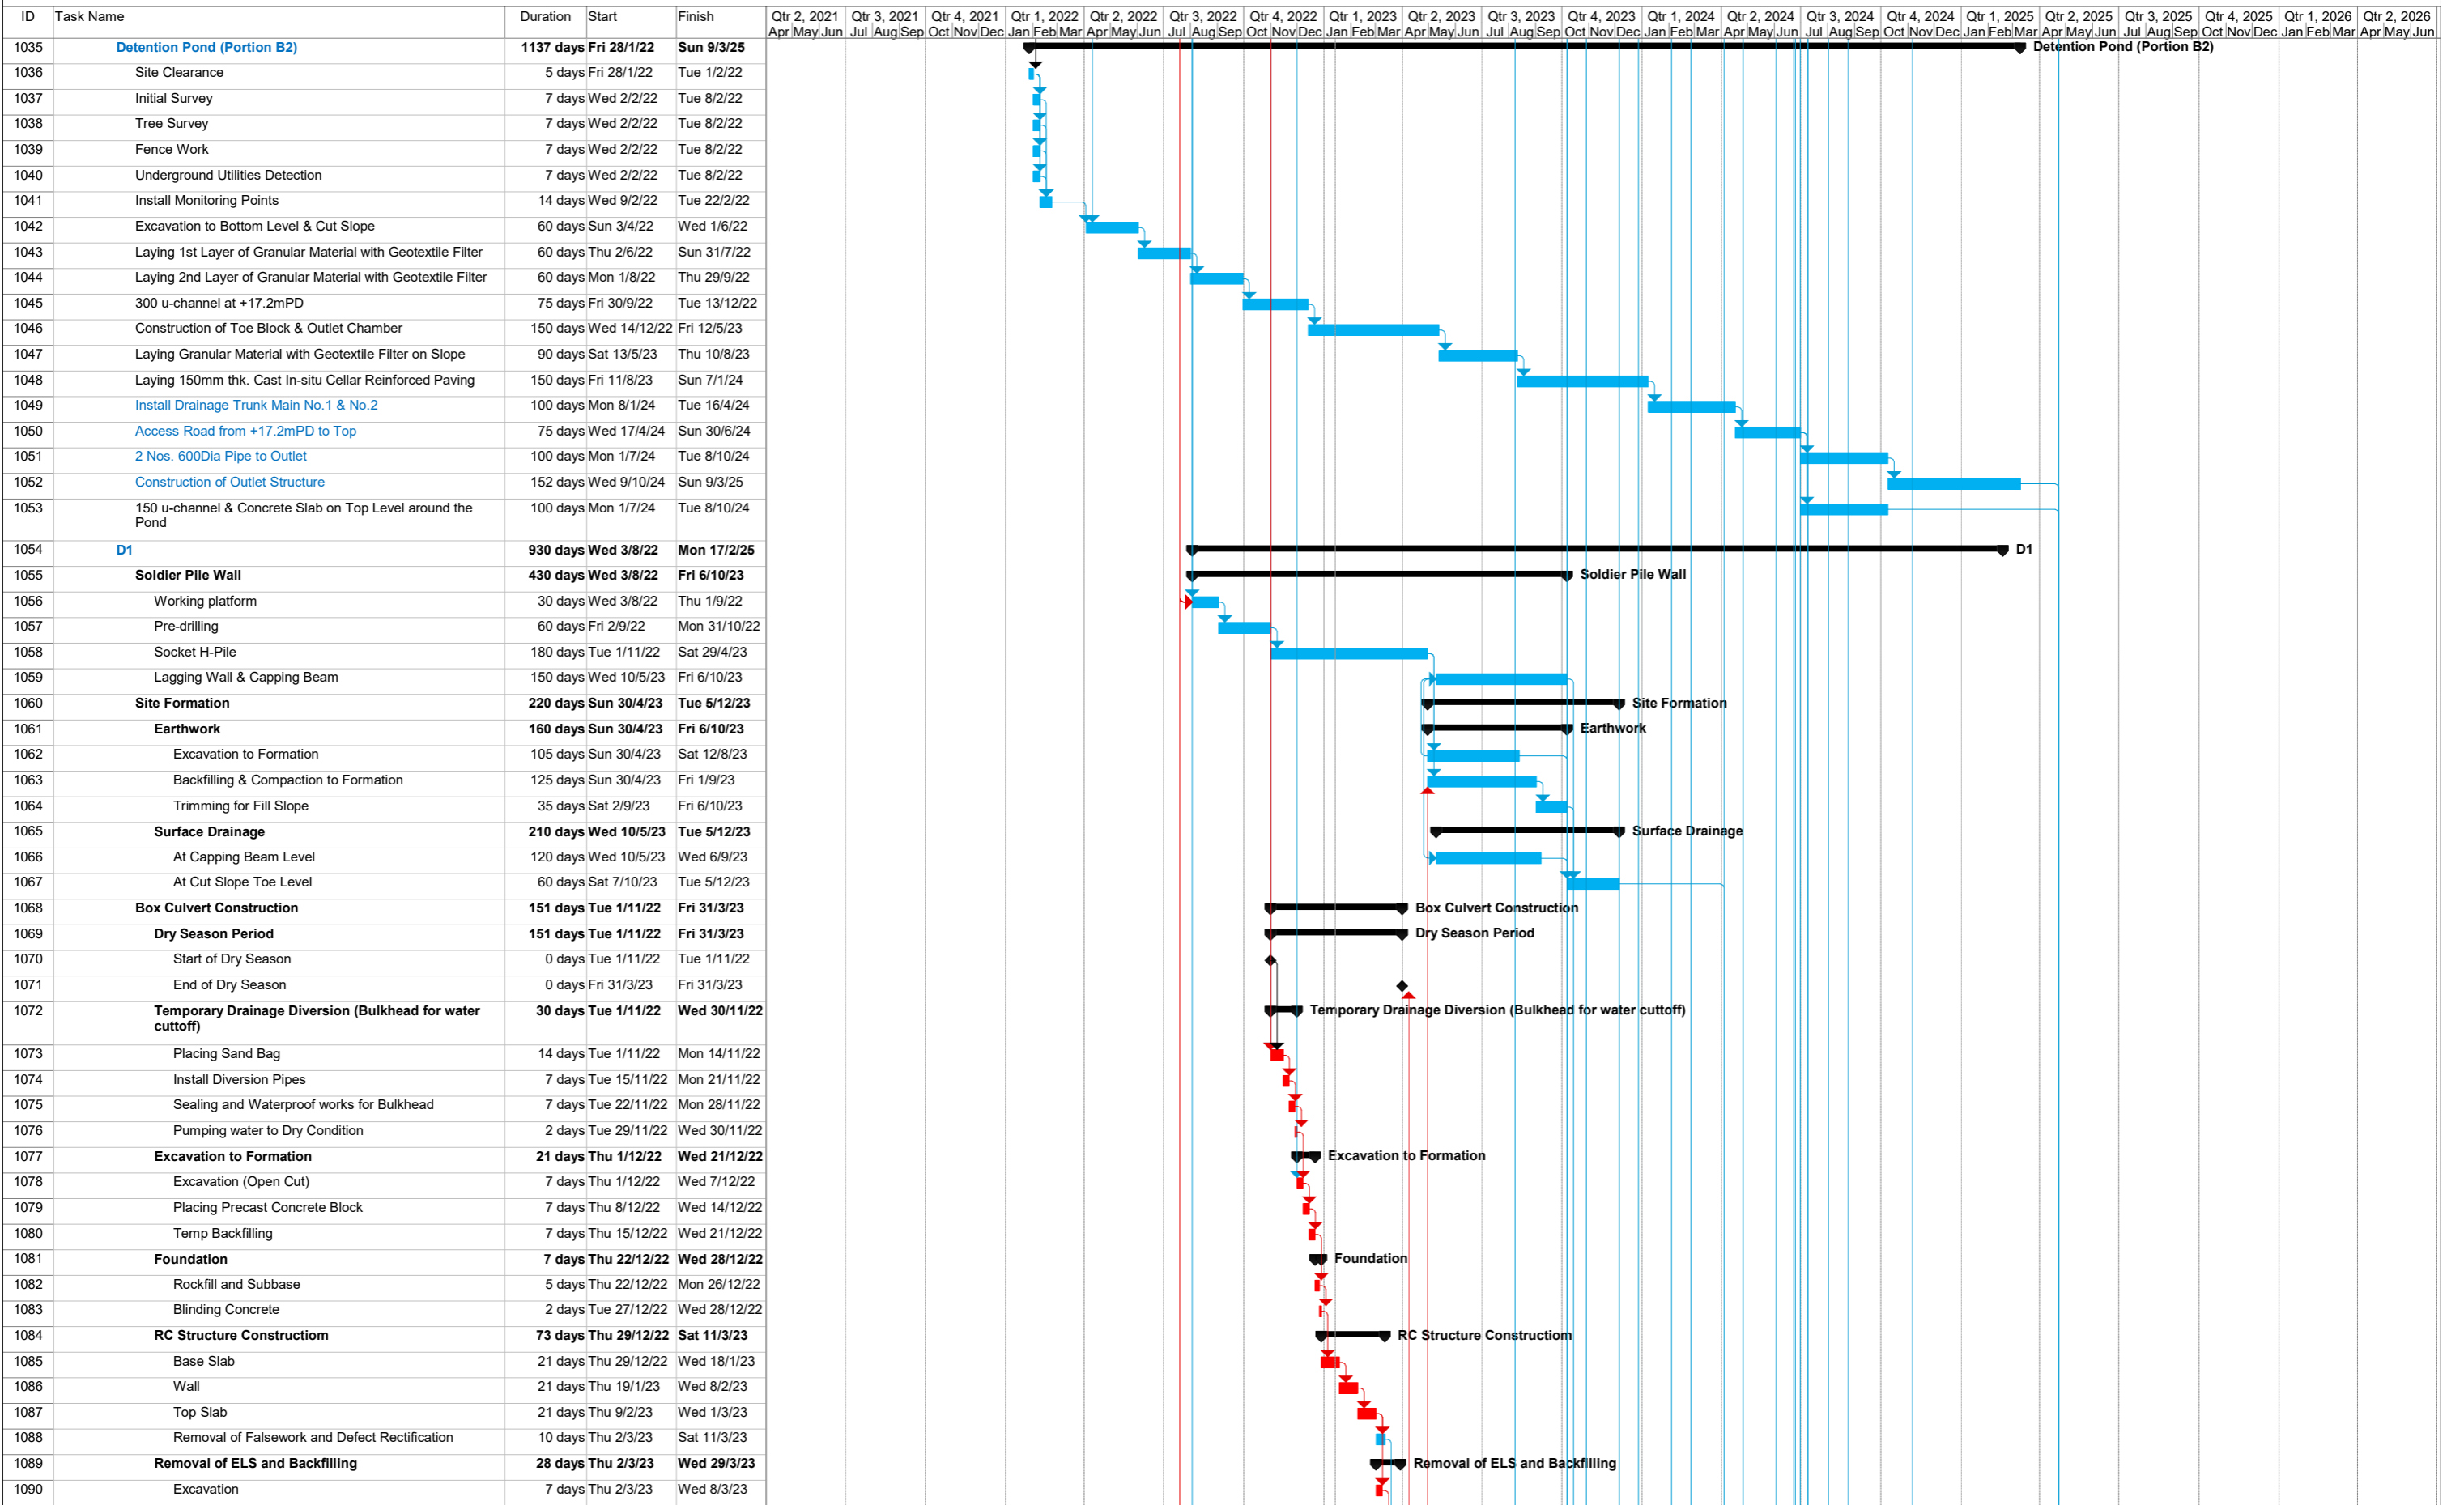

Task █ Critical Task █ Milestone ◆ Summary ▬

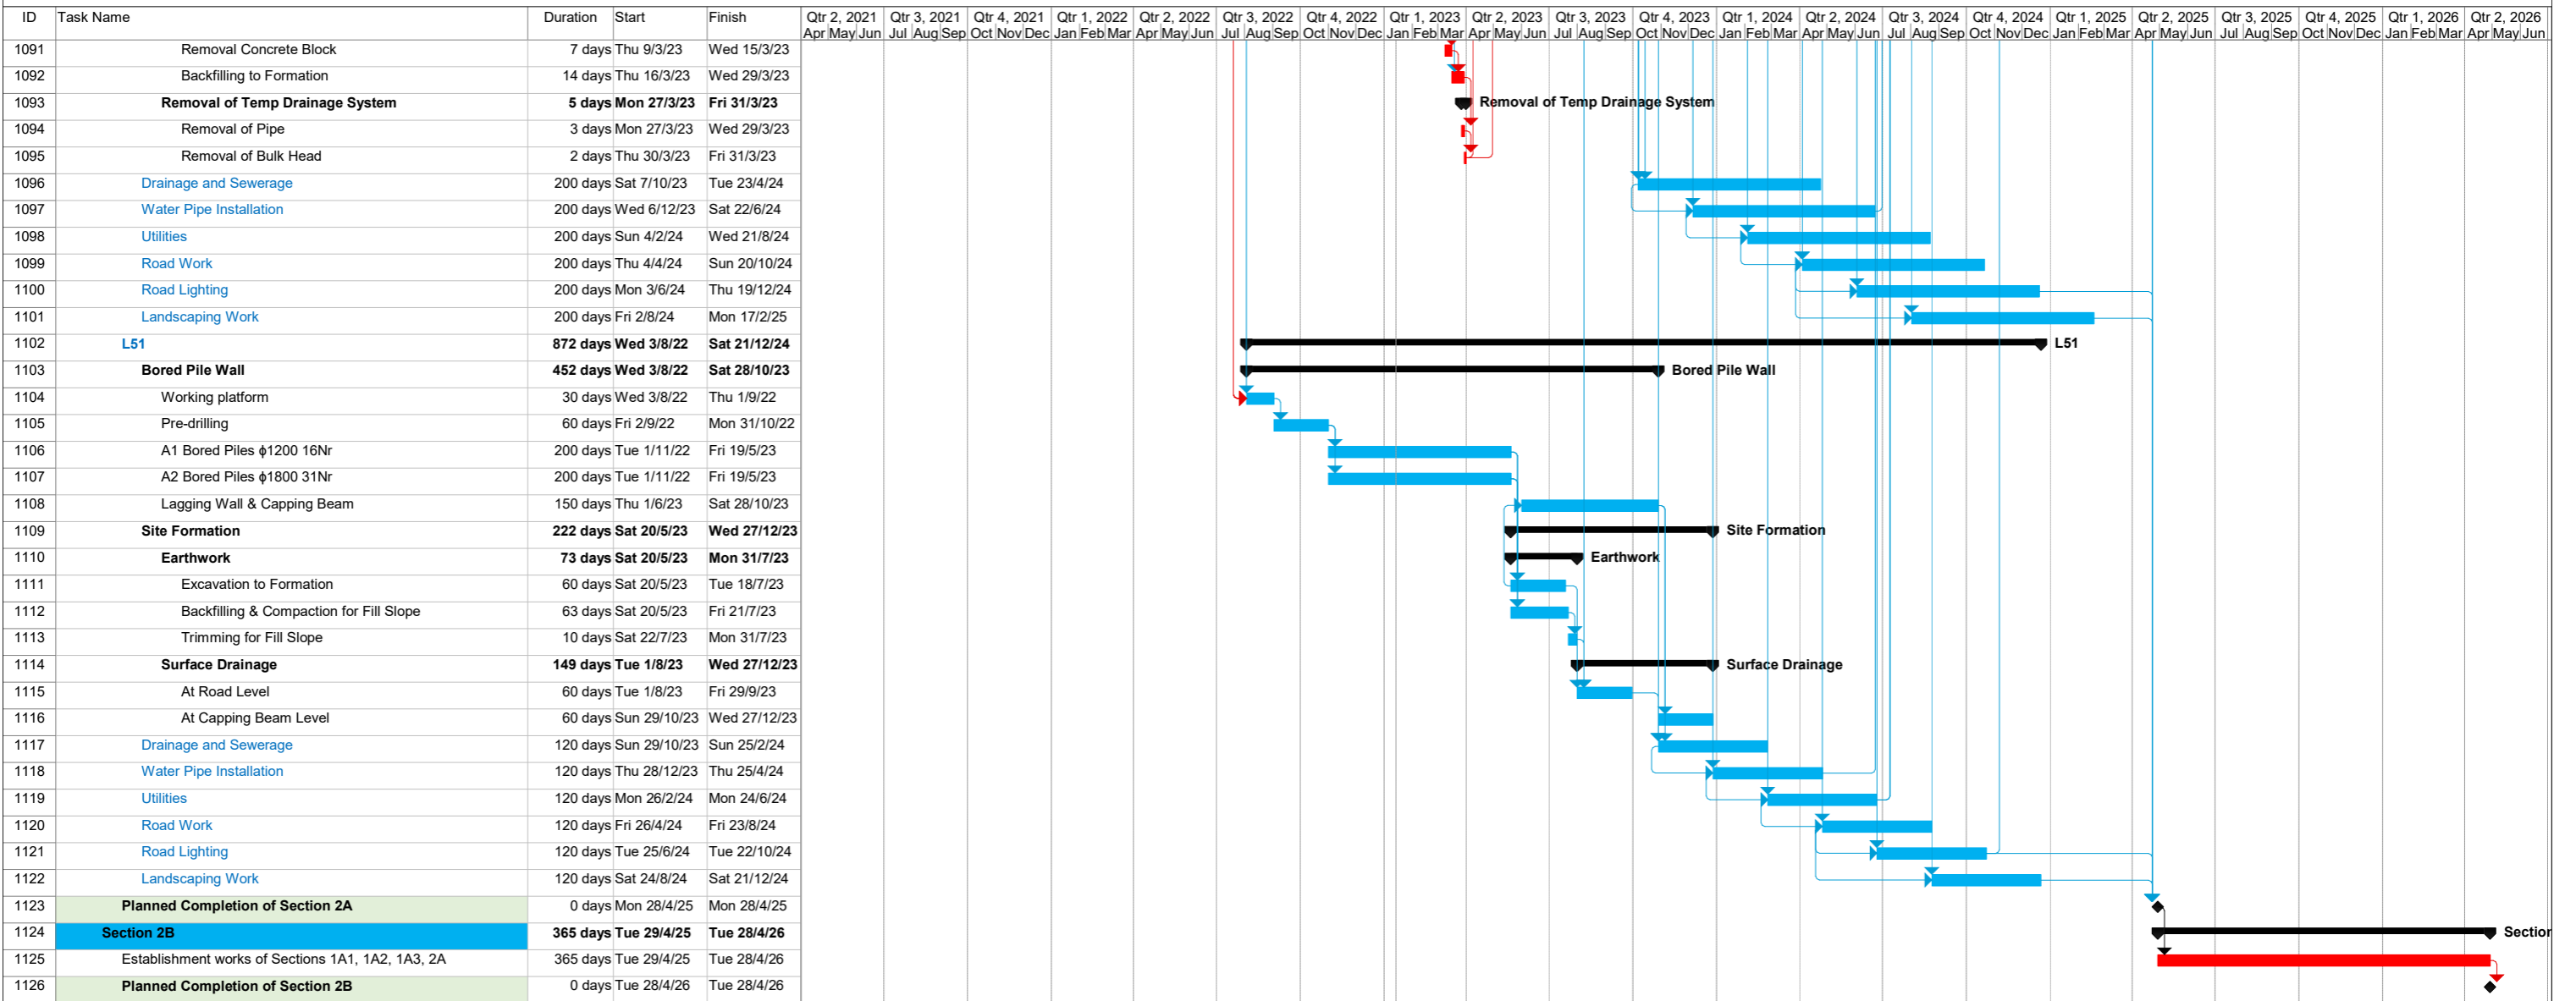

Task █ Critical Task █ Milestone ◆ Summary ▬
