

ID	Activity ID	Task Name	Duration	Remaining Duration	% Work Complete	Start	Finish	Late Start	Late Finish	Free Slack	Total Slack	Predecessors	Successors	2021	Half 2, 2021	Half 1, 2022	Half 2, 2022	Half 1, 2023	Half 2, 2023	Half 1, 2024	Half 2, 2024	Half 1, 2025	Half 2, 2025	Half 1, 2026	Half 2, 2026
1		Revised Programme of YL/2020/03	1989 days	149.38 d...	99%	Mon 19/4/21	Mon 28/9/26	Mon 19/4/21	Mon 28/9/26	0 days	0 days														
2	CD-10000	Contract Date	0 days	0 days	0%	Mon 19/4/21	Mon 19/4/21	Mon 19/4/21	Mon 19/4/21	0 days	0 days		63FS+1 day,64FS+1 day,6												
3	CD-20000	Project Dates	1980 days	0 days	0%	Wed 28/4/21	Mon 28/9/26	Wed 28/4/21	Mon 28/9/26	0 days	0 days														
4	CD-20100	Starting Date	0 days	0 days	100%	Wed 28/4/21	Wed 28/4/21	Wed 28/4/21	Wed 28/4/21	0 days	0 days		59FS+549 days,60FS+184												
5	CD-20200	Access Date 1	0 days	0 days	100%	Wed 28/4/21	Wed 28/4/21	Wed 28/4/21	Wed 28/4/21	0 days	0 days														
6	CD-20300	Access Date 122	0 days	0 days	100%	Sat 28/8/21	Sat 28/8/21	Sat 28/8/21	Sat 28/8/21	0 days	0 days														
7	CD-20400	Access Date 275	0 days	0 days	100%	Fri 28/1/22	Fri 28/1/22	Fri 28/1/22	Fri 28/1/22	0 days	0 days		57												
8	CD-20500	Access Date 456	0 days	0 days	100%	Thu 28/7/22	Thu 28/7/22	Thu 28/7/22	Thu 28/7/22	0 days	0 days		58,159FS+1 day												
9		Contract Completion Dates	913 days	913 days	0%	Sat 28/10/23	Tue 28/4/26	Sat 28/10/23	Tue 28/4/26	0 days	0 days														
10	CD-30100	Section 1A1 Completion Date: 913 Days after the Sta	0 days	0 days	0%	Sat 28/10/23	Sat 28/10/23	Sat 28/10/23	Sat 28/10/23	0 days	0 days														
11	CD-30200	Section 1A2 Completion Date: 913 Days after the Sta	0 days	0 days	0%	Sat 28/10/23	Sat 28/10/23	Sat 28/10/23	Sat 28/10/23	0 days	0 days														
12	CD-30300	Section 1A3 Completion Date: 913 Days after the Sta	0 days	0 days	0%	Sat 28/10/23	Sat 28/10/23	Sat 28/10/23	Sat 28/10/23	0 days	0 days														
13	CD-30400	Section 1A4 Completion Date: 913 Days after the Starting Date	0 days	0 days	0%	Sat 28/10/23	Sat 28/10/23	Sat 28/10/23	Sat 28/10/23	0 days	0 days														
14	CD-30500	Section 1A5 Completion Date: 913 Days after the Sta	0 days	0 days	0%	Sat 28/10/23	Sat 28/10/23	Sat 28/10/23	Sat 28/10/23	0 days	0 days														
15	CD-30600	Section 1A6 Completion Date: 913 Days after the Sta	0 days	0 days	0%	Sat 28/10/23	Sat 28/10/23	Sat 28/10/23	Sat 28/10/23	0 days	0 days														
16	CD-30700	Section 1B Completion Date: 1278 Days after the Sta	0 days	0 days	0%	Sun 27/10/23	Sun 27/10/23	Sun 27/10/23	Sun 27/10/23	0 days	0 days														
17	CD-30800	Section 2A Completion Date: 1461 Days after the Sta	0 days	0 days	0%	Mon 28/4/25	Mon 28/4/25	Mon 28/4/25	Mon 28/4/25	0 days	0 days														
18	CD-30900	Section 2B Completion Date: 1826 Days after the Sta	0 days	0 days	0%	Tue 28/4/26	Tue 28/4/26	Tue 28/4/26	Tue 28/4/26	0 days	0 days														
19		Planned Completion Dates	675 days	675 days	0%	Fri 22/11/24	Mon 28/9/26	Fri 22/11/24	Mon 28/9/26	0 days	0 days														
20	CD-31100	Section 1A1 Planned Completion Date	0 days	0 days	0%	Thu 27/3/25	Thu 27/3/25	Thu 27/3/25	Thu 27/3/25	0 days	0 days	611													
21	CD-31200	Section 1A2 Planned Completion Date	0 days	0 days	0%	Thu 27/3/25	Thu 27/3/25	Thu 27/3/25	Thu 27/3/25	0 days	0 days	701													
22	CD-31300	Section 1A3 Planned Completion Date	0 days	0 days	0%	Thu 27/3/25	Thu 27/3/25	Thu 27/3/25	Thu 27/3/25	0 days	0 days	824													
23	CD-31400	Section 1A4 Planned Completion Date	0 days	0 days	0%	Fri 22/11/24	Fri 22/11/24	Fri 22/11/24	Fri 22/11/24	0 days	0 days	895													
24	CD-31500	Section 1A5 Planned Completion Date	0 days	0 days	0%	Fri 22/11/24	Fri 22/11/24	Fri 22/11/24	Fri 22/11/24	0 days	0 days	986													
25	CD-31600	Section 1A6 Planned Completion Date	0 days	0 days	0%	Sat 27/9/25	Sat 27/9/25	Sat 27/9/25	Sat 27/9/25	0 days	0 days	1078													
26	CD-31700	Section 1B Planned Completion Date	0 days	0 days	0%	Sun 27/9/26	Sun 27/9/26	Sun 27/9/26	Sun 27/9/26	0 days	0 days	1081													
27	CD-31800	Section 2A Planned Completion Date	0 days	0 days	0%	Sun 28/9/25	Sun 28/9/25	Sun 28/9/25	Sun 28/9/25	0 days	0 days	1334,1327													
28	CD-31900	Section 2B Planned Completion Date	0 days	0 days	0%	Mon 28/9/26	Mon 28/9/26	Mon 28/9/26	Mon 28/9/26	0 days	0 days	1337													
29		Access Dates	456 days	0 days	100%	Wed 28/4/21	Thu 28/7/22	Wed 28/4/21	Thu 28/7/22	0 days	0 days														
30	CD-40100	Portion A1 Access Date: 122 days after starting date or earlier date notified by the Project Manager	0 days	0 days	100%	Sat 28/8/21	Sat 28/8/21	Sat 28/8/21	Sat 28/8/21	0 days	0 days		34												
31	CD-40200	Portion A2 Access Date: 122 days after starting date or earlier date notified by the Project Manager	0 days	0 days	100%	Tue 18/1/22	Tue 18/1/22	Tue 18/1/22	Tue 18/1/22	0 days	0 days		533,253,134,428FS+1 day,392FS+1 day,392FS+1 day,425FS+1 day												
32	CD-40300	Portion A3 Access Date: 122 days after starting date or earlier date notified by the Project Manager	0 days	0 days	100%	Tue 28/12/21	Tue 28/12/21	Tue 28/12/21	Tue 28/12/21	0 days	0 days		714,153FS+1 day,1108,134,715,1109												
33	CD-40400	Portion A4 Access Date: 122 days after starting date or earlier date notified by the Project Manager	0 days	0 days	100%	Sat 28/8/21	Sat 28/8/21	Sat 28/8/21	Sat 28/8/21	0 days	0 days														
34	CD-40500	Portion A5 Access Date: 122 days after starting date or earlier date notified by the Project Manager	0 days	0 days	100%	Sat 28/8/21	Sat 28/8/21	Sat 28/8/21	Sat 28/8/21	0 days	0 days	30	156,340												
35	CD-40600	Portion A6 Access Date: 122 days after starting date or earlier date notified by the Project Manager	0 days	0 days	100%	Sat 28/8/21	Sat 28/8/21	Sat 28/8/21	Sat 28/8/21	0 days	0 days		153FS+1 day,1108,1109												
36	CD-40700	Portion A7 Access Date: 122 days after starting date or earlier date notified by the Project Manager	0 days	0 days	100%	Sat 28/8/21	Sat 28/8/21	Sat 28/8/21	Sat 28/8/21	0 days	0 days		153FS+1 day,1108,1109												
37	CD-40800	Portion A8 Access Date: 122 days after starting date or earlier date notified by the Project Manager	0 days	0 days	100%	Sat 28/8/21	Sat 28/8/21	Sat 28/8/21	Sat 28/8/21	0 days	0 days		153FS+1 day,1108,1109												
38	CD-40900	Portion B1 Access Date: 275 days after starting date or earlier date notified by the Project Manager	0 days	0 days	100%	Fri 28/1/22	Fri 28/1/22	Fri 28/1/22	Fri 28/1/22	0 days	0 days		534,303SS+1 day												
39	CD-41000	Portion B2 Access Date: 275 days after starting date or earlier date notified by the Project Manager	0 days	0 days	100%	Fri 28/1/22	Fri 28/1/22	Fri 28/1/22	Fri 28/1/22	0 days	0 days		534,1133,344FS+1 day,303SS+1 day												
40	CD-41400	Portion B6 Access Date: 275 days after starting date or earlier date notified by the Project Manager	0 days	0 days	100%	Fri 28/1/22	Fri 28/1/22	Fri 28/1/22	Fri 28/1/22	0 days	0 days		348FS+1 day,161FS+1 day												
41	CD-41500	Portion B7 Access Date: 275 days after starting date or earlier date notified by the Project Manager	0 days	0 days	100%	Fri 28/1/22	Fri 28/1/22	Fri 28/1/22	Fri 28/1/22	0 days	0 days		42												
42	CD-41600	Portion B8 Access Date: 275 days after starting date or earlier date notified by the Project Manager	0 days	0 days	100%	Fri 28/1/22	Fri 28/1/22	Fri 28/1/22	Fri 28/1/22	0 days	0 days	41													

Task

Critical Task

Milestone

Summary

Page 2

E=Excavator L=Lorry W=Worker D=Drill plant C=Crane Lorry R=Rotter

ID	Activity ID	Task Name	Duration	Remaining Duration	% Work Complete	Start	Finish	Late Start	Late Finish	Free Slack	Total Slack	Predecessors	Successors	2021	Half 2, 2021	Half 1, 2022	Half 2, 2022	Half 1, 2023	Half 2, 2023	Half 1, 2024	Half 2, 2024	Half 1, 2025	Half 2, 2025	Half 1, 2026	Half 2, 2026
80	PRE-11800	Temp Drainage Management Plan	30 days	0 days	100%	Thu 29/4/21	Fri 28/5/21	Thu 29/4/21	Fri 28/5/21	0 days	0 days	4FS+1 day	86												
81	PRE-11900	Contingency Plan to deal with Flooding	30 days	0 days	100%	Thu 29/4/21	Fri 28/5/21	Thu 29/4/21	Fri 28/5/21	0 days	0 days	4FS+1 day	86												
82	PRE-12000	Supply of Brand New Survey Equipment (PS Append	30 days	0 days	100%	Thu 29/4/21	Fri 28/5/21	Thu 29/4/21	Fri 28/5/21	0 days	0 days	4FS+1 day	86												
83	PRE-12100	Site Uniform (PS1.88)	30 days	0 days	100%	Thu 29/4/21	Fri 28/5/21	Thu 29/4/21	Fri 28/5/21	0 days	0 days	4FS+1 day	86												
84	PRE-12200	PII insurance Policy	60 days	0 days	100%	Tue 20/4/21	Fri 18/6/21	Tue 20/4/21	Fri 18/6/21	0 days	0 days	2FS+1 day													
85	PRE-12300	Book with a certification body acceptable to the Employer the date of audit for the ISO 9001:2015 certification	90 days	0 days	100%	Thu 29/4/21	Tue 27/7/21	Thu 29/4/21	Tue 27/7/21	0 days	0 days	4FS+1 day													
86	PRE-13000	Completion of Initial General Submission	0 days	0 days	100%	Fri 28/5/21	Fri 28/5/21	Fri 28/5/21	Fri 28/5/21	0 days	0 days	63,64,65,66,67,68,69,137													
87	PRE-20000	Programme	104 days	0 days	100%	Tue 20/4/21	Sun 1/8/21	Tue 20/4/21	Sun 1/8/21	0 days	0 days														
88	PRE-20100	First Programme (CDP1.3)	14 days	0 days	100%	Tue 20/4/21	Mon 3/5/21	Tue 20/4/21	Mon 3/5/21	0 days	0 days	2FS+1 day	89,91												
89	PRE-20200	Acceptance of the First Programme	30 days	0 days	100%	Tue 4/5/21	Wed 2/6/21	Tue 4/5/21	Wed 2/6/21	0 days	0 days	88	90,92												
90	PRE-20300	Expanded and more detailed version of the first programme (PSA 1.3)	60 days	0 days	100%	Thu 3/6/21	Sun 1/8/21	Thu 3/6/21	Sun 1/8/21	0 days	0 days	89													
91	PRE-20400	First Monthly Progress Report (PS1.08A)	30 days	0 days	100%	Tue 4/5/21	Wed 2/6/21	Tue 4/5/21	Wed 2/6/21	0 days	0 days	88	92												
92	PRE-23000	Completion of Initial Programme Submission	0 days	0 days	100%	Wed 2/6/21	Wed 2/6/21	Wed 2/6/21	Wed 2/6/21	0 days	0 days	89,91	137												
93	PRE-30000	Appointment of Personnel	99 days	0 days	100%	Tue 20/4/21	Tue 27/7/21	Tue 20/4/21	Tue 27/7/21	0 days	0 days														
94	PRE-30100	Contractor's Labour Officer (PS29.09)	7 days	0 days	100%	Tue 20/4/21	Mon 26/4/21	Tue 20/4/21	Mon 26/4/21	0 days	0 days	2FS+1 day	112												
95	PRE-30200	Contractor's Surveyor (PS1.09)	7 days	0 days	100%	Thu 29/4/21	Wed 5/5/21	Thu 29/4/21	Wed 5/5/21	0 days	0 days	4FS+1 day	112												
96	PRE-30300	List of Staff for Construction Management Team (ACC	14 days	0 days	100%	Thu 29/4/21	Wed 12/5/21	Thu 29/4/21	Wed 12/5/21	0 days	0 days	4FS+1 day	112												
97	PRE-30400	RSO and SS (ACC D1)	14 days	0 days	100%	Thu 29/4/21	Wed 12/5/21	Thu 29/4/21	Wed 12/5/21	0 days	0 days	4FS+1 day	112												
98	PRE-30500	E0 and ES (ACC D1)	14 days	0 days	100%	Thu 29/4/21	Wed 12/5/21	Thu 29/4/21	Wed 12/5/21	0 days	0 days	4FS+1 day	112												
99	PRE-30600	Site Agents and Employees (PS1.12)	14 days	0 days	100%	Thu 29/4/21	Wed 12/5/21	Thu 29/4/21	Wed 12/5/21	0 days	0 days	4FS+1 day	112												
100	PRE-30700	Construction Manager (PS1.12A)	14 days	0 days	100%	Thu 29/4/21	Wed 12/5/21	Thu 29/4/21	Wed 12/5/21	0 days	0 days	4FS+1 day	112												
101	PRE-30800	Construction, Landscape and Land Decontamination Leader (PS1.12B)	14 days	0 days	100%	Thu 29/4/21	Wed 12/5/21	Thu 29/4/21	Wed 12/5/21	0 days	0 days	4FS+1 day	112												
102	PRE-30900	Geotechnical Engineer, Geologist, Geotechnical Supervisor and GFT (1.12C)	14 days	0 days	100%	Thu 29/4/21	Wed 12/5/21	Thu 29/4/21	Wed 12/5/21	0 days	0 days	4FS+1 day	112												
103	PRE-31000	Foreman for Road and Drainage Works	14 days	0 days	100%	Thu 29/4/21	Wed 12/5/21	Thu 29/4/21	Wed 12/5/21	0 days	0 days	4FS+1 day	112												
104	PRE-31100	Particulars of Emergency Unit (PS1.99)	14 days	0 days	100%	Thu 29/4/21	Wed 12/5/21	Thu 29/4/21	Wed 12/5/21	0 days	0 days	4FS+1 day	112												
105	PRE-31200	Tree Supervisor (PS26.02)	30 days	0 days	100%	Tue 20/4/21	Wed 19/5/21	Tue 20/4/21	Wed 19/5/21	0 days	0 days	2FS+1 day	112												
106	PRE-31300	Public Relocation Officer (PS 1.12F)	28 days	0 days	100%	Thu 29/4/21	Wed 26/5/21	Thu 29/4/21	Wed 26/5/21	0 days	0 days	4FS+1 day	112												
107	PRE-31400	Quantity Surveying Clerk (PS1.49)	28 days	0 days	100%	Thu 29/4/21	Wed 26/5/21	Thu 29/4/21	Wed 26/5/21	0 days	0 days	4FS+1 day	112												
108	PRE-31500	Field and Drafting assistant (PS1.49C)	28 days	0 days	100%	Thu 29/4/21	Wed 26/5/21	Thu 29/4/21	Wed 26/5/21	0 days	0 days	4FS+1 day	112												
109	PRE-31600	Independent Checking Engineer (PS1.105)	30 days	0 days	100%	Thu 29/4/21	Fri 28/5/21	Thu 29/4/21	Fri 28/5/21	0 days	0 days	4FS+1 day	112												
110	PRE-31700	Employ CEG and TA (PS1.83)	90 days	0 days	100%	Thu 29/4/21	Tue 27/7/21	Thu 29/4/21	Tue 27/7/21	0 days	0 days	4FS+1 day													
111	PRE-31800	BIM Team Leader (PS1.108)	90 days	0 days	100%	Thu 29/4/21	Tue 27/7/21	Thu 29/4/21	Tue 27/7/21	0 days	0 days	4FS+1 day,200FF													
112	PRE-33000	Completion of Construction Management Team Subm	0 days	0 days	100%	Fri 28/5/21	Fri 28/5/21	Fri 28/5/21	Fri 28/5/21	0 days	0 days	94,95,96,97,98,99,100	137												
113	PRE-40000	Safety	42 days	0 days	100%	Tue 20/4/21	Mon 31/5/21	Tue 20/4/21	Mon 31/5/21	0 days	0 days														
114	PRE-40100	Draft Construction Health and Safety Plan (ACC D6)	14 days	0 days	100%	Tue 20/4/21	Mon 3/5/21	Tue 20/4/21	Mon 3/5/21	0 days	0 days	2FS+1 day	115												
115	PRE-40200	Ad-hoc meeting with Supervisor or discuss the draft Safety Plan (ACC D6)	7 days	0 days	100%	Tue 4/5/21	Mon 10/5/21	Tue 4/5/21	Mon 10/5/21	0 days	0 days	114	121												
116	PRE-40300	Monthly Reports on Safety Performance (ACC D28)	30 days	0 days	100%	Tue 20/4/21	Wed 19/5/21	Tue 20/4/21	Wed 19/5/21	0 days	0 days	2FS+1 day	121												
117	PRE-40400	Monthly Safety Report	30 days	0 days	100%	Tue 20/4/21	Wed 19/5/21	Tue 20/4/21	Wed 19/5/21	0 days	0 days	2FS+1 day	121												
118	PRE-40500	Submission of Safety Plan (ACC D6)	35 days	0 days	100%	Tue 20/4/21	Mon 24/5/21	Tue 20/4/21	Mon 24/5/21	0 days	0 days	2FS+1 day	121												
119	PRE-40600	Establish and conduct first SSC and SSMC meeting (	40 days	0 days	100%	Tue 20/4/21	Sat 29/5/21	Tue 20/4/21	Sat 29/5/21	0 days	0 days	2FS+1 day	121												
120	PRE-40700	Site Traffic Safety Management Plan (PS1.71C)	42 days	0 days	100%	Tue 20/4/21	Mon 31/5/21	Tue 20/4/21	Mon 31/5/21	0 days	0 days	2FS+1 day	121												
121	PRE-43000	Completion of Initial Safety Submission	0 days	0 days	100%	Mon 31/5/21	Mon 31/5/21	Mon 31/5/21	Mon 31/5/21	0 days	0 days	115,116,117,118,119,137													
122	PRE-50000	Environmental	573 days	0 days	100%	Tue 20/4/21	Sun 13/11/21	Tue 20/4/21	Sun 13/11/21	0 days	0 days														
123	PRE-50100	Register of the DDF and Trip Ticket System	14 days	0 days	100%	Tue 20/4/21	Mon 3/5/21	Tue 20/4/21	Mon 3/5/21	0 days	0 days	2FS+1 day	136												
124	PRE-50200	Draft Environmental Management Plan (ACC D20, PS	21 days	0 days	100%	Tue 20/4/21	Mon 10/5/21	Tue 20/4/21	Mon 10/5/21	0 days	0 days	2FS+1 day	136												
125	PRE-50300	Daily Cleaning Supervisor (PS1.32)	21 days	0 days	100%	Tue 20/4/21	Mon 10/5/21	Tue 20/4/21	Mon 10/5/21	0 days	0 days	2FS+1 day	136,1286												
126	PRE-50400	Inspection Checklist for Daily Cleaning (PS1.32)	21 days	0 days	100%	Tue 20/4/21	Mon 10/5/21	Tue 20/4/21	Mon 10/5/21	0 days	0 days	2FS+1 day	136												
127	PRE-50500	Monthly Reports on Environmental Management (PS1	30 days	0 days	100%	Tue 20/4/21	Wed 19/5/21	Tue 20/4/21	Wed 19/5/21	0 days	0 days	2FS+1 day	136												
128	PRE-50600	Rodents Disinestation Operation	14 days	0 days	100%	Thu 29/4/21	Wed 12/5/21	Thu 29/4/21	Wed 12/5/21	0 days	0 days	4FS+1 day	136												
129	PRE-50700	Apply for registration as Chemical Waste Producer (C	21 days	0 days	100%	Thu 29/4/21	Wed 19/5/21	Thu 29/4/21	Wed 19/5/21	0 days	0 days	4FS+1 day	136												

ID	Activity ID	Task Name	Duration	Remaining Duration	% Work Complete	Start	Finish	Late Start	Late Finish	Free Slack	Total Slack	Predecessors	Successors	2021	Half 1, 2021	Half 1, 2022	Half 2, 2022	Half 1, 2023	Half 2, 2023	Half 1, 2024	Half 2, 2024	Half 1, 2025	Half 2, 2025	Half 1, 2026	Half 2, 2026
130	PRE-50800	Trip Ticket System Proposal	21 days	0 days	100%	Thu 29/4/21	Wed 19/5/21	Thu 29/4/21	Wed 19/5/21	0 days	0 days	4FS+1 day	136												
131	PRE-50900	Site Management Plan for implementation of Trip Ticket System (PS25.25S)	45 days	0 days	100%	Tue 20/4/21	Thu 3/6/21	Tue 20/4/21	Thu 3/6/21	0 days	0 days	2FS+1 day	136												
132	PRE-51000	Finalized Environmental Management Plan	45 days	0 days	100%	Tue 20/4/21	Thu 3/6/21	Tue 20/4/21	Thu 3/6/21	0 days	0 days	2FS+1 day	136												
133	PRE-51200	Application of Discharge License - First Batch	45 days	0 days	100%	Thu 29/4/21	Sat 12/6/21	Thu 29/4/21	Sat 12/6/21	0 days	0 days	4FS+1 day	571												
134	PRE-51300	Application of Discharge License - Second Batch	45 days	0 days	100%	Tue 18/1/22	Thu 3/3/22	Tue 18/1/22	Thu 3/3/22	0 days	0 days	31,32	866,667												
135	PRE-51400	Application of Discharge License - Third Batch	45 days	0 days	100%	Fri 30/9/22	Sun 13/1/23	Fri 30/9/22	Sun 13/1/23	0 days	0 days	52	861,862												
136	PRE-53000	Completion of Initial Environmental Submission	0 days	0 days	100%	Thu 3/6/21	Thu 3/6/21	Thu 3/6/21	Thu 3/6/21	0 days	0 days	123,124,125,126,127, 137													
137	PRE-54000	Ready for Commencement of Site Works	0 days	0 days	100%	Thu 3/6/21	Thu 3/6/21	Thu 3/6/21	Thu 3/6/21	0 days	0 days	86,92,112,121,136													
138	PRE-60000	Public Relation	60 days	0 days	100%	Thu 29/4/21	Sun 27/6/21	Thu 29/4/21	Sun 27/6/21	0 days	0 days														
139	PRE-60100	Provision of PRO (PS1.12F)	30 days	0 days	100%	Thu 29/4/21	Fri 28/5/21	Thu 29/4/21	Fri 28/5/21	0 days	0 days	4FS+1 day													
140	PRE-60200	Setup 24-hour telephone line cum information centre	60 days	0 days	100%	Thu 29/4/21	Sun 27/6/21	Thu 29/4/21	Sun 27/6/21	0 days	0 days	4FS+1 day													
141	PRE-70000	Traffic Management	147 days	0 days	100%	Thu 29/4/21	Wed 22/9/21	Thu 29/4/21	Wed 22/9/21	0 days	0 days														
142	PRE-70100	Traffic Consultant and Traffic Engineer (PS1.16A)	7 days	0 days	100%	Thu 29/4/21	Wed 5/5/21	Thu 29/4/21	Wed 5/5/21	0 days	0 days	4FS+1 day	143												
143	PRE-70200	Prepare Detailed Construction Sequence with associated TTA and obtain endorsement in principle	24 days	0 days	100%	Thu 1/7/21	Sat 24/7/21	Thu 1/7/21	Sat 24/7/21	0 days	0 days	142,182	144,145												
144	PRE-70300	Setup TMLG	30 days	0 days	100%	Sun 25/7/21	Mon 23/8/21	Sun 25/7/21	Mon 23/8/21	0 days	0 days	143	146												
145	PRE-70400	Setup SLG	30 days	0 days	100%	Sun 25/7/21	Mon 23/8/21	Sun 25/7/21	Mon 23/8/21	0 days	0 days	143	146												
146	PRE-70500	Arrange First TMLG meeting	30 days	0 days	100%	Tue 24/8/21	Wed 22/9/21	Tue 24/8/21	Wed 22/9/21	0 days	0 days	144,145	465												
147	PRE-80000	Excavation Permit	719 days	0 days	100%	Thu 29/4/21	Mon 17/4/22	Thu 29/4/21	Mon 17/4/22	0 days	0 days														
148	PRE-80100	Request employer to apply for XP (ACC D18)	7 days	0 days	100%	Thu 29/4/21	Wed 5/5/21	Thu 29/4/21	Wed 5/5/21	0 days	0 days	4FS+1 day	150												
149	PRE-80200	1st Batch of XP (Ping Ha Road)	100 days	0 days	100%	Thu 6/5/21	Fri 13/8/21	Thu 6/5/21	Fri 13/8/21	0 days	0 days														
150	PRE-80210	Prepare Particular for XP Application	40 days	0 days	100%	Thu 6/5/21	Mon 14/6/21	Thu 6/5/21	Mon 14/6/21	0 days	0 days	148	151												
151	PRE-80220	Application and Approval of Excavation Permit for street maintained by HyD - (ACCX D18). Plan ID 1305926 XP is issued. Plan ID 1305459 XP is issued. Plan ID 1305928 XP is issued.	60 days	0 days	100%	Tue 15/6/21	Fri 13/8/21	Tue 15/6/21	Fri 13/8/21	0 days	0 days	150	327												
152	PRE-80300	2nd Batch of XP (Ha Tsuen Road)	120 days	0 days	100%	Tue 29/12/21	Wed 27/4/22	Wed 29/1/22	Wed 27/4/22	0 days	0 days														
153	PRE-80310	Prepare particular for XP Application	60 days	0 days	100%	Tue 29/12/21	Sat 26/2/22	Wed 29/1/22	Sat 26/2/22	0 days	0 days	32FS+1 day,35FS+1 day	154												
154	PRE-80320	Application and approval of Excavation Permit for street maintained by HyD - (ACC D18). Plan ID 1315864 is under case coordination.	60 days	0 days	100%	Sun 27/2/22	Wed 27/4/22	Sun 27/2/22	Wed 27/4/22	0 days	0 days	153	470,1131												
155	PRE-80400	3rd Batch of XP (Fung Kong Tsuen Road)	200 days	0 days	100%	Fri 30/9/22	Mon 17/4/23	Fri 30/9/22	Mon 17/4/23	0 days	0 days														
156	PRE-80410	Prepare particular for XP Application	80 days	0 days	100%	Fri 30/9/22	Sun 18/12/22	Fri 30/9/22	Sun 18/1/23	0 days	0 days	34,44,52	157												
157	PRE-80420	Application and approval of Excavation Permit for street maintained by HyD - (ACC D18). Plan ID 1305467 XP is issued. Plan ID 1320028 XP is issued. Plan ID 1333983 XP is issued.	120 days	0 days	100%	Mon 19/12/22	Mon 17/4/23	Mon 19/12/22	Mon 17/4/23	0 days	0 days	156	475,283,480												
158	PRE-90000	Utilities Works	1185 days	0 days	100%	Tue 28/12/22	Thu 27/3/25	Tue 28/12/22	Thu 27/3/25	0 days	0 days														
159	PRE-90100	Setup of Utilities Liaison Group	90 days	0 days	100%	Fri 29/7/22	Wed 26/10/22	Fri 29/7/22	Wed 26/1/23	0 days	0 days	8FS+1 day	163												
160	PRE-90200	Diversion Scheme of Existing Utilities, if any	391 days	0 days	100%	Sat 29/1/22	Thu 23/2/23	Sat 29/1/22	Thu 23/2/23	0 days	0 days														
161	PRE-90210	Drainage Diversion (Existing Stream at Road D1)	150 days	0 days	100%	Sat 29/1/22	Mon 27/6/22	Sat 29/1/22	Mon 27/6/22	0 days	0 days	40FS+1 day	349FF												
162	PRE-90220	Existing Service at Road D1 and L51	60 days	0 days	100%	Mon 26/12/22	Thu 23/2/23	Mon 26/12/22	Thu 23/2/23	0 days	0 days	163	1314,1261,1234,1210,124												
163	PRE-90230	Existing Service at Road L53 and L54	60 days	0 days	100%	Thu 27/10/22	Sun 25/12/22	Thu 27/10/22	Sun 25/1/23	0 days	0 days	159	989,162,1039												
164	PRE-90300	New Utilities Connection	1185 days	0 days	100%	Tue 28/12/22	Thu 27/3/25	Tue 28/12/22	Thu 27/3/25	0 days	0 days														
165	PRE-90310	Watermain	73 days	0 days	100%	Mon 13/1/23	Thu 27/3/25	Mon 13/1/23	Thu 27/3/25	0 days	0 days														
166	PRE-90311	Road D1, L51 and Ha Tsuen Road	0 days	0 days	100%	Fri 28/2/25	Fri 28/2/25	Fri 28/2/25	Fri 28/2/25	0 days	0 days	1111SS	1114FF												
167	PRE-90312	Road L53 and L54	30 days	0 days	100%	Mon 13/1/25	Tue 11/2/25	Mon 13/1/25	Tue 11/2/25	0 days	0 days	999SS,1051SS	1054FF												
168	PRE-90313	Ping Ha Road	0 days	0 days	100%	Thu 27/3/25	Thu 27/3/25	Thu 27/3/25	Thu 27/3/25	0 days	0 days	1101SS	1104FF												
169	PRE-90320	Road Lighting System	531 days	0 days	100%	Thu 31/8/23	Wed 12/2/24	Thu 31/8/23	Wed 12/2/24	0 days	0 days														
170	PRE-90321	Road D1 and L51	0 days	0 days	100%	Thu 31/8/23	Thu 31/8/23	Thu 31/8/23	Thu 31/8/23	0 days	0 days	1325FF	1289,1327												
171	PRE-90322	Road L53 and L54	60 days	0 days	100%	Sat 21/11/24	Wed 12/2/25	Sat 21/11/24	Wed 12/2/25	0 days	0 days	1068FF	1068												
172	PRE-90330	CLP	1017 days	0 days	100%	Tue 28/12/22	Wed 9/10/24	Tue 28/12/22	Wed 9/10/24	0 days	0 days														
173	PRE-90331	Road D1 and L51	0 days	0 days	100%	Tue 28/12/22	Tue 28/12/22	Tue 28/12/22	Tue 28/12/22	0 days	0 days	1316FF	1327,1289												
174	PRE-90332	Road L53 and L54	60 days	0 days	100%	Sun 11/8/24	Wed 9/10/24	Sun 11/8/24	Wed 9/10/24	0 days	0 days	1003FF,1055FF	1068												

ID	Activity ID	Task Name	Duration	Remaining Duration	% Work Complete	Start	Finish	Late Start	Late Finish	Free Slack	Total Slack	Predecessors	Successors	2021	Half 2, 2021	Half 1, 2022	Half 2, 2022	Half 1, 2023	Half 2, 2023	Half 1, 2024	Half 2, 2024	Half 1, 2025	Half 2, 2025	Half 1, 2026	Half 2, 2026
175	PRE-90340	Telecom (HKT, HGC, HKBN)	977 days	0 days	100%	Fri 25/2/22	Tue 29/10/21	Fri 25/2/22	Tue 29/1/...	0 days	0 days														
176	PRE-90341	Road D1 and L51	0 days	0 days	100%	Fri 25/2/22	Fri 25/2/22	Fri 25/2/22	Fri 25/2/22	0 days	0 days	1316FF	1327,1289												
177	PRE-90342	Road L53 and L54	60 days	0 days	100%	Sat 31/8/24	Tue 29/10/21	Sat 31/8/24	Tue 29/1/...	0 days	0 days	1003FF,1055FF	1068												
178		Procurement	983 days	0 days	100%	Wed 28/4/21	Fri 5/1/24	Wed 28/4/...	Fri 5/1/24	0 days	0 days														
179	PS-10000	Subcontracting / Procurement	652 days	0 days	100%	Thu 29/4/21	Thu 9/2/23	Thu 29/4/21	Thu 9/2/23	0 days	0 days														
180	PS-10100	Traffic Consultant	63 days	0 days	100%	Thu 29/4/21	Wed 30/6/21	Thu 29/4/21	Wed 30/6/...	0 days	0 days														
181	PS-10110	Subletting	28 days	0 days	100%	Thu 29/4/21	Wed 26/5/21	Thu 29/4/21	Wed 26/5/...	0 days	0 days	4FS+1 day	182												
182	PS-10120	Submission and Approval	35 days	0 days	100%	Thu 27/5/21	Wed 30/6/21	Thu 27/5/21	Wed 30/6/...	0 days	0 days	181	143												
183	PS-10200	Independent Checking Engineer	63 days	0 days	100%	Thu 29/4/21	Wed 30/6/21	Thu 29/4/21	Wed 30/6/...	0 days	0 days														
184	PS-10210	Subletting	28 days	0 days	100%	Thu 29/4/21	Wed 26/5/21	Thu 29/4/21	Wed 26/5/...	0 days	0 days	4FS+1 day	185												
185	PS-10220	Submission and Approval	35 days	0 days	100%	Thu 27/5/21	Wed 30/6/21	Thu 27/5/21	Wed 30/6/...	0 days	0 days	184													
186	PS-10300	PM's Accommodation (MIC Method)	63 days	0 days	100%	Thu 29/4/21	Wed 30/6/21	Thu 29/4/21	Wed 30/6/...	0 days	0 days														
187	PS-10310	Subletting	28 days	0 days	100%	Thu 29/4/21	Wed 26/5/21	Thu 29/4/21	Wed 26/5/...	0 days	0 days	4FS+1 day	188												
188	PS-10320	Submission and Approval	35 days	0 days	100%	Thu 27/5/21	Wed 30/6/21	Thu 27/5/21	Wed 30/6/...	0 days	0 days	187	274												
189	PS-10400	Environmental Team and Team Leader	63 days	0 days	100%	Thu 29/4/21	Wed 30/6/21	Thu 29/4/21	Wed 30/6/...	0 days	0 days														
190	PS-10410	Subletting	28 days	0 days	100%	Thu 29/4/21	Wed 26/5/21	Thu 29/4/21	Wed 26/5/...	0 days	0 days	4FS+1 day	191												
191	PS-10420	Submission and Approval	35 days	0 days	100%	Thu 27/5/21	Wed 30/6/21	Thu 27/5/21	Wed 30/6/...	0 days	0 days	190	487												
192	PS-10500	Tree Survey and Treatment	63 days	0 days	100%	Thu 29/4/21	Wed 30/6/21	Thu 29/4/21	Wed 30/6/...	0 days	0 days														
193	PS-10510	Subletting	28 days	0 days	100%	Thu 29/4/21	Wed 26/5/21	Thu 29/4/21	Wed 26/5/...	0 days	0 days	4FS+1 day	194												
194	PS-10520	Submission and Approval	35 days	0 days	100%	Thu 27/5/21	Wed 30/6/21	Thu 27/5/21	Wed 30/6/...	0 days	0 days	193													
195	PS-10600	Specialist for Decontamination Works	63 days	0 days	100%	Thu 29/4/21	Wed 30/6/21	Thu 29/4/21	Wed 30/6/...	0 days	0 days														
196	PS-10610	Subletting	28 days	0 days	100%	Thu 29/4/21	Wed 26/5/21	Thu 29/4/21	Wed 26/5/...	0 days	0 days	4FS+1 day	197												
197	PS-10620	Submission and Approval	35 days	0 days	100%	Thu 27/5/21	Wed 30/6/21	Thu 27/5/21	Wed 30/6/...	0 days	0 days	196													
198	PS-10700	BIM Service	63 days	0 days	100%	Thu 29/4/21	Wed 30/6/21	Thu 29/4/21	Wed 30/6/...	0 days	0 days														
199	PS-10710	Subletting	28 days	0 days	100%	Thu 29/4/21	Wed 26/5/21	Thu 29/4/21	Wed 26/5/...	0 days	0 days	4FS+1 day	200												
200	PS-10720	Submission and Approval	35 days	0 days	100%	Thu 27/5/21	Wed 30/6/21	Thu 27/5/21	Wed 30/6/...	0 days	0 days	199	111FF												
201	PS-10800	Rebar Supply	63 days	0 days	100%	Wed 7/7/21	Tue 7/9/21	Wed 7/7/21	Tue 7/9/21	0 days	0 days														
202	PS-10810	Subletting	28 days	0 days	100%	Wed 7/7/21	Tue 3/8/21	Wed 7/7/21	Tue 3/8/21	0 days	0 days	4FS+70 days	203												
203	PS-10820	Submission and Approval	35 days	0 days	100%	Wed 4/8/21	Tue 7/9/21	Wed 4/8/21	Tue 7/9/21	0 days	0 days	202													
204	PS-10900	Concrete Supply	63 days	0 days	100%	Wed 7/7/21	Tue 7/9/21	Wed 7/7/21	Tue 7/9/21	0 days	0 days														
205	PS-10910	Subletting	28 days	0 days	100%	Wed 7/7/21	Tue 3/8/21	Wed 7/7/21	Tue 3/8/21	0 days	0 days	4FS+70 days	206												
206	PS-10920	Submission and Approval	35 days	0 days	100%	Wed 4/8/21	Tue 7/9/21	Wed 4/8/21	Tue 7/9/21	0 days	0 days	205													
207	PS-11000	Bitumen Supply and Paving	63 days	0 days	100%	Wed 7/7/21	Tue 7/9/21	Wed 7/7/21	Tue 7/9/21	0 days	0 days														
208	PS-11010	Subletting	28 days	0 days	100%	Wed 7/7/21	Tue 3/8/21	Wed 7/7/21	Tue 3/8/21	0 days	0 days	4FS+70 days	209												
209	PS-11020	Submission and Approval	35 days	0 days	100%	Wed 4/8/21	Tue 7/9/21	Wed 4/8/21	Tue 7/9/21	0 days	0 days	208													
210	PS-11100	Ground Investigation Works	63 days	0 days	100%	Wed 7/7/21	Tue 7/9/21	Wed 7/7/21	Tue 7/9/21	0 days	0 days														
211	PS-11110	Subletting	28 days	0 days	100%	Wed 7/7/21	Tue 3/8/21	Wed 7/7/21	Tue 3/8/21	0 days	0 days	4FS+70 days	212												
212	PS-11120	Submission and Approval	35 days	0 days	100%	Wed 4/8/21	Tue 7/9/21	Wed 4/8/21	Tue 7/9/21	0 days	0 days	211													
213	PS-11200	Demolition Works	63 days	0 days	100%	Wed 7/7/21	Tue 7/9/21	Wed 7/7/21	Tue 7/9/21	0 days	0 days														
214	PS-11210	Subletting	28 days	0 days	100%	Wed 7/7/21	Tue 3/8/21	Wed 7/7/21	Tue 3/8/21	0 days	0 days	4FS+70 days	215												
215	PS-11220	Submission and Approval	35 days	0 days	100%	Wed 4/8/21	Tue 7/9/21	Wed 4/8/21	Tue 7/9/21	0 days	0 days	214													
216	PS-11300	Pipe Jacking Works	63 days	0 days	100%	Thu 29/4/21	Wed 30/6/21	Thu 29/4/21	Wed 30/6/...	0 days	0 days														
217	PS-11310	Subletting	28 days	0 days	100%	Thu 29/4/21	Wed 26/5/21	Thu 29/4/21	Wed 26/5/...	0 days	0 days	4FS+1 day	218												
218	PS-11320	Submission and Approval	35 days	0 days	100%	Thu 27/5/21	Wed 30/6/21	Thu 27/5/21	Wed 30/6/...	0 days	0 days	217	327												
219	PS-11400	Road Marking	63 days	0 days	100%	Fri 9/12/22	Thu 9/2/23	Fri 9/12/22	Thu 9/2/23	0 days	0 days														
220	PS-11410	Subletting	28 days	0 days	100%	Fri 9/12/22	Thu 5/1/23	Fri 9/12/22	Thu 5/1/23	0 days	0 days	52FS+70 days	221												
221	PS-11420	Submission and Approval	35 days	0 days	100%	Fri 6/1/23	Thu 9/2/23	Fri 6/1/23	Thu 9/2/23	0 days	0 days	220	1007,1062												
222	PS-11500	Road Lighting System	63 days	0 days	100%	Fri 9/12/22	Thu 9/2/23	Fri 9/12/22	Thu 9/2/23	0 days	0 days														
223	PS-11510	Subletting	28 days	0 days	100%	Fri 9/12/22	Thu 5/1/23	Fri 9/12/22	Thu 5/1/23	0 days	0 days	52FS+70 days	224												
224	PS-11520	Submission and Approval	35 days	0 days	100%	Fri 6/1/23	Thu 9/2/23	Fri 6/1/23	Thu 9/2/23	0 days	0 days	223	264,249												
225	PS-11600	Landscaping Works	63 days	0 days	100%	Fri 9/12/22	Thu 9/2/23	Fri 9/12/22	Thu 9/2/23	0 days	0 days														
226	PS-11610	Subletting	28 days	0 days	100%	Fri 9/12/22	Thu 5/1/23	Fri 9/12/22	Thu 5/1/23	0 days	0 days	4FS+70 days	227												
227	PS-11620	Submission and Approval	35 days	0 days	100%	Fri 6/1/23	Thu 9/2/23	Fri 6/1/23	Thu 9/2/23	0 days	0 days	226	461FS+830 days												
228	PS-11700	E&M Works	63 days	0 days	100%	Fri 9/12/22	Thu 9/2/23	Fri 9/12/22	Thu 9/2/23	0 days	0 days														
229	PS-11710	Subletting	28 days	0 days	100%	Fri 9/12/22	Thu 5/1/23	Fri 9/12/22	Thu 5/1/23	0 days	0 days	52FS+70 days	230												


Task Critical Task Milestone Summary

*E-Excavator, L-Lorry, W-Worker, D-Drill plant, C-Crane Lorry, R-Rotter

ID	Activity ID	Task Name	Duration	Remaining Duration	% Work Complete	Start	Finish	Late Start	Late Finish	Free Slack	Total Slack	Predecessors	Successors	2021	Half 2, 2021	Half 1, 2022	Half 2, 2022	Half 1, 2023	Half 2, 2023	Half 1, 2024	Half 2, 2024	Half 1, 2025	Half 2, 2025	Half 1, 2026	Half 2, 2026
283	DM-20141	Traffic Diversion for Kai Pak Ling Road and L53 Construction	12 days	0 days	100%	Tue 18/4/23	Sat 29/4/23	Tue 18/4/23	Sat 29/4/23	0 days	0 days	157	475,480												
284	DM-20200	Decontamination Works	351 days	0 days	100%	Thu 3/3/22	Thu 16/2/23	Thu 3/3/22	Thu 16/2/...	0 days	0 days														
285	DM-20210	Contamination Assessment Plan	283 days	0 days	100%	Thu 3/3/22	Sat 10/12/22	Thu 3/3/22	Sat 10/12/...	0 days	0 days														
286	DM-20211	Batch 1 (Site 3-6, Site 3-7, Road D1 adjacent to site 3-6 and site 3-7, Detention Pond)	44 days	0 days	100%	Fri 28/10/22	Sat 10/12/22	Fri 28/10/22	Sat 10/12/22	0 days	0 days														
287	DM-202111	Site Appraisal and Preparation of Plan	14 days	0 days	100%	Fri 28/10/22	Thu 10/11/22	Fri 28/10/22	Thu 10/1/...	0 days	0 days	564SS	288												
288	DM-202112	Submission and Endorsement by EPD	30 days	0 days	100%	Fri 11/11/22	Sat 10/12/22	Fri 11/11/22	Sat 10/12/...	0 days	0 days	287	652FF												
289	DM-20212	Batch 2 (Site 3-8, Road L51, Road D1 at adjacent to Site 3-8)	55 days	0 days	100%	Thu 3/3/22	Tue 26/4/22	Thu 3/3/22	Tue 26/4/22	0 days	0 days														
290	DM-202121	Site Appraisal and Preparation of Plan	25 days	0 days	100%	Thu 3/3/22	Sun 27/3/22	Thu 3/3/22	Sun 27/3/...	0 days	0 days	746SS	291												
291	DM-202122	Submission and Endorsement by EPD	30 days	0 days	100%	Mon 28/3/22	Tue 26/4/22	Mon 28/3/22	Tue 26/4/...	0 days	0 days	290	747FF												
292	DM-20213	Batch 3 (Site 2-18, Site 2-19, Road L54)	55 days	0 days	100%	Fri 29/4/22	Wed 22/6/22	Fri 29/4/22	Wed 22/6/...	0 days	0 days														
293	DM-202131	Site Appraisal and Preparation of Plan	25 days	0 days	100%	Fri 29/4/22	Mon 23/5/22	Fri 29/4/22	Mon 23/5/...	0 days	0 days	846SS	294												
294	DM-202132	Submission and Endorsement by EPD	30 days	0 days	100%	Tue 24/5/22	Wed 22/6/22	Tue 24/5/22	Wed 22/6/...	0 days	0 days	293	847FF,926FF												
295	DM-20220	Cement Solidification System	48 days	0 days	100%	Sat 31/12/22	Thu 16/2/23	Sat 31/12/...	Thu 16/2/...	0 days	0 days														
296	DM-20221	Prepare and Submit Design	24 days	0 days	100%	Sat 31/12/22	Mon 23/1/23	Sat 31/12/...	Mon 23/1/...	0 days	0 days	750,567,849	297												
297	DM-20222	ICE Certification, Approval and Consent	24 days	0 days	100%	Tue 24/1/23	Thu 16/2/23	Tue 24/1/23	Thu 16/2/...	0 days	0 days	296	432FS-24 days												
298	DM-20230	Biopile System	48 days	0 days	100%	Sat 31/12/22	Thu 16/2/23	Sat 31/12/...	Thu 16/2/...	0 days	0 days														
299	DM-20231	Prepare and Submit Design	24 days	0 days	100%	Sat 31/12/22	Mon 23/1/23	Sat 31/12/...	Mon 23/1/...	0 days	0 days	750,567,849	300												
300	DM-20232	ICE Certification, Approval and Consent	24 days	0 days	100%	Tue 24/1/23	Thu 16/2/23	Tue 24/1/23	Thu 16/2/...	0 days	0 days	299	435FS-24 days												
301	DM-20300	Demolition Works	84 days	0 days	100%	Sat 29/1/22	Fri 22/4/22	Sat 29/1/22	Fri 22/4/22	0 days	0 days														
302	DM-20310	Demolition of RC Structures less than 2-storey	48 days	0 days	100%	Sat 29/1/22	Thu 17/3/22	Sat 29/1/22	Thu 17/3/...	0 days	0 days														
303	DM-20311	Prepare and Submit Design	24 days	0 days	100%	Sat 29/1/22	Mon 21/2/22	Sat 29/1/22	Mon 21/2/...	0 days	0 days	38SS+1 day,39SS+1 c	304,306												
304	DM-20312	ICE Certification, Approval and Consent	24 days	0 days	100%	Tue 22/2/22	Thu 17/3/22	Tue 22/2/22	Thu 17/3/...	0 days	0 days	303	396												
305	DM-20320	Demolition of Steel Frame Structures	60 days	0 days	100%	Tue 22/2/22	Fri 22/4/22	Tue 22/2/22	Fri 22/4/22	0 days	0 days														
306	DM-20321	Prepare and Submit Design	36 days	0 days	100%	Tue 22/2/22	Tue 29/3/22	Tue 22/2/22	Tue 29/3/...	0 days	0 days	303	307												
307	DM-20322	ICE Certification, Approval and Consent	24 days	0 days	100%	Wed 30/3/22	Fri 22/4/22	Wed 30/3/...	Fri 22/4/22	0 days	0 days	306	399												
308	DM-20400	Drainage, Sewerage and Water Works	60 days	0 days	100%	Thu 29/4/21	Sun 27/6/21	Thu 29/4/21	Sun 27/6/...	0 days	0 days														
309	DM-20410	ELS Design (By Shoring Method)	36 days	0 days	100%	Thu 29/4/21	Thu 3/6/21	Thu 29/4/21	Thu 3/6/21	0 days	0 days														
310	DM-20411	Prepare and Submit Design	12 days	0 days	100%	Thu 29/4/21	Mon 10/5/21	Thu 29/4/21	Mon 10/5/...	0 days	0 days	46FS+1 day	311,313												
311	DM-20412	ICE Certification, Approval and Consent	24 days	0 days	100%	Tue 11/5/21	Thu 3/6/21	Tue 11/5/21	Thu 3/6/21	0 days	0 days	310	403,406,409												
312	DM-20420	Temporary Utility Support	36 days	0 days	100%	Tue 11/5/21	Tue 15/6/21	Tue 11/5/21	Tue 15/6/...	0 days	0 days														
313	DM-20421	Prepare and Submit Design	12 days	0 days	100%	Tue 11/5/21	Sat 22/5/21	Tue 11/5/21	Sat 22/5/21	0 days	0 days	310	314,316												
314	DM-20422	ICE Certification, Approval and Consent	24 days	0 days	100%	Sun 23/5/21	Tue 15/6/21	Sun 23/5/21	Tue 15/6/...	0 days	0 days	313	403,406,409												
315	DM-20430	Formwork Design for Manhole Construction	36 days	0 days	100%	Sun 23/5/21	Sun 27/6/21	Sun 23/5/21	Sun 27/6/...	0 days	0 days														
316	DM-20431	Prepare and Submit Design	12 days	0 days	100%	Sun 23/5/21	Thu 3/6/21	Sun 23/5/21	Thu 3/6/21	0 days	0 days	313	317												
317	DM-20432	ICE Certification, Approval and Consent	24 days	0 days	100%	Fri 4/6/21	Sun 27/6/21	Fri 4/6/21	Sun 27/6/...	0 days	0 days	316	406,409												
318	DM-20500	Geotechnical Works	48 days	0 days	100%	Sat 21/10/22	Thu 7/12/23	Sat 21/10/...	Thu 7/12/...	0 days	0 days														
319	DM-20510	Working Platform	36 days	0 days	100%	Sat 21/10/22	Sat 25/11/22	Sat 21/10/...	Sat 25/11/...	0 days	0 days														
320	DM-20511	Prepare and Submit Design	12 days	0 days	100%	Sat 21/10/22	Wed 1/11/22	Sat 21/10/...	Wed 1/11/...	0 days	0 days	254	321,323												
321	DM-20512	ICE Certification, Approval and Consent	24 days	0 days	100%	Thu 2/11/23	Sat 25/11/22	Thu 2/11/23	Sat 25/11/...	0 days	0 days	320	422												
322	DM-20520	Formwork Design for RC Structures	36 days	0 days	100%	Thu 2/11/23	Thu 7/12/23	Thu 2/11/23	Thu 7/12/...	0 days	0 days														
323	DM-20521	Prepare and Submit Design	12 days	0 days	100%	Thu 2/11/23	Mon 13/11/22	Thu 2/11/23	Mon 13/1/...	0 days	0 days	320	324												
324	DM-20522	ICE Certification, Approval and Consent	24 days	0 days	100%	Tue 14/11/22	Thu 7/12/23	Tue 14/11/...	Thu 7/12/...	0 days	0 days	323	422												
325	DM-20600	Pipe Jacking	60 days	0 days	100%	Sat 14/8/21	Tue 12/10/22	Sat 14/8/21	Tue 12/1/...	0 days	0 days														
326	DM-20610	ELS Design (By Shoring Method)	60 days	0 days	100%	Sat 14/8/21	Tue 12/10/22	Sat 14/8/21	Tue 12/1/...	0 days	0 days														
327	DM-20611	Prepare and Submit Design	30 days	0 days	100%	Sat 14/8/21	Sun 12/9/21	Sat 14/8/21	Sun 12/9/...	0 days	0 days	151,218	328												
328	DM-20612	ICE Certification, Approval and Consent	30 days	0 days	100%	Mon 13/9/21	Tue 12/10/22	Mon 13/9/21	Tue 12/1/...	0 days	0 days	327	454												
329	DM-20700	Retaining Wall	158 days	0 days	100%	Wed 28/4/21	Sat 2/10/21	Wed 28/4/...	Sat 2/10/21	0 days	0 days														
330	DM-20710	Formwork Design for Lagging Wall Construction (Soldier Pile Wall)	36 days	0 days	100%	Wed 28/4/21	Wed 2/6/21	Wed 28/4/21	Wed 2/6/21	0 days	0 days														
331	DM-20711	Prepare and Submit Design	12 days	0 days	100%	Wed 28/4/21	Sun 9/5/21	Wed 28/4/...	Sun 9/5/21	0 days	0 days		332,334												
332	DM-20712	ICE Certification, Approval and Consent	24 days	0 days	100%	Mon 10/5/21	Wed 2/6/21	Mon 10/5/21	Wed 2/6/21	0 days	0 days	331	413												

ID	Activity ID	Task Name	Duration	Remaining Duration	% Work Complete	Start	Finish	Late Start	Late Finish	Free Slack	Total Slack	Predecessors	Successors	2021	Half 2, 2021	Half 1, 2022	Half 2, 2022	Half 1, 2023	Half 2, 2023	Half 1, 2024	Half 2, 2024	Half 1, 2025	Half 2, 2025	Half 1, 2026	Half 2, 2026
333	DM-20720	Formwork Design for Lagging Wall Construction (Bored Pile Wall)	36 days	0 days	100%	Mon 10/5/21	Mon 14/6/21	Mon 10/5/21	Mon 14/6/21	0 days	0 days														
334	DM-20721	Prepare and Submit Design	12 days	0 days	100%	Mon 10/5/21	Fri 21/5/21	Mon 10/5/21	Fri 21/5/21	0 days	0 days	331	335,337												
335	DM-20722	ICE Certification, Approval and Consent	24 days	0 days	100%	Sat 22/5/21	Mon 14/6/21	Sat 22/5/21	Mon 14/6/21	0 days	0 days	334	416												
336	DM-20730	Formwork Design for RC Capping Beam Construction	36 days	0 days	100%	Sat 22/5/21	Sat 26/6/21	Sat 22/5/21	Sat 26/6/21	0 days	0 days														
337	DM-20731	Prepare and Submit Design	12 days	0 days	100%	Sat 22/5/21	Wed 2/6/21	Sat 22/5/21	Wed 2/6/21	0 days	0 days	334	338												
338	DM-20732	ICE Certification, Approval and Consent	24 days	0 days	100%	Thu 3/6/21	Sat 26/6/21	Thu 3/6/21	Sat 26/6/21	0 days	0 days	337	413,416												
339	DM-20740	Formwork Design for RC Retaining Wall Constr	36 days	0 days	100%	Sat 28/8/21	Sat 2/10/21	Sat 28/8/21	Sat 2/10/21	0 days	0 days														
340	DM-20741	Prepare and Submit Design	12 days	0 days	100%	Sat 28/8/21	Wed 8/9/21	Sat 28/8/21	Wed 8/9/21	0 days	0 days	34	341												
341	DM-20742	ICE Certification, Approval and Consent	24 days	0 days	100%	Thu 9/9/21	Sat 2/10/21	Thu 9/9/21	Sat 2/10/21	0 days	0 days	340	419												
342	DM-20800	Detention Pond	36 days	0 days	100%	Sat 29/1/22	Sat 5/3/22	Sat 29/1/22	Sat 5/3/22	0 days	0 days														
343	DM-20810	Formwork Design for RC Structure Constructio	36 days	0 days	100%	Sat 29/1/22	Sat 5/3/22	Sat 29/1/22	Sat 5/3/22	0 days	0 days														
344	DM-20011	Prepare and Submit Design	12 days	0 days	100%	Sat 29/1/22	Wed 9/2/22	Sat 29/1/22	Wed 9/2/22	0 days	0 days	39FS+1 day	345												
345	DM-20812	ICE Certification, Approval and Consent	24 days	0 days	100%	Thu 10/2/22	Sat 5/3/22	Thu 10/2/22	Sat 5/3/22	0 days	0 days	344	444												
346	DM-20900	RC Box Culvert	150 days	0 days	100%	Sat 29/1/22	Mon 27/6/22	Sat 29/1/22	Mon 27/6/22	0 days	0 days		887												
347	DM-20910	Temp Works for Drainage Diversion	150 days	0 days	100%	Sat 29/1/22	Mon 27/6/22	Sat 29/1/22	Mon 27/6/22	0 days	0 days														
348	DM-20911	Prepare and Submit Design	30 days	0 days	100%	Sat 29/1/22	Sun 27/2/22	Sat 29/1/22	Sun 27/2/22	0 days	0 days	40FS+1 day	349,351,448SS												
349	DM-20912	ICE Certification, Approval and Consent (By DSE)	120 days	0 days	100%	Mon 28/2/22	Mon 27/6/22	Mon 28/2/22	Mon 27/6/22	0 days	0 days	348,161FF	449FF												
350	DM-20920	Temp Excavation for Box Culvert Construction (Open Cut with Concrete Block Wall)	50 days	0 days	100%	Mon 28/2/22	Mon 18/4/22	Mon 28/2/22	Mon 18/4/22	0 days	0 days														
351	DM-20921	Prepare and Submit Design	25 days	0 days	100%	Mon 28/2/22	Thu 24/3/22	Mon 28/2/22	Thu 24/3/22	0 days	0 days	348	352,354												
352	DM-20922	ICE Certification, Approval and Consent	25 days	0 days	100%	Fri 25/3/22	Mon 18/4/22	Fri 25/3/22	Mon 18/4/22	0 days	0 days	351	451												
353	DM-20930	Formwork and Falsework Design for RC Structures	50 days	0 days	100%	Fri 25/3/22	Fri 13/5/22	Fri 25/3/22	Fri 13/5/22	0 days	0 days														
354	DM-20931	Prepare and Submit Design	25 days	0 days	100%	Fri 25/3/22	Mon 18/4/22	Fri 25/3/22	Mon 18/4/22	0 days	0 days	351	355												
355	DM-20932	ICE Certification, Approval and Consent	25 days	0 days	100%	Tue 19/4/22	Fri 13/5/22	Tue 19/4/22	Fri 13/5/22	0 days	0 days	354	451												
356	DM-21000	Transformer Room	50 days	0 days	100%	Fri 29/10/21	Fri 17/12/21	Fri 29/10/21	Fri 17/12/21	0 days	0 days														
357	DM-21010	Formwork and Falsework Design for RC Structures	50 days	0 days	100%	Fri 29/10/21	Fri 17/12/21	Fri 29/10/21	Fri 17/12/21	0 days	0 days														
358	DM-21011	Prepare and Submit Design	25 days	0 days	100%	Fri 29/10/21	Mon 22/11/21	Fri 29/10/21	Mon 22/11/21	0 days	0 days	262	359												
359	DM-21012	ICE Certification, Approval and Consent	25 days	0 days	100%	Tue 23/11/21	Fri 17/12/21	Tue 23/11/21	Fri 17/12/21	0 days	0 days	358	441												
360	DM-21100	Sewage Pumping Station	75 days	0 days	100%	Mon 18/9/21	Fri 1/12/23	Mon 18/9/21	Fri 1/12/23	0 days	0 days														
361	DM-21110	ELS Design (By Shoring Method)	50 days	0 days	100%	Mon 18/9/21	Mon 6/11/21	Mon 18/9/21	Mon 6/11/21	0 days	0 days														
362	DM-21111	Prepare and Submit Design	25 days	0 days	100%	Mon 18/9/21	Thu 12/10/21	Mon 18/9/21	Thu 12/10/21	0 days	0 days	258	363,365												
363	DM-21112	ICE Certification, Approval and Consent	25 days	0 days	100%	Fri 13/10/23	Mon 6/11/23	Fri 13/10/23	Mon 6/11/23	0 days	0 days	362	366,247												
364	DM-21120	Formwork and Falsework Design for RC Structures	50 days	0 days	100%	Fri 13/10/23	Fri 1/12/23	Fri 13/10/23	Fri 1/12/23	0 days	0 days														
365	DM-21121	Prepare and Submit Design	25 days	0 days	100%	Fri 13/10/23	Mon 6/11/23	Fri 13/10/23	Mon 6/11/23	0 days	0 days	362	366												
366	DM-21122	ICE Certification, Approval and Consent	25 days	0 days	100%	Tue 7/11/23	Fri 1/12/23	Tue 7/11/23	Fri 1/12/23	0 days	0 days	365,363	438,1124												
367	DM-30000	Method Statement and Risk Assessment	1529 days	54.4 days	0%	Tue 20/4/21	Thu 26/6/25	Tue 20/4/21	Thu 31/7/21	35 days	35 days														
368	DM-30100	Site Establishment	150 days	0 days	100%	Tue 20/4/21	Thu 16/9/21	Tue 20/4/21	Thu 16/9/21	0 days	0 days														
369	DM-30110	General Site Clearance	9 days	0 days	100%	Tue 20/4/21	Wed 28/4/21	Tue 20/4/21	Wed 28/4/21	0 days	0 days														
370	DM-30111	Prepare and Submit Method Statement/Risk Assessment	2 days	0 days	100%	Tue 20/4/21	Wed 21/4/21	Tue 20/4/21	Wed 21/4/21	0 days	0 days	2FS+1 day	371												
371	DM-30112	Approval and Consent	7 days	0 days	100%	Thu 22/4/21	Wed 28/4/21	Thu 22/4/21	Wed 28/4/21	0 days	0 days	370	491												
372	DM-30120	Hoarding Construction	38 days	0 days	100%	Sat 22/5/21	Mon 28/6/21	Sat 22/5/21	Mon 28/6/21	0 days	0 days														
373	DM-30121	Prepare and Submit Method Statement/Risk Assessment	24 days	0 days	100%	Sat 22/5/21	Mon 14/6/21	Sat 22/5/21	Mon 14/6/21	0 days	0 days	278	374												
374	DM-30122	Approval and Consent	14 days	0 days	100%	Tue 15/6/21	Mon 28/6/21	Tue 15/6/21	Mon 28/6/21	0 days	0 days	373													
375	DM-30130	Construction of PM's Accommodation (MIC)	38 days	0 days	100%	Tue 10/8/21	Thu 16/9/21	Tue 10/8/21	Thu 16/9/21	0 days	0 days														
376	DM-30131	Prepare and Submit Method Statement/Risk Assessment	24 days	0 days	100%	Tue 10/8/21	Thu 2/9/21	Tue 10/8/21	Thu 2/9/21	0 days	0 days	275	377												
377	DM-30132	Approval and Consent	14 days	0 days	100%	Fri 3/9/21	Thu 16/9/21	Fri 3/9/21	Thu 16/9/21	0 days	0 days	376	503												
378	DM-30140	Utilities Detection and Trial Pit Excavation	21 days	0 days	100%	Wed 9/6/21	Tue 29/6/21	Wed 9/6/21	Tue 29/6/21	0 days	0 days														
379	DM-30141	Prepare and Submit Method Statement/Risk Assessment	7 days	0 days	100%	Wed 9/6/21	Tue 15/6/21	Wed 9/6/21	Tue 15/6/21	0 days	0 days	281	380												
380	DM-30142	Approval and Consent	14 days	0 days	100%	Wed 16/6/21	Tue 29/6/21	Wed 16/6/21	Tue 29/6/21	0 days	0 days	379													
381	DM-30150	Project Signboard Construction	38 days	0 days	100%	Sat 22/5/21	Mon 28/6/21	Sat 22/5/21	Mon 28/6/21	0 days	0 days														
382	DM-30151	Prepare and Submit Method Statement/Risk Assessment	24 days	0 days	100%	Sat 22/5/21	Mon 14/6/21	Sat 22/5/21	Mon 14/6/21	0 days	0 days	278	383												
383	DM-30152	Approval and Consent	14 days	0 days	100%	Tue 15/6/21	Mon 28/6/21	Tue 15/6/21	Mon 28/6/21	0 days	0 days	382	500												
384	DM-30200	Tree Treatment	42 days	0 days	100%	Tue 20/4/21	Mon 31/5/21	Tue 20/4/21	Mon 31/5/21	0 days	0 days														

ID	Activity ID	Task Name	Duration	Remaining Duration	% Work Complete	Start	Finish	Late Start	Late Finish	Free Slack	Total Slack	Predecessors	Successors	2021	Half 2, 2021	Half 1, 2022	Half 2, 2022	Half 1, 2023	Half 2, 2023	Half 1, 2024	Half 2, 2024	Half 1, 2025	Half 2, 2025	Half 1, 2026	Half 2, 2026
385	DM-30210	Tree Felling and Protection	28 days	0 days	100%	Tue 20/4/21	Mon 17/5/21	Tue 20/4/21	Mon 17/5/...	0 days	0 days														
386	DM-30211	Prepare and Submit Method Statement/Risk Ass	14 days	0 days	100%	Tue 20/4/21	Mon 3/5/21	Tue 20/4/21	Mon 3/5/21	0 days	0 days	2FS+1 day	387, 389												
387	DM-30212	Approval and Consent	14 days	0 days	100%	Tue 4/5/21	Mon 17/5/21	Tue 4/5/21	Mon 17/5/...	0 days	0 days	386	553												
388	DM-30220	Tree Transplanting	28 days	0 days	100%	Tue 4/5/21	Mon 31/5/21	Tue 4/5/21	Mon 31/5/...	0 days	0 days														
389	DM-30221	Prepare and Submit Method Statement/Risk Ass	14 days	0 days	100%	Tue 4/5/21	Mon 17/5/21	Tue 4/5/21	Mon 17/5/...	0 days	0 days	386	390												
390	DM-30222	Approval and Consent	14 days	0 days	100%	Tue 18/5/21	Mon 31/5/21	Tue 18/5/21	Mon 31/5/...	0 days	0 days	389	556												
391	DM-30300	Ground Investigation (Environmental Borehole, Trial Pit and GI Borehole)	38 days	0 days	100%	Wed 19/1/22	Fri 25/2/22	Wed 19/1/22	Fri 25/2/22	0 days	0 days														
392	DM-30310	Prepare and Submit Method Statement/Risk Asses	24 days	0 days	100%	Wed 19/1/22	Fri 11/2/22	Wed 19/1/...	Fri 11/2/22	0 days	0 days	31FS+1 day	393												
393	DM-30320	Approval and Consent	14 days	0 days	100%	Sat 12/2/22	Fri 25/2/22	Sat 12/2/22	Fri 25/2/22	0 days	0 days	392	750,849,928,654												
394	DM-30400	Demolition Works	74 days	0 days	100%	Fri 18/3/22	Mon 30/5/22	Fri 18/3/22	Mon 30/5/...	0 days	0 days														
395	DM-30410	Demolition of RC Structures less than 2-storey	28 days	0 days	100%	Fri 18/3/22	Thu 14/4/22	Fri 18/3/22	Thu 14/4/...	0 days	0 days														
396	DM-30411	Prepare and Submit Method Statement/Risk Ass	14 days	0 days	100%	Fri 18/3/22	Thu 31/3/22	Fri 18/3/22	Thu 31/3/...	0 days	0 days	304	397, 399												
397	DM-30412	Approval and Consent	14 days	0 days	100%	Fri 1/4/22	Thu 14/4/22	Fri 1/4/22	Thu 14/4/...	0 days	0 days	396	559,560,647,646,843,922												
398	DM-30420	Demolition of Steel Frame Structures	38 days	0 days	100%	Sat 23/4/22	Mon 30/5/22	Sat 23/4/22	Mon 30/5/...	0 days	0 days														
399	DM-30421	Prepare and Submit Method Statement/Risk Ass	24 days	0 days	100%	Sat 23/4/22	Mon 16/5/22	Sat 23/4/22	Mon 16/5/...	0 days	0 days	396,307	400												
400	DM-30422	Approval and Consent	14 days	0 days	100%	Tue 17/5/22	Mon 30/5/22	Tue 17/5/22	Mon 30/5/...	0 days	0 days	399	559,560,647,646,843,922												
401	DM-30500	Drainage, Sewerage and Waterworks	56 days	0 days	100%	Tue 16/6/21	Tue 10/8/21	Wed 16/6/...	Tue 10/8/...	0 days	0 days														
402	DM-30510	Waterworks and Associated Reinstatement Wo	28 days	0 days	100%	Wed 16/6/21	Tue 13/7/21	Wed 16/6/...	Tue 13/7/...	0 days	0 days														
403	DM-30511	Prepare and Submit Method Statement/Risk Ass	14 days	0 days	100%	Wed 16/6/21	Tue 29/6/21	Wed 16/6/...	Tue 29/6/...	0 days	0 days	311,314	404,406												
404	DM-30512	Approval and Consent	14 days	0 days	100%	Wed 30/6/21	Tue 13/7/21	Wed 30/6/...	Tue 13/7/...	0 days	0 days	403	997,1099,1108,1264,1236												
405	DM-30520	Drainage and Associated Roadworks	28 days	0 days	100%	Wed 30/6/21	Tue 27/7/21	Wed 30/6/...	Tue 27/7/...	0 days	0 days														
406	DM-30521	Prepare and Submit Method Statement/Risk Ass	14 days	0 days	100%	Wed 30/6/21	Tue 13/7/21	Wed 30/6/...	Tue 13/7/...	0 days	0 days	403,317,311,314	407,409												
407	DM-30522	Approval and Consent	14 days	0 days	100%	Wed 14/7/21	Tue 27/7/21	Wed 14/7/...	Tue 27/7/...	0 days	0 days	406	989,1314,1261,1234,1210												
408	DM-30530	Sewerage and Associated Reinstatement Work	28 days	0 days	100%	Wed 14/7/21	Tue 10/8/21	Wed 14/7/...	Tue 10/8/...	0 days	0 days														
409	DM-30531	Prepare and Submit Method Statement/Risk Ass	14 days	0 days	100%	Wed 14/7/21	Tue 27/7/21	Wed 14/7/...	Tue 27/7/...	0 days	0 days	406,317,311,314	410												
410	DM-30532	Approval and Consent	14 days	0 days	100%	Wed 28/7/21	Tue 10/8/21	Wed 28/7/...	Tue 10/8/...	0 days	0 days	409	991,1314,1261,1234,1210												
411	DM-30600	Construction of Retaining Wall	136 days	0 days	100%	Sun 27/6/21	Tue 9/11/21	Sun 27/6/21	Tue 9/11/...	0 days	0 days														
412	DM-30610	Soldier Pile Wall	38 days	0 days	100%	Sun 27/6/21	Tue 3/8/21	Sun 27/6/21	Tue 3/8/21	0 days	0 days														
413	DM-30611	Prepare and Submit Method Statement/Risk Ass	24 days	0 days	100%	Sun 27/6/21	Tue 20/7/21	Sun 27/6/21	Tue 20/7/...	0 days	0 days	332,338	414												
414	DM-30612	Approval and Consent	14 days	0 days	100%	Wed 21/7/21	Tue 3/8/21	Wed 21/7/...	Tue 3/8/21	0 days	0 days	413													
415	DM-30620	Bored Pile Wall	38 days	0 days	100%	Sun 27/6/21	Tue 3/8/21	Sun 27/6/21	Tue 3/8/21	0 days	0 days														
416	DM-30621	Prepare and Submit Method Statement/Risk Ass	24 days	0 days	100%	Sun 27/6/21	Tue 20/7/21	Sun 27/6/21	Tue 20/7/...	0 days	0 days	335,338	417												
417	DM-30622	Approval and Consent	14 days	0 days	100%	Wed 21/7/21	Tue 3/8/21	Wed 21/7/...	Tue 3/8/21	0 days	0 days	416													
418	DM-30630	RC Retaining Wall	38 days	0 days	100%	Sun 3/10/21	Tue 9/11/21	Sun 3/10/21	Tue 9/11/...	0 days	0 days														
419	DM-30631	Prepare and Submit Method Statement/Risk Ass	24 days	0 days	100%	Sun 3/10/21	Tue 26/10/21	Sun 3/10/21	Tue 26/1/...	0 days	0 days	341	420												
420	DM-30632	Approval and Consent	14 days	0 days	100%	Wed 27/10/21	Tue 9/11/21	Wed 27/1/...	Tue 9/11/...	0 days	0 days	419	944												
421	DM-30700	Geotechnical Works	39 days	0 days	100%	Thu 2/5/24	Sun 9/6/24	Thu 2/5/24	Sun 9/6/24	0 days	0 days														
422	DM-30710	Prepare and Submit Method Statement/Risk Asses	24 days	0 days	100%	Thu 2/5/24	Sat 25/5/24	Thu 2/5/24	Sat 25/5/24	0 days	0 days	324,321	423												
423	DM-30720	Approval and Consent	14 days	0 days	100%	Mon 27/5/24	Sun 9/6/24	Mon 27/5/24	Sun 9/6/24	0 days	0 days	422	1329FS+80 days												
424	DM-30800	Typical Roadworks Construction (Ducts, Pavement, Street furniture, Road Marking etc.)	38 days	0 days	100%	Wed 19/1/22	Fri 25/2/22	Wed 19/1/22	Fri 25/2/22	0 days	0 days														
425	DM-30810	Prepare and Submit Method Statement/Risk Asses	24 days	0 days	100%	Wed 19/1/22	Fri 11/2/22	Wed 19/1/...	Fri 11/2/22	0 days	0 days	31FS+1 day	426												
426	DM-30820	Approval and Consent	14 days	0 days	100%	Sat 12/2/22	Fri 25/2/22	Sat 12/2/22	Fri 25/2/22	0 days	0 days	425	1003,1316,1281,1282,122												
427	DM-30900	Site Formation Works (Earthwork and Surface Dr	38 days	0 days	100%	Wed 19/1/22	Fri 25/2/22	Wed 19/1/...	Fri 25/2/22	0 days	0 days														
428	DM-30910	Prepare and Submit Method Statement/Risk Asses	24 days	0 days	100%	Wed 19/1/22	Fri 11/2/22	Wed 19/1/...	Fri 11/2/22	0 days	0 days	31FS+1 day	429												
429	DM-30920	Approval and Consent	14 days	0 days	100%	Sat 12/2/22	Fri 25/2/22	Sat 12/2/22	Fri 25/2/22	0 days	0 days	428	574,672,775,780,867,935,6												
430	DM-31000	Decontamination Works	28 days	0 days	100%	Tue 24/1/23	Mon 20/2/23	Tue 24/1/23	Mon 20/2/...	0 days	0 days														
431	DM-31010	Cement Solidification Works	28 days	0 days	100%	Tue 24/1/23	Mon 20/2/23	Tue 24/1/23	Mon 20/2/...	0 days	0 days														
432	DM-31011	Prepare and Submit Method Statement/Risk Ass	14 days	0 days	100%	Tue 24/1/23	Mon 6/2/23	Tue 24/1/23	Mon 6/2/23	0 days	0 days	297FS-24 days	433												
433	DM-31012	Approval and Consent	14 days	0 days	100%	Tue 7/2/23	Mon 20/2/23	Tue 7/2/23	Mon 20/2/...	0 days	0 days	432													
434	DM-31020	Biopile Works	28 days	0 days	100%	Tue 24/1/23	Mon 20/2/23	Tue 24/1/23	Mon 20/2/...	0 days	0 days														
435	DM-31021	Prepare and Submit Method Statement/Risk Ass	14 days	0 days	100%	Tue 24/1/23	Mon 6/2/23	Tue 24/1/23	Mon 6/2/23	0 days	0 days	300FS-24 days	436												
436	DM-31022	Approval and Consent	14 days	0 days	100%	Tue 7/2/23	Mon 20/2/23	Tue 7/2/23	Mon 20/2/...	0 days	0 days	435													
437	DM-31100	Construction of Sewage Pumping Station	38 days	0 days	100%	Sat 2/12/23	Mon 8/1/24	Sat 2/12/23	Mon 8/1/24	0 days	0 days														

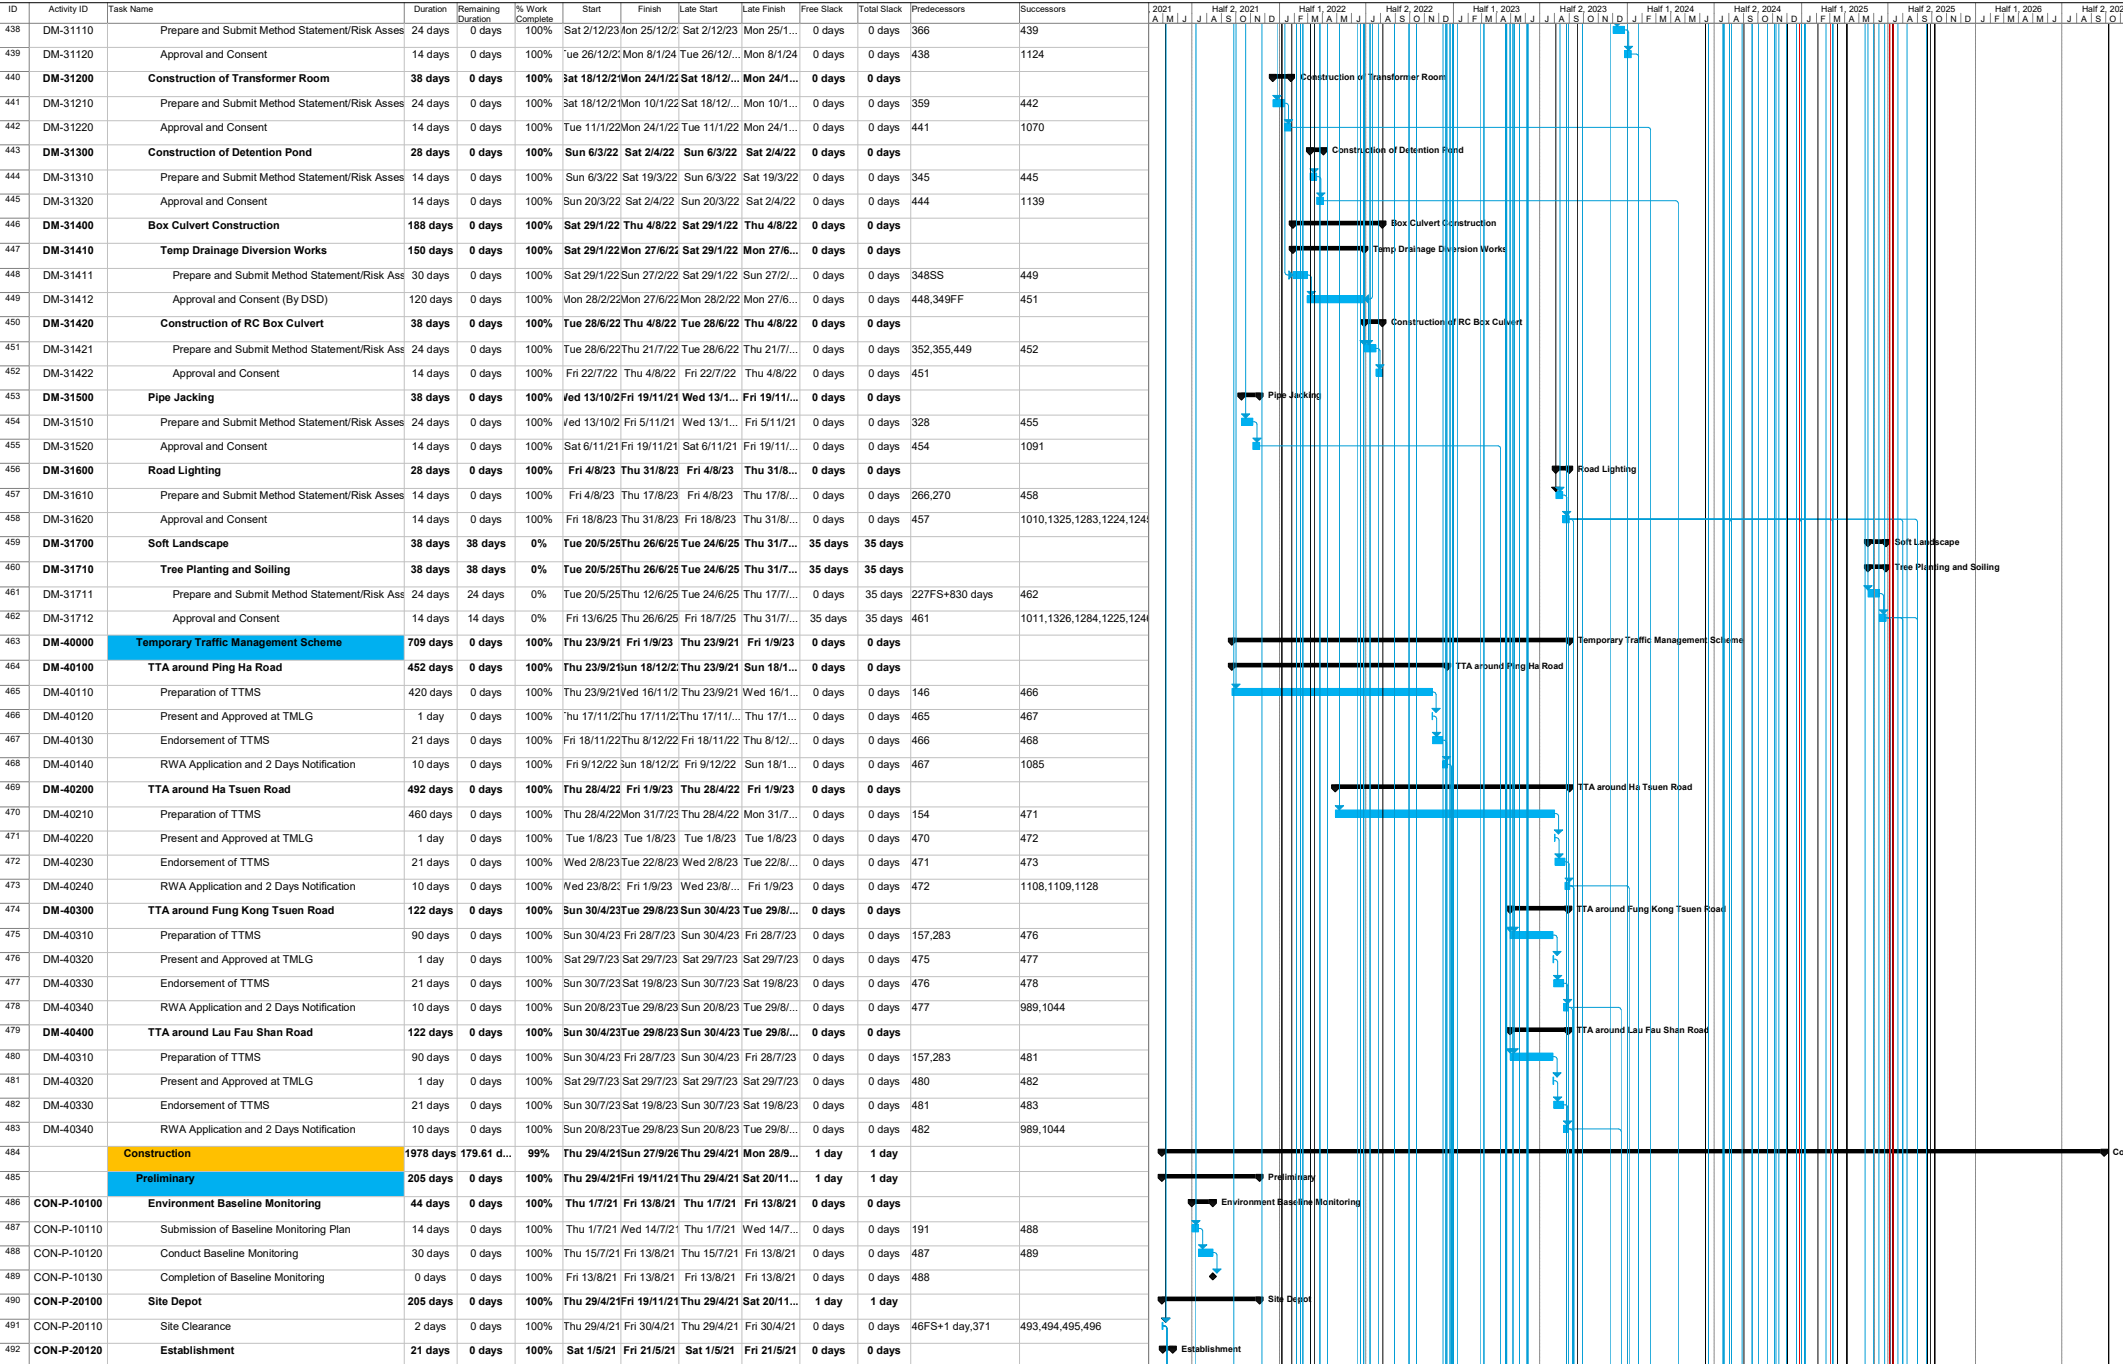

ID	Activity ID	Task Name	Duration	Remaining Duration	% Work Complete	Start	Finish	Late Start	Late Finish	Free Slack	Total Slack	Predecessors	Successors	2021	Half 2, 2021	Half 1, 2022	Half 2, 2022	Half 1, 2023	Half 2, 2023	Half 1, 2024	Half 2, 2024	Half 1, 2025	Half 2, 2025	Half 1, 2026	Half 2, 2026
493	CON-P-20121	Condition Survey	7 days	0 days	100%	Sat 1/5/21	Fri 7/5/21	Sat 1/5/21	Fri 7/5/21	0 days	0 days	491	498												
494	CON-P-20122	Tree Survey	7 days	0 days	100%	Sat 1/5/21	Fri 7/5/21	Sat 1/5/21	Fri 7/5/21	0 days	0 days	491	498												
495	CON-P-20123	Initial Survey	14 days	0 days	100%	Sat 1/5/21	Fri 14/5/21	Sat 1/5/21	Fri 14/5/21	0 days	0 days	491	498												
496	CON-P-20124	Health & Hygiene Facilities	7 days	0 days	100%	Sat 1/5/21	Fri 7/5/21	Sat 1/5/21	Fri 7/5/21	0 days	0 days	491	497												
497	CON-P-20125	Underground Utilities Detection	7 days	0 days	100%	Sat 8/5/21	Fri 14/5/21	Sat 8/5/21	Fri 14/5/21	0 days	0 days	496	498												
498	CON-P-20126	Setting up Temporary Office	7 days	0 days	100%	Sat 15/5/21	Fri 21/5/21	Sat 15/5/21	Fri 21/5/21	0 days	0 days	493,494,495,497	500												
499	CON-P-20130	Hoarding/Project Signboard	8 days	0 days	100%	Tue 29/6/21	Tue 6/7/21	Tue 29/6/21	Tue 6/7/21	0 days	0 days														
500	CON-P-20131	Construction of Concrete Strip	2 days	0 days	100%	Tue 29/6/21	Wed 30/6/21	Tue 29/6/21	Wed 30/6/21	0 days	0 days	383,498	501												
501	CON-P-20132	Erection of Project Signboard	6 days	0 days	100%	Thu 1/7/21	Tue 6/7/21	Thu 1/7/21	Tue 6/7/21	0 days	0 days	500	503,514												
502	CON-P-20140	Project Manager's Accommodation	54 days	0 days	100%	Mon 27/9/21	Fri 19/11/21	Mon 27/9/21	Fri 19/11/21	0 days	0 days														
503	CON-P-20141	Construction of Foundation	42 days	0 days	100%	Mon 27/9/21	Sun 7/11/21	Mon 27/9/21	Sun 7/11/21	0 days	0 days	233FF,377,501	504,510SS												
504	CON-P-20142	Delivery of MiC Modulars	3 days	0 days	100%	Mon 8/11/21	Wed 10/11/21	Mon 8/11/21	Wed 10/11/21	0 days	0 days	503	505FS-3 days												
505	CON-P-20143	Erection of MiC Modulars	4 days	0 days	100%	Mon 8/11/21	Thu 11/11/21	Mon 8/11/21	Thu 11/11/21	0 days	0 days	504FS-3 days	506												
506	CON-P-20144	Connection of Power and associated E&M works	4 days	0 days	100%	Fri 12/11/21	Mon 15/11/21	Fri 12/11/21	Mon 15/11/21	0 days	0 days	505	507												
507	CON-P-20145	Testing and Commissioning	2 days	0 days	100%	Tue 16/11/21	Wed 17/11/21	Tue 16/11/21	Wed 17/11/21	0 days	0 days	506	508												
508	CON-P-20146	Delivery of Office Furniture and Equipment	2 days	0 days	100%	Thu 18/11/21	Fri 19/11/21	Thu 18/11/21	Fri 19/11/21	0 days	0 days	507	514												
509	CON-P-20150	Contractor's Accommodation	17 days	0 days	100%	Mon 27/9/21	Wed 13/10/21	Mon 27/9/21	Wed 13/10/21	0 days	0 days														
510	CON-P-20151	Construction of Foundation	10 days	0 days	100%	Mon 27/9/21	Wed 6/10/21	Mon 27/9/21	Wed 6/10/21	0 days	0 days	503SS	511												
511	CON-P-20152	Delivery and Erection of Office Containers	3 days	0 days	100%	Thu 7/10/21	Sat 9/10/21	Thu 7/10/21	Sat 9/10/21	0 days	0 days	510	512												
512	CON-P-20153	Connection of Power Supply	2 days	0 days	100%	Sun 10/10/21	Mon 11/10/21	Sun 10/10/21	Mon 11/10/21	0 days	0 days	511	513												
513	CON-P-20154	Delivery of office Furniture and Equipment	2 days	0 days	100%	Tue 12/10/21	Wed 13/10/21	Tue 12/10/21	Wed 13/10/21	0 days	0 days	512	514												
514	CON-P-30000	Completion of Site Accommodation	0 days	0 days	100%	Fri 19/11/21	Fri 19/11/21	Sat 20/11/21	Sat 20/11/21	1 day	1 day	508,513,501													
515		Section 1A1	1195 days	0 days	100%	Sun 19/12/21	Thu 27/3/25	Sun 19/12/21	Thu 27/3/25	0 days	0 days														
516		Site 3-6 Additional Works affected by CIF Area	744 days	0 days	100%	Mon 30/1/22	Tue 11/2/25	Mon 30/1/22	Tue 11/2/25	0 days	0 days														
517	CON-3.6-CIF101	Mobilization of Plant and Labour Required (PMI 073)	14 days	0 days	100%	Mon 10/6/24	Sun 23/6/24	Mon 10/6/24	Sun 23/6/24	0 days	0 days	51	518,519												
518	CON-3.6-CIF102	Removal of MiC Modules (PMI 073)	26 days	0 days	100%	Mon 24/6/24	Fri 19/7/24	Mon 24/6/24	Fri 19/7/24	0 days	0 days	517	535,1209,1217												
519	CON-3.6-CIF110	Removal of Hoarding for CIF (PMI 073)	8 days	0 days	100%	Mon 24/6/24	Mon 1/7/24	Mon 24/6/24	Mon 1/7/24	0 days	0 days	517	524												
520	CON-3.6-CIF120	Transportation of Imported Fill Material from Site 3-6 UP to Site 3-6 LP for Future Backfilling works	120 days	0 days	100%	Mon 30/1/23	Mon 29/5/23	Mon 30/1/23	Mon 29/5/23	0 days	0 days	577	581,526												
521	CON-3.6-CIF130	Transportation of Excavated Material from Site 3-6 UP (south) to Completed Platform at Site 3-8 for Future Backfilling works	155 days	0 days	100%	Mon 30/1/23	Mon 30/7/23	Mon 30/1/23	Mon 30/7/23	0 days	0 days	577	581,526												
522	CON-3.6-CIF140	Transportation of Excavated Material from Site 3-6 UP (North) to Completed Platform at Site 3-6 UP(South) for Future Backfilling works	155 days	0 days	100%	Mon 30/1/23	Mon 30/7/23	Mon 30/1/23	Mon 30/7/23	0 days	0 days	577	581,526												
523	CON-3.6-CIF150	Transportation of Treated Heavy Metal contaminated soil from Detention pond to Site 3-6 for Future Backfilling works at Road D1	120 days	0 days	100%	Sat 28/10/23	Sat 24/2/24	Sat 28/10/23	Sat 24/2/24	0 days	0 days	1187SS	524												
524	CON-3.6-CIF160	Transportation of Treated Heavy Metal contaminated soil from Site 3-6 to Road D1 for Backfilling	37 days	0 days	100%	Fri 9/8/24	Sat 14/9/24	Fri 9/8/24	Sat 14/9/24	0 days	0 days	1217,1209,523,519	611,526												
525	CON-3.6-CIF170	Transport of Stockpile to other Location for Backfill	171 days	0 days	100%	Sun 25/8/24	Tue 11/2/25	Sun 25/8/24	Tue 11/2/25	0 days	0 days	581SS	611												
526	CON-3.6-CIF180	Transport of Stock Material to Site 3-7 for Backfilling	63 days	0 days	100%	Sun 15/9/24	Sat 16/11/24	Sun 15/9/24	Sat 16/11/24	0 days	0 days	680SS,520,521,522,5598													
527	CON-3.6-CIF200	Removal of Temporary Sewerage Pumping Station and Septic Tank (PMI 073)	20 days	0 days	100%	Mon 22/7/24	Sat 10/8/24	Mon 22/7/24	Sat 10/8/24	0 days	0 days	535	528												
528	CON-3.6-CIF210	Backfill & Compaction at Sewerage Pumping Station and Septic Tank +19.0mPD (PMI 073)	14 days	0 days	100%	Sun 11/8/24	Sat 24/8/24	Sun 11/8/24	Sat 24/8/24	0 days	0 days	527	581												
529	CON-3.6-CIF220	Removal of additional Pavement within HSKCIF (Portion A2,B1,B2,B3)	16 days	0 days	100%	Wed 24/7/24	Thu 8/8/24	Wed 24/7/24	Thu 8/8/24	0 days	0 days	550,535	530SS+7 days,578												
530	CON-3.6-CIF230	Removal of Sewer and Watermain (PMI 073)	15 days	0 days	100%	Wed 31/7/24	Wed 14/8/24	Wed 31/7/24	Wed 14/8/24	0 days	0 days	550,529SS+7 days	581												
531		Site 3-6 (Portion A2,B1,B2,B3)	1195 days	0 days	100%	Sun 19/12/21	Thu 27/3/25	Sun 19/12/21	Thu 27/3/25	0 days	0 days														
532	CON-3.6-10000	Site Clearance	916 days	0 days	100%	Tue 18/1/22	Sun 21/7/24	Tue 18/1/22	Sun 21/7/24	0 days	0 days														
533	CON-3.6-10100	Site Clearance for Portion A2	5 days	0 days	100%	Tue 18/1/22	Sat 22/1/22	Tue 18/1/22	Sat 22/1/22	0 days	0 days	31	537,539,541,543,545,546,548												
534	CON-3.6-10200	Site Clearance for Portion B1,B2	5 days	0 days	100%	Fri 28/1/22	Tue 1/2/22	Fri 28/1/22	Tue 1/2/22	0 days	0 days	38,39	538,540,542,544,547,549												
535	CON-3.6-10300	Site Clearance for Portion B2,B3 (CIF) after Decommissioning of CIF	2 days	0 days	100%	Sat 20/7/24	Sun 21/7/24	Sat 20/7/24	Sun 21/7/24	0 days	0 days	518	550,560,527,529												
536	CON-3.6-20000	Establishment	948 days	0 days	100%	Sun 19/12/21	Tue 23/7/24	Sun 19/12/21	Tue 23/7/24	0 days	0 days														

Activity ID	Task Name	Duration	Remaining Duration	% Work Complete	Start	Finish	Late Start	Late Finish	Free Slack	Total Slack	Predecessors	Successors	2021	Half 2, 2021	Half 1, 2022	Half 2, 2022	Half 1, 2023	Half 2, 2023	Half 1, 2024	Half 2, 2024	Half 1, 2025	Half 2, 2025	Half 1, 2026	Half 2, 2026	
537	CON-3.6-20100	Condition Survey for Existing Structures to be Demolished for Portion A2	14 days	0 days	100%	Sun 23/1/22	Sat 5/2/22	Sun 23/1/22	Sat 5/2/22	0 days	0 days	533	538												
538	CON-3.6-20200	Condition Survey for Existing Structures to be Demolished for Portion B1,B2	14 days	0 days	100%	Sun 6/2/22	Sat 19/2/22	Sun 6/2/22	Sat 19/2/22	0 days	0 days	534,537	557,559,554												
539	CON-3.6-20300	Tree Survey for Portion A2	14 days	0 days	100%	Sun 23/1/22	Sat 5/2/22	Sun 23/1/22	Sat 5/2/22	0 days	0 days	533	553,556												
540	CON-3.6-20400	Tree Survey for Portion B1,B2	14 days	0 days	100%	Wed 2/2/22	Tue 15/2/22	Wed 2/2/22	Tue 15/2/22	0 days	0 days	534	557,554												
541	CON-3.6-20500	Initial Survey for Portion A2	14 days	0 days	100%	Sun 23/1/22	Sat 5/2/22	Sun 23/1/22	Sat 5/2/22	0 days	0 days	533	553,556												
542	CON-3.6-20600	Initial Survey for Portion B1,B2	14 days	0 days	100%	Wed 2/2/22	Tue 15/2/22	Wed 2/2/22	Tue 15/2/22	0 days	0 days	534	557,554												
543	CON-3.6-20700	Site Haul Road for Portion A2	7 days	0 days	100%	Sun 23/1/22	Sat 29/1/22	Sun 23/1/22	Sat 29/1/22	0 days	0 days	533	553,556												
544	CON-3.6-20800	Site Haul Road for Portion B1,B2	7 days	0 days	100%	Sun 19/12/21	Sat 25/12/21	Sun 19/12/21	Sat 25/12/21	0 days	0 days	534	557,554												
545	CON-3.6-20900	Health & Hygiene Facilities	7 days	0 days	100%	Sun 23/1/22	Sat 29/1/22	Sun 23/1/22	Sat 29/1/22	0 days	0 days	533	553,556												
546	CON-3.6-21000	Fence Work & Gate for Portion A2	14 days	0 days	100%	Sun 23/1/22	Sat 5/2/22	Sun 23/1/22	Sat 5/2/22	0 days	0 days	533	553,556												
547	CON-3.6-21100	Fence Work for Portion B1,B2	14 days	0 days	100%	Sun 19/12/21	Sat 1/1/22	Sun 19/12/21	Sat 1/1/22	0 days	0 days	534	557,551,554												
548	CON-3.6-21200	Underground Utilities Detection for Portion A2	7 days	0 days	100%	Sun 23/1/22	Sat 29/1/22	Sun 23/1/22	Sat 29/1/22	0 days	0 days	533	553,556												
549	CON-3.6-21300	Underground Utilities Detection for Portion B1,B2	7 days	0 days	100%	Sun 19/12/21	Sat 25/12/21	Sun 19/12/21	Sat 25/12/21	0 days	0 days	534	557,554												
550	CON-3.6-21310	Underground Utilities Detection for Portion B2,B3	2 days	0 days	100%	Mon 22/7/24	Tue 23/7/24	Mon 22/7/24	Tue 23/7/24	0 days	0 days	535	555,529,530												
551	CON-3.6-21400	Install Monitoring Points	14 days	0 days	100%	Sun 2/1/22	Sat 15/1/22	Sun 2/1/22	Sat 15/1/22	0 days	0 days	547	559,567,568,611												
552	CON-3.6-30000	Tree Treatment	901 days	0 days	100%	Sun 6/2/22	Thu 25/7/24	Sun 6/2/22	Thu 25/7/24	0 days	0 days														
553	CON-3.6-30100	Tree Felling for Portion A2	14 days	0 days	100%	Sun 6/2/22	Sat 19/2/22	Sun 6/2/22	Sat 19/2/22	0 days	0 days	539,541,543,545,546,563													
554	CON-3.6-30200	Tree Felling for Portion B1, B2	14 days	0 days	100%	Sun 20/2/22	Sat 5/3/22	Sun 20/2/22	Sat 5/3/22	0 days	0 days	538,540,542,544,547,559,567,568,611,556													
555	CON-3.6-30210	Tree Felling for Portion B2,B3 (CIF)	2 days	0 days	100%	Wed 24/7/24	Thu 25/7/24	Wed 24/7/24	Thu 25/7/24	0 days	0 days	550													
556	CON-3.6-30300	Tree Protection Portion A2	14 days	0 days	100%	Sun 6/2/22	Sat 19/2/22	Sun 6/2/22	Sat 19/2/22	0 days	0 days	539,541,543,545,546,559,563													
557	CON-3.6-30400	Tree Protection Portion B1,B2	14 days	0 days	100%	Sun 20/2/22	Sat 5/3/22	Sun 20/2/22	Sat 5/3/22	0 days	0 days	538,540,542,544,547,559													
558	CON-3.6-40000	Demolition work	777 days	0 days	100%	Mon 20/6/22	Sun 4/8/24	Mon 20/6/22	Sun 4/8/24	0 days	0 days														
559	CON-3.6-40100	Demolition of Existing Structures	60 days	0 days	100%	Mon 20/6/22	Thu 18/8/22	Mon 20/6/22	Thu 18/8/22	0 days	0 days	538,397,400,551,557,574,567FS-20 days,568FS													
560	CON-3.6-40110	Demolition of Existing Steel Structures, existing sheet pile wall between +26.5mPD and +19.5mPD Platform (CIF)	14 days	0 days	100%	Mon 22/7/24	Sun 4/8/24	Mon 22/7/24	Sun 4/8/24	0 days	0 days	397,400,535	581												
561	CON-3.6-50000	Decontamination (Include Adjacent Road D1, Remediation of contaminated soil carried out at Detention Pond)	248 days	0 days	100%	Sun 20/2/22	Tue 25/10/22	Sun 20/2/22	Tue 25/10/22	0 days	0 days														
562	CON-3.6-51000	CAP	136 days	0 days	100%	Sun 20/2/22	Tue 5/7/22	Sun 20/2/22	Tue 5/7/22	0 days	0 days														
563	CON-3.6-51100	Site Appraisal for Portion A2	60 days	0 days	100%	Sun 20/2/22	Wed 20/4/22	Sun 20/2/22	Wed 20/4/22	0 days	0 days	553,556	564												
564	CON-3.6-51200	Site Appraisal for Portion B1,B2,B3& Preparation of CAP for all Portions	25 days	0 days	100%	Thu 21/4/22	Sun 15/5/22	Thu 21/4/22	Sun 15/5/22	0 days	0 days	563	287SS,565												
565	CON-3.6-51300	Submission& Endorsement by EPD	30 days	0 days	100%	Mon 6/6/22	Tue 5/7/22	Mon 6/6/22	Tue 5/7/22	0 days	0 days	564	567,568												
566	CON-3.6-52000	Ground Investigation (Trial Pit / Borehole)	45 days	0 days	100%	Sat 30/7/22	Mon 12/9/22	Sat 30/7/22	Mon 12/9/22	0 days	0 days														
567	CON-3.6-52100	Trial Pit Sampling& Testing	45 days	0 days	100%	Sat 30/7/22	Mon 12/9/22	Sat 30/7/22	Mon 12/9/22	0 days	0 days	565,551,554,559FS-2(570,296,299													
568	CON-3.6-52200	Inspection Pit for installing Groundwater Wells	45 days	0 days	100%	Sat 30/7/22	Mon 12/9/22	Sat 30/7/22	Mon 12/9/22	0 days	0 days	565,551,554,559FS-2(570													
569	CON-3.6-53000	CAR & RAP Submission	43 days	0 days	100%	Tue 13/9/22	Tue 25/10/22	Tue 13/9/22	Tue 25/10/22	0 days	0 days														
570	CON-3.6-53100	Preparation of CAR& RAP	15 days	0 days	100%	Tue 13/9/22	Tue 27/9/22	Tue 13/9/22	Tue 27/9/22	0 days	0 days	567,568	571												
571	CON-3.6-53200	Review and Accepted by EPD	28 days	0 days	100%	Wed 28/9/22	Tue 25/10/22	Wed 28/9/22	Tue 25/10/22	0 days	0 days	570,133	574												
572	CON-3.6-70000	Site formation	786 days	0 days	100%	Wed 1/2/23	Thu 27/3/25	Wed 1/2/23	Thu 27/3/25	0 days	0 days														
573	CON-3.6-70100	Earthwork	258 days	0 days	100%	Sat 13/7/24	Thu 27/3/25	Sat 13/7/24	Thu 27/3/25	0 days	0 days														
574	CON-3.6-70110	Excavation from Kai Pak Ling Road to Maintenance Access (+35.5 to +30.0mPD)	30 days	0 days	100%	Wed 2/10/24	Thu 31/10/24	Wed 2/10/24	Thu 31/10/24	0 days	0 days	429,559,571,591FS+1575 days,583FS+10 days	575												
575	CON-3.6-70120	Cut Slope to Maintenance Access +30mPD	28 days	0 days	100%	Fri 1/11/24	Thu 28/11/24	Fri 1/11/24	Thu 28/11/24	0 days	0 days	574	576												
576	CON-3.6-70130	Excavation to Formation +23.0mPD	30 days	0 days	100%	Thu 2/1/25	Fri 31/1/25	Thu 2/1/25	Fri 31/1/25	0 days	0 days	575,609	577												
577	CON-3.6-70140	Cut Slope to Formation +23.0mPD	18 days	0 days	100%	Sat 1/2/25	Tue 18/2/25	Sat 1/2/25	Tue 18/2/25	0 days	0 days	576	520,521,522,600FF+21 days												
578	CON-3.6-70151	Trim slope at the bottom corner for temporary traffic diversion	5 days	0 days	100%	Fri 6/12/24	Tue 10/12/24	Fri 6/12/24	Tue 10/12/24	0 days	0 days	529,584	603												
579	CON-3.6-70152	Backfilling & Compaction to Formation +23.0mPD	12 days	0 days	100%	Sat 18/1/25	Wed 29/1/25	Sat 18/1/25	Wed 29/1/25	0 days	0 days	604FS-12 days	580												
580	CON-3.6-70160	Trimming for Fill Slope	4 days	0 days	100%	Thu 30/1/25	Sun 2/2/25	Thu 30/1/25	Sun 2/2/25	0 days	0 days	579	605												
581	CON-3.6-70170	Backfill & Compaction to Formation +23.0mPD (Site 3-6 CIF)	110 days	0 days	100%	Sun 25/8/24	Thu 12/12/24	Sun 25/8/24	Thu 12/12/24	0 days	0 days	560,520,521,522,528,582,525SS													
582	CON-3.6-70180	Trimming for Fill Slope (Site 3-6 CIF)	8 days	0 days	100%	Fri 13/12/24	Fri 20/12/24	Fri 13/12/24	Fri 20/12/24	0 days	0 days	581	611,598												

ID	Activity ID	Task Name	Duration	Remaining Duration	% Work Complete	Start	Finish	Late Start	Late Finish	Free Slack	Total Slack	Predecessors	Successors	2021	Half 2, 2021	Half 1, 2022	Half 2, 2022	Half 1, 2023	Half 2, 2023	Half 1, 2024	Half 2, 2024	Half 1, 2025	Half 2, 2025	Half 1, 2026	Half 2, 2026
583	CON-3.6-70190	Soil Replacement with No-fines concrete at Kai Pak Ling Road (PMI 137)	71 days	0 days	100%	Sat 13/7/24	Sat 21/9/24	Sat 13/7/24	Sat 21/9/24	0 days	0 days	591	594,592,584,574FS+10 days												
584	CON-3.6-70191	Soil Replacement with No-fines concrete at Ray-On Depot (PMI 156)	75 days	0 days	100%	Sun 22/9/24	Thu 5/12/24	Sun 22/9/24	Thu 5/12/24	0 days	0 days	583	603,578												
585	CON-3.6-70192	Chain Link Fence and Construction of Access Gate (PMI 168, PMI 250)	66 days	0 days	100%	Tue 21/1/25	Thu 27/3/25	Tue 21/1/25	Thu 27/3/25	0 days	0 days		600FF												
586	CON-3.6-70200	Surface Drainage	786 days	0 days	100%	Wed 1/2/23	Thu 27/3/25	Wed 1/2/23	Thu 27/3/25	0 days	0 days														
587	CON-3.6-70210	At Cut Slope Crest +35.5mPD (KPLR)	620 days	0 days	100%	Wed 1/2/23	Sat 12/10/24	Wed 1/2/23	Sat 12/10/24	0 days	0 days														
588	CON-3.6-70211	Excavation to Formation	100 days	0 days	100%	Wed 1/2/23	Thu 11/5/23	Wed 1/2/23	Thu 11/5/23	0 days	0 days		589												
589	CON-3.6-70212	UU slewing at U-channel location	355 days	0 days	100%	Fri 12/5/23	Tue 30/4/24	Fri 12/5/23	Tue 30/4/24	0 days	0 days	588	590												
590	CON-3.6-70213	Catchpit	50 days	0 days	100%	Wed 1/5/24	Wed 19/6/24	Wed 1/5/24	Wed 19/6/24	0 days	0 days	589	591SS+13 days,611												
591	CON-3.6-70214	U-channel	60 days	0 days	100%	Tue 14/5/24	Fri 12/7/24	Tue 14/5/24	Fri 12/7/24	0 days	0 days	590SS+13 days	574FS+10 days,1315FS+10 days												
592	CON-3.6-70215	Diversion of uncharted 600mm Crossroad Drain at Kai Pak Ling Road (PMI 102)	21 days	0 days	100%	Sun 22/9/24	Sat 12/10/24	Sun 22/9/24	Sat 12/10/24	0 days	0 days	583	594												
593	CON-3.6-70220	At Maintenance Access +30mPD	51 days	0 days	100%	Sun 13/10/24	Mon 21/12/24	Sun 13/10/24	Mon 21/12/24	0 days	0 days														
594	CON-3.6-70221	Excavation to Formation	30 days	0 days	100%	Sun 13/10/24	Mon 11/11/24	Sun 13/10/24	Mon 11/11/24	0 days	0 days	583,592	595SS+7 days												
595	CON-3.6-70222	Catchpit	30 days	0 days	100%	Sun 20/10/24	Mon 18/11/24	Sun 20/10/24	Mon 18/11/24	0 days	0 days	594SS+7 days	596SS+14 days												
596	CON-3.6-70223	U-channel	30 days	0 days	100%	Sun 3/11/24	Mon 21/12/24	Sun 3/11/24	Mon 21/12/24	0 days	0 days	595SS+14 days	609												
597	CON-3.6-70230	At Formation Level +23.0mPD	97 days	0 days	100%	Sat 21/12/24	Thu 27/3/25	Sat 21/12/24	Thu 27/3/25	0 days	0 days														
598	CON-3.6-70235	Excavation to Formation (Site 3-6 CIF)	67 days	0 days	100%	Sat 21/12/24	Tue 25/2/25	Sat 21/12/24	Tue 25/2/25	0 days	0 days	526,582	599SS+7 days												
599	CON-3.6-70236	Catchpit (Site 3-6 CIF)	67 days	0 days	100%	Sat 28/12/24	Tue 4/3/25	Sat 28/12/24	Tue 4/3/25	0 days	0 days	598SS+7 days	600SS+7 days												
600	CON-3.6-70237	U-channel (Site 3-6 CIF)	83 days	0 days	100%	Sat 4/1/25	Thu 27/3/25	Sat 4/1/25	Thu 27/3/25	0 days	0 days	599SS+7 days,577FF	601SS+44 days,611												
601	CON-3.6-70238	Stepped Channel (Site 3-6 CIF)	23 days	0 days	100%	Mon 17/2/25	Tue 11/3/25	Mon 17/2/25	Tue 11/3/25	0 days	0 days	600SS+44 days	611,610FS-7 days												
602	CON-3.6-70240	At Fill Slope Toe +23.0mPD	91 days	0 days	100%	Wed 11/12/24	Tue 11/3/25	Wed 11/12/24	Tue 11/3/25	0 days	0 days														
603	CON-3.6-70241	Excavation to Formation	40 days	0 days	100%	Wed 11/12/24	Sun 19/1/25	Wed 11/12/24	Sun 19/1/25	0 days	0 days	584,578,1153	604SS+10 days,605												
604	CON-3.6-70242	Dia. 675 drain pipe with 2 manholes	40 days	0 days	100%	Sat 21/12/24	Wed 29/1/25	Sat 21/12/24	Wed 29/1/25	0 days	0 days	603SS+10 days	605,579FS-12 days												
605	CON-3.6-70243	Excavation to Formation of Uchannel	8 days	0 days	100%	Mon 3/2/25	Mon 10/2/25	Mon 3/2/25	Mon 10/2/25	0 days	0 days	580,604,603	606												
606	CON-3.6-70244	Catchpit	8 days	0 days	100%	Tue 11/2/25	Tue 18/2/25	Tue 11/2/25	Tue 18/2/25	0 days	0 days	605	607												
607	CON-3.6-70245	U-channel	21 days	0 days	100%	Wed 19/2/25	Tue 11/3/25	Wed 19/2/25	Tue 11/3/25	0 days	0 days	606	611												
608	CON-3.6-70300	Concrete Access	115 days	0 days	100%	Tue 3/12/24	Thu 27/3/25	Tue 3/12/24	Thu 27/3/25	0 days	0 days														
609	CON-3.6-70310	Maintenance Access	30 days	0 days	100%	Tue 3/12/24	Wed 11/1/25	Tue 3/12/24	Wed 11/1/25	0 days	0 days	596	576												
610	CON-3.6-70340	Stairway above Formation Level +23.0mPD (Site 3-6 CIF)	23 days	0 days	100%	Wed 5/3/25	Thu 27/3/25	Wed 5/3/25	Thu 27/3/25	0 days	0 days	601FS-7 days	611												
611	CON-3.6-80000	Planned Completion of Section 1A1	0 days	0 days	100%	Thu 27/3/25	Thu 27/3/25	Thu 27/3/25	Thu 27/3/25	0 days	0 days	610,607,601,582,524,120													
612	CON-3.6-80000	Section 1A2	974 days	0 days	100%	Thu 28/7/22	Thu 27/3/25	Thu 28/7/22	Thu 27/3/25	0 days	0 days														
613	CON-3.6-80000	Site 3-7 Additional Works affected by CIF Area	559 days	0 days	100%	Wed 22/2/25	Mon 2/9/24	Wed 22/2/25	Mon 2/9/24	0 days	0 days														
614	CON-3.7-CIF101	Mobilization of Plant and Labour Required (PMI 07)	14 days	0 days	100%	Mon 10/6/24	Sun 23/6/24	Mon 10/6/24	Sun 23/6/24	0 days	0 days	51	615FS-7 days,616												
615	CON-3.7-CIF102	Removal of MIC Modules (PMI 073)	33 days	0 days	100%	Mon 17/6/24	Fri 19/7/24	Mon 17/6/24	Fri 19/7/24	0 days	0 days	614FS-7 days	625,642,647,644												
616	CON-3.7-CIF110	Removal of Hoarding and Type 2 railing for CIF (PMI 073)	7 days	0 days	100%	Mon 24/6/24	Sun 30/6/24	Mon 24/6/24	Sun 30/6/24	0 days	0 days	614	680												
617	CON-3.7-CIF120	Relocation of Contractor's Storage Area	98 days	0 days	100%	Wed 22/2/25	Tue 30/5/23	Wed 22/2/25	Tue 30/5/23	0 days	0 days														
618	CON-3.7-CIF121	Relocation of Storage Area from site 3-7 to Lam	60 days	0 days	100%	Wed 22/2/25	Sat 22/4/23	Wed 22/2/25	Sat 22/4/23	0 days	0 days														
619	CON-3.7-CIF122	Relocation of Storage Area from site 3-7 to Deep	30 days	0 days	100%	Mon 1/5/23	Tue 30/5/23	Mon 1/5/23	Tue 30/5/23	0 days	0 days														
620	CON-3.7-CIF200	Removal of Additional Concrete Pavement within HSK CIF (PMI 073)	30 days	0 days	100%	Sun 4/8/24	Mon 2/9/24	Sun 4/8/24	Mon 2/9/24	0 days	0 days	647,638,634	680,678												
621	CON-3.7-CIF210	Removal of Sewer and Watermain for CIF (PMI 073)	20 days	0 days	100%	Thu 25/7/24	Tue 13/8/24	Thu 25/7/24	Tue 13/8/24	0 days	0 days	625	680,710												
622	CON-3.7-10000	Site 3-7 (Portion A2,B2,B3,B5)	974 days	0 days	100%	Thu 28/7/22	Thu 27/3/25	Thu 28/7/22	Thu 27/3/25	0 days	0 days														
623	CON-3.7-10000	Site Clearance	728 days	0 days	100%	Thu 28/7/22	Wed 24/7/24	Thu 28/7/22	Wed 24/7/24	0 days	0 days														
624	CON-3.7-10100	Site Clearance for Portion A2	5 days	0 days	100%	Thu 28/7/22	Mon 1/8/22	Thu 28/7/22	Mon 1/8/22	0 days	0 days	50	635,636,637,627,629,631,632												
625	CON-3.7-10300	Site Clearance for Portion B2,B3,B4,B5 (CIF) after Decommissioning of CIF	5 days	0 days	100%	Sat 20/7/24	Wed 24/7/24	Sat 20/7/24	Wed 24/7/24	0 days	0 days	615	638,634,621												
626	CON-3.7-20000	Establishment	725 days	0 days	100%	Tue 2/8/22	Fri 26/7/24	Tue 2/8/22	Fri 26/7/24	0 days	0 days														
627	CON-3.7-20100	Condition Survey for Existing Structures to be Demolished for Portion A2	14 days	0 days	100%	Tue 2/8/22	Mon 15/8/22	Tue 2/8/22	Mon 15/8/22	0 days	0 days	624	628,646												
628	CON-3.7-20200	Condition Survey for Existing Structures to be Demolished for Portion B2,B3,B5	14 days	0 days	100%	Tue 16/8/22	Mon 29/8/22	Tue 16/8/22	Mon 29/8/22	0 days	0 days	627													

ID	Activity ID	Task Name	Duration	Remaining Duration	% Work Complete	Start	Finish	Late Start	Late Finish	Free Slack	Total Slack	Predecessors	Successors	2021	Half 2, 2021	Half 1, 2022	Half 2, 2022	Half 1, 2023	Half 2, 2023	Half 1, 2024	Half 2, 2024	Half 1, 2025	Half 2, 2025	Half 1, 2026	Half 2, 2026
629	CON-3.7-20300	Tree Survey for Portion A2	14 days	0 days	100%	Tue 2/8/22	Mon 15/8/22	Tue 2/8/22	Mon 15/8/...	0 days	0 days	624	630												
630	CON-3.7-20400	Tree Survey for Portion B2,B3,B5	14 days	0 days	100%	Tue 16/8/22	Mon 29/8/22	Tue 16/8/22	Mon 29/8/...	0 days	0 days	629													
631	CON-3.7-20500	Initial Survey for Portion A2	14 days	0 days	100%	Tue 2/8/22	Mon 15/8/22	Tue 2/8/22	Mon 15/8/...	0 days	0 days	624	632												
632	CON-3.7-20600	Initial Survey for Portion B2,B3,B5	14 days	0 days	100%	Tue 16/8/22	Mon 29/8/22	Tue 16/8/22	Mon 29/8/...	0 days	0 days	631													
633	CON-3.7-20700	Site Haul Road for Portion A2	14 days	0 days	100%	Tue 2/8/22	Mon 15/8/22	Tue 2/8/22	Mon 15/8/...	0 days	0 days	624	650												
634	CON-3.7-20810	Site Haul Road for Portion (B2,B3,B4,B5 - CIF)	2 days	0 days	100%	Thu 25/7/24	Fri 26/7/24	Thu 25/7/24	Fri 26/7/24	0 days	0 days	625	620												
635	CON-3.7-20900	Health & Hygiene Facilities	7 days	0 days	100%	Tue 2/8/22	Mon 8/8/22	Tue 2/8/22	Mon 8/8/22	0 days	0 days	624	641,643												
636	CON-3.7-21000	Fence Work & Gate for Portion A2	14 days	0 days	100%	Tue 2/8/22	Mon 15/8/22	Tue 2/8/22	Mon 15/8/...	0 days	0 days	624	641,643												
637	CON-3.7-21200	Underground Utilities Detection for Portion A2	7 days	0 days	100%	Tue 2/8/22	Mon 8/8/22	Tue 2/8/22	Mon 8/8/22	0 days	0 days	624	641,639,643												
638	CON-3.7-21310	Underground Utilities Detection for Portion (B2,B3,B4,B5 - CIF)	2 days	0 days	100%	Thu 25/7/24	Fri 26/7/24	Thu 25/7/24	Fri 26/7/24	0 days	0 days	625	620												
639	CON-3.7-21400	Install Monitoring Points	14 days	0 days	100%	Tue 9/8/22	Mon 22/8/22	Tue 9/8/22	Mon 22/8/...	0 days	0 days	637	654,655												
640	CON-3.7-30000	Tree Treatment	746 days	0 days	100%	Tue 16/8/22	Fri 30/8/24	Tue 16/8/22	Fri 30/8/24	0 days	0 days														
641	CON-3.7-30100	Tree Felling for Portion A2	14 days	0 days	100%	Tue 16/8/22	Mon 29/8/22	Tue 16/8/22	Mon 29/8/...	0 days	0 days	635,636,637	646,650												
642	CON-3.7-30210	Tree Felling for Portion (B2,B3,B4,B5 - CIF)	7 days	0 days	100%	Sat 24/8/24	Fri 30/8/24	Sat 24/8/24	Fri 30/8/24	0 days	0 days	615	678												
643	CON-3.7-30300	Tree Protection Portion A2	14 days	0 days	100%	Tue 16/8/22	Mon 29/8/22	Tue 16/8/22	Mon 29/8/...	0 days	0 days	635,636,637	650												
644	CON-3.7-30400	Tree Protection Portion B2,B3,B4,B5 -CIF	7 days	0 days	100%	Tue 30/8/22	Wed 24/7/24	Tue 30/8/22	Wed 24/7/...	0 days	0 days	615	678												
645	CON-3.7-40000	Demolition work	705 days	0 days	100%	Tue 30/8/22	Sat 3/8/24	Tue 30/8/22	Sat 3/8/24	0 days	0 days														
646	CON-3.7-40100	Demolition of Existing Structures A2	15 days	0 days	100%	Tue 30/8/22	Tue 13/9/22	Tue 30/8/22	Tue 13/9/...	0 days	0 days	397,400,627,641	685												
647	CON-3.7-40110	Demolition of Existing Steel Structures - CIF	15 days	0 days	100%	Sat 20/7/24	Sat 3/8/24	Sat 20/7/24	Sat 3/8/24	0 days	0 days	397,400,615	680,1305,1306,710,678,62												
648	CON-3.7-50000	Decontamination (include adjacent Road D1 and Road L51 , remediation of contaminated soil carried out at Detention Pond)	177 days	0 days	100%	Sat 1/10/22	Sun 26/3/23	Sat 1/10/22	Sun 26/3/23	0 days	0 days														
649	CON-3.7-51000	CAP	75 days	0 days	100%	Sat 1/10/22	Wed 14/1/22	Sat 1/10/22	Wed 14/1/...	0 days	0 days														
650	CON-3.7-51100	Site Appraisal for Portion A2	20 days	0 days	100%	Sat 1/10/22	Thu 20/10/22	Sat 1/10/22	Thu 20/1/...	0 days	0 days	641,643,633	651												
651	CON-3.7-51200	Site Appraisal for Portion B2,B3,B5& Preparation of CAP for all Portions	25 days	0 days	100%	Fri 21/10/22	Mon 14/11/22	Fri 21/10/22	Mon 14/11/22	0 days	0 days	650	652												
652	CON-3.7-51300	Submission& Endorsement by EPD	30 days	0 days	100%	ue 15/11/22	Wed 14/12/22	Tue 15/11/...	Wed 14/1/...	0 days	0 days	651,288FF	654,655												
653	CON-3.7-52000	Ground Investigation (Trial Pit / Borehole)	45 days	0 days	100%	hu 15/12/22	Sat 28/1/23	Thu 15/12/...	Sat 28/1/23	0 days	0 days														
654	CON-3.7-52100	Trial Pit Sampling& Testing	45 days	0 days	100%	hu 15/12/22	Sat 28/1/23	Thu 15/12/...	Sat 28/1/23	0 days	0 days	639,652,393	657												
655	CON-3.7-52200	Inspection Pit for installing Groundwater Wells	45 days	0 days	100%	hu 15/12/22	Sat 28/1/23	Thu 15/12/...	Sat 28/1/23	0 days	0 days	639,652	657												
656	CON-3.7-53000	CAR & RAP Submission	43 days	0 days	100%	Sun 29/1/23	Sun 12/3/23	Sun 29/1/23	Sun 12/3/...	0 days	0 days														
657	CON-3.7-53100	Preparation of CAR& RAP	15 days	0 days	100%	Sun 29/1/23	Sun 12/2/23	Sun 29/1/23	Sun 12/2/...	0 days	0 days	654,655	658												
658	CON-3.7-53200	Review and Accepted by EPD	28 days	0 days	100%	Mon 13/2/23	Sun 12/3/23	Mon 13/2/23	Sun 12/3/...	0 days	0 days	657	661,663												
659	CON-3.7-54000	Decontamination Works	14 days	0 days	100%	Sun 12/3/23	Sun 26/3/23	Sun 12/3/23	Sun 26/3/...	0 days	0 days														
660	CON-3.7-54100	Treatability Test for Heavy Metal	0 days	0 days	100%	Sun 12/3/23	Sun 12/3/23	Sun 12/3/23	Sun 12/3/...	0 days	0 days														
661	CON-3.7-54110	Treatability Test for Heavy Metal	0 days	0 days	100%	Sun 12/3/23	Sun 12/3/23	Sun 12/3/23	Sun 12/3/...	0 days	0 days	658	667												
662	CON-3.7-54200	Confirmation Test Sampling and Testing	0 days	0 days	100%	Sun 12/3/23	Sun 12/3/23	Sun 12/3/23	Sun 12/3/...	0 days	0 days														
663	CON-3.7-54210	Trial Pit	0 days	0 days	100%	Sun 12/3/23	Sun 12/3/23	Sun 12/3/23	Sun 12/3/...	0 days	0 days	658	664												
664	CON-3.7-54220	Sampling and Testing	0 days	0 days	100%	Sun 12/3/23	Sun 12/3/23	Sun 12/3/23	Sun 12/3/...	0 days	0 days	663	666,667												
665	CON-3.7-54300	Excavation of Contaminated Soil	0 days	0 days	100%	Sun 12/3/23	Sun 12/3/23	Sun 12/3/23	Sun 12/3/...	0 days	0 days														
666	CON-3.7-54310	To Stockpile for Biopile	0 days	0 days	100%	Sun 12/3/23	Sun 12/3/23	Sun 12/3/23	Sun 12/3/...	0 days	0 days	664,134	668SS+14 days												
667	CON-3.7-54320	To Stockpile for Cement Solidification	0 days	0 days	100%	Sun 12/3/23	Sun 12/3/23	Sun 12/3/23	Sun 12/3/...	0 days	0 days	664,134,661	669SS+14 days,1181SS+4												
668	CON-3.7-54400	Backfilling to Formation of Biopile Location	0 days	0 days	100%	Sun 26/3/23	Sun 26/3/23	Sun 26/3/23	Sun 26/3/...	0 days	0 days	666SS+14 days													
669	CON-3.7-54500	Backfilling to Formation Cement Solidification	0 days	0 days	100%	Sun 26/3/23	Sun 26/3/23	Sun 26/3/23	Sun 26/3/...	0 days	0 days	667SS+14 days													
670	CON-3.7-60000	Site Formation	926 days	0 days	100%	Wed 14/9/22	Thu 27/3/25	Wed 14/9/...	Thu 27/3/...	0 days	0 days														
671	CON-3.7-60100	Earthwork	452 days	0 days	100%	Mon 1/1/24	Thu 27/3/25	Mon 1/1/24	Thu 27/3/...	0 days	0 days														
672	CON-3.7-60110	Excavation to Access Road / +30mPD and Stockpile to Site 3-6	30 days	0 days	100%	Mon 1/1/24	Tue 30/1/24	Mon 1/1/24	Tue 30/1/24	0 days	0 days	429,688	673FS-15 days												
673	CON-3.7-60120	Cut Slope to to Access Road / +30mPD and Stockpile to Site 3-6 (location no Asbestos containing material)	100 days	0 days	100%	Tue 16/1/24	Wed 24/4/24	Tue 16/1/24	Wed 24/4/24	0 days	0 days	672FS-15 days	675												
674	CON-3.7-60121	Asbestos Report Submission and Environmental Department Approval	90 days	0 days	100%	Fri 1/3/24	Wed 29/5/24	Fri 1/3/24	Wed 29/5/24	0 days	0 days		675												
675	CON-3.7-60122	Removal of Asbestos Containing Material at S	14 days	0 days	100%	Fri 28/6/24	Thu 11/7/24	Fri 28/6/24	Thu 11/7/...	0 days	0 days	674,673	677												
676	CON-3.7-60123	Termination of power by CLP	1 day	0 days	100%	Sun 22/9/24	Sun 22/9/24	Sun 22/9/24	Sun 22/9/...	0 days	0 days		677												

*E-Excavator, L-Lorry, W-Worker, D-Drill plant, C-Crane Lorry, R-Rotter


Contract No. YL/2020/03 Hung Shui Kiu/Ha Tsuen New Development Area Stage 1 Works - Site Formation and Engineering Infrastructure														Revised Programme Rev.13 (May 2025)													
ID	Activity ID	Task Name	Duration	Remaining Duration	% Work Complete	Start	Finish	Late Start	Late Finish	Free Slack	Total Slack	Predecessors	Successors	2021	Half 2, 2021	Half 1, 2022	Half 2, 2022	Half 1, 2023	Half 2, 2023	Half 1, 2024	Half 2, 2024	Half 1, 2025	Half 2, 2025	Half 1, 2026	Half 2, 2026		
725	CON-3.8-20800	Site Haul Road for Portion B6,B7	7 days	0 days	100%	Sun 2/1/22	Sat 8/1/22	Sun 2/1/22	Sat 8/1/22	0 days	0 days	715	736,739														
726	CON-3.8-20810	Site Haul Road for Portion B4,B5 - (Site 3-8 CIF)	2 days	0 days	100%	Fri 9/8/24	Sat 10/8/24	Fri 9/8/24	Sat 10/8/24	0 days	0 days	716,706	780														
727	CON-3.8-20900	Health & Hygiene Facilities	7 days	0 days	100%	Sun 2/1/22	Sat 8/1/22	Sun 2/1/22	Sat 8/1/22	0 days	0 days	714	735,738														
728	CON-3.8-21000	Fence Work & Gate for Portion A3	14 days	0 days	100%	Sun 2/1/22	Sat 15/1/22	Sun 2/1/22	Sat 15/1/22	0 days	0 days	714	735,738														
729	CON-3.8-21100	Fence Work for Portion B6,B7	7 days	0 days	100%	Sun 2/1/22	Sat 8/1/22	Sun 2/1/22	Sat 8/1/22	0 days	0 days	715	736,733,739														
730	CON-3.8-21200	Underground Utilities Detection for Portion A3	7 days	0 days	100%	Sun 2/1/22	Sat 8/1/22	Sun 2/1/22	Sat 8/1/22	0 days	0 days	714	735,738														
731	CON-3.8-21300	Underground Utilities Detection for Portion B6,B7	7 days	0 days	100%	Sun 2/1/22	Sat 8/1/22	Sun 2/1/22	Sat 8/1/22	0 days	0 days	715	736,739														
732	CON-3.8-21310	Underground Utilities Detection for Portion B4,B5 - (Site 3-8 CIF)	2 days	0 days	100%	Fri 9/8/24	Sat 10/8/24	Fri 9/8/24	Sat 10/8/24	0 days	0 days	716,706	780														
733	CON-3.8-21400	Install Monitoring Points	14 days	0 days	100%	Sun 9/1/22	Sat 22/1/22	Sun 9/1/22	Sat 22/1/22	0 days	0 days	729	750,751														
734	CON-3.8-30000	Tree Treatment	944 days	0 days	100%	Sun 16/1/22	Fri 16/8/24	Sun 16/1/22	Fri 16/8/24	0 days	0 days		Tree Treatment														
735	CON-3.8-30100	Tree Felling for Portion A3	14 days	0 days	100%	Sun 16/1/22	Sat 29/1/22	Sun 16/1/22	Sat 29/1/22	0 days	0 days	720,722,724,727,728,750,751															
736	CON-3.8-30200	Tree Felling for Portion B6,B7	14 days	0 days	100%	Sun 16/1/22	Sat 29/1/22	Sun 16/1/22	Sat 29/1/22	0 days	0 days	721,723,725,729,731	750,751														
737	CON-3.8-30210	Tree Felling for Portion B4,B5 - (Site 3-8 CIF)	4 days	0 days	100%	Tue 13/8/24	Fri 16/8/24	Tue 13/8/24	Fri 16/8/24	0 days	0 days	743	780														
738	CON-3.8-30300	Tree Protection for Portion A3	14 days	0 days	100%	Sun 16/1/22	Sat 29/1/22	Sun 16/1/22	Sat 29/1/22	0 days	0 days	720,722,724,727,728,750,751															
739	CON-3.8-30400	Tree Protection for Portion B6,B7	14 days	0 days	100%	Sun 16/1/22	Sat 29/1/22	Sun 16/1/22	Sat 29/1/22	0 days	0 days	721,723,725,729,731	750,751														
740	CON-3.8-30410	Tree Protection for Portion B4,B5 - (Site 3-8 CIF)	4 days	0 days	100%	Tue 13/8/24	Fri 16/8/24	Tue 13/8/24	Fri 16/8/24	0 days	0 days	743	780														
741	CON-3.8-40000	Demolition work	934 days	0 days	100%	Sat 22/1/22	Mon 12/8/24	Sat 22/1/22	Mon 12/8/24	0 days	0 days		Demolition work														
742	CON-3.8-40100	Demolition of Existing Structures	40 days	0 days	100%	Sat 22/1/22	Wed 2/3/22	Sat 22/1/22	Wed 2/3/22	0 days	0 days	719	750FS-30 days,751FS-30 days														
743	CON-3.8-40120	Demolition of Existing Steel Structures - (Site 3-8 CIF)	10 days	0 days	100%	Sat 3/8/24	Mon 12/8/24	Sat 3/8/24	Mon 12/8/24	0 days	0 days	705	767FS+39 days,780,1273,781														
744	CON-3.8-50000	Decontamination (Include adjacent Road D1 and Road L51,remediation of contaminated soil carried out at Detention Pond)	963 days	0 days	100%	Thu 3/3/22	Sun 20/10/24	Thu 3/3/22	Sun 20/10/24	0 days	0 days		Decontamination (Include adjacent Road D1 and Road L51,remediation of contaminated soil carried out at Detention Pond)														
745	CON-3.8-51000	CAP	115 days	0 days	100%	Thu 3/3/22	Sat 25/6/22	Thu 3/3/22	Sat 25/6/22	0 days	0 days		CAP														
746	CON-3.8-51100	Site Appraisal for Portion A3	60 days	0 days	100%	Thu 3/3/22	Sun 1/5/22	Thu 3/3/22	Sun 1/5/22	0 days	0 days	742	747,290SS														
747	CON-3.8-51200	Site Appraisal for Portion B4,B5,B6,B7 & Preparation of CAP for all Portions	25 days	0 days	100%	Mon 2/5/22	Thu 26/5/22	Mon 2/5/22	Thu 26/5/22	0 days	0 days	715,746,291FF	748														
748	CON-3.8-51300	Submission & Endorsement by EPD	30 days	0 days	100%	Fri 27/5/22	Sat 25/6/22	Fri 27/5/22	Sat 25/6/22	0 days	0 days	747	750,751														
749	CON-3.8-52000	Ground Investigation (Trial Pit / Borehole)	45 days	0 days	100%	Sun 26/6/22	Tue 9/8/22	Sun 26/6/22	Tue 9/8/22	0 days	0 days	718,719															
750	CON-3.8-52100	Trial Pit Sampling & Testing	45 days	0 days	100%	Sun 26/6/22	Tue 9/8/22	Sun 26/6/22	Tue 9/8/22	0 days	0 days	733,736,739,742FS-3(296,299,753															
751	CON-3.8-52200	Inspection Pit for installing Groundwater Wells	45 days	0 days	100%	Sun 26/6/22	Tue 9/8/22	Sun 26/6/22	Tue 9/8/22	0 days	0 days	748,733,736,739,742F753															
752	CON-3.8-53000	CAR & RAP Submission	43 days	0 days	100%	Wed 10/8/22	Wed 21/9/22	Wed 10/8/22	Wed 21/9/22	0 days	0 days		CAR & RAP Submission														
753	CON-3.8-53100	Preparation of CAR & RAP	15 days	0 days	100%	Wed 10/8/22	Wed 24/8/22	Wed 10/8/22	Wed 24/8/22	0 days	0 days	750,751	754														
754	CON-3.8-53200	Review & Accepted by EPD	28 days	0 days	100%	Thu 25/8/22	Wed 21/9/22	Thu 25/8/22	Wed 21/9/22	0 days	0 days	753	775FS+9 days,757FS+165 days														
755	CON-3.8-54000	Decontamination Works	596 days	0 days	100%	Sun 5/3/23	Sun 20/10/24	Sun 5/3/23	Sun 20/10/24	0 days	0 days		Decontamination Works														
756	CON-3.8-54100	Treatability Test	172 days	0 days	100%	Mon 6/3/23	Thu 24/8/23	Mon 6/3/23	Thu 24/8/23	0 days	0 days		Treatability Test														
757	CON-3.8-54110	Treatability Test for Heavy Metal	24 days	0 days	100%	Mon 6/3/23	Wed 29/3/23	Mon 6/3/23	Wed 29/3/23	0 days	0 days	754FS+165 days	765,766														
758	CON-3.8-54120	Treatability Test for Heavy Metal (CIF)	24 days	0 days	100%	Tue 1/8/23	Thu 24/8/23	Tue 1/8/23	Thu 24/8/23	0 days	0 days	754	768,762														
759	CON-3.8-54200	Confirmation Test Sampling and Testing	215 days	0 days	100%	Sun 5/3/23	Thu 5/10/23	Sun 5/3/23	Thu 5/10/23	0 days	0 days		Confirmation Test Sampling and Testing														
760	CON-3.8-54210	Trial Pit	14 days	0 days	100%	Sun 5/3/23	Sat 18/3/23	Sun 5/3/23	Sat 18/3/23	0 days	0 days	754FS+164 days	761														
761	CON-3.8-54220	Sampling and Testing	14 days	0 days	100%	Sun 19/3/23	Sat 1/4/23	Sun 19/3/23	Sat 1/4/23	0 days	0 days	760	765,766														
762	CON-3.8-54230	Trial Pit (CIF)	14 days	0 days	100%	Fri 25/8/23	Thu 7/9/23	Fri 25/8/23	Thu 7/9/23	0 days	0 days	758	763														
763	CON-3.8-54240	Sampling and Testing (CIF)	28 days	0 days	100%	Fri 8/9/23	Thu 5/10/23	Fri 8/9/23	Thu 5/10/23	0 days	0 days	762	768														
764	CON-3.8-54300	Excavation of Contaminated Soil	553 days	0 days	100%	Sun 2/4/23	Sat 5/10/24	Sun 2/4/23	Sat 5/10/24	0 days	0 days		Excavation of Contaminated Soil														
765	CON-3.8-54310	To Biopile (Site 3-8)	65 days	0 days	100%	Sun 2/4/23	Mon 5/6/23	Sun 2/4/23	Mon 5/6/23	0 days	0 days	757,761	769SS+14 days,1166SS+14 days														
766	CON-3.8-54320	To Stockpile for Cement Solidification (Site 3-8)	65 days	0 days	100%	Sun 2/4/23	Mon 5/6/23	Sun 2/4/23	Mon 5/6/23	0 days	0 days	757,761	770SS+14 days,1183SS+14 days														
767	CON-3.8-54330	To Biopile (Site 3-8 CIF)	15 days	0 days	100%	Sat 21/9/24	Sat 5/10/24	Sat 21/9/24	Sat 5/10/24	0 days	0 days	1163,743FS+39 days	1167,771,1154FS+150 days														
768	CON-3.8-54340	To Stockpile for Cement Solidification (Site 3-8)	15 days	0 days	100%	Fri 27/10/23	Fri 10/11/23	Fri 27/10/23	Fri 10/11/23	0 days	0 days	1177,758,763	1185SS+25 days,772FS+14 days														
769	CON-3.8-54400	Backfill to Formation for Biopile Location (Site 3-8)	65 days	0 days	100%	Sun 16/4/23	Mon 19/6/23	Sun 16/4/23	Mon 19/6/23	0 days	0 days	765SS+14 days	781														
770	CON-3.8-54500	Backfill to Formation for Cement Solidification Location (Site 3-8)	65 days	0 days	100%	Sun 16/4/23	Mon 19/6/23	Sun 16/4/23	Mon 19/6/23	0 days	0 days	766SS+14 days	781														
771	CON-3.8-54600	Backfill to Formation for Biopile Location (Site 3-8)	15 days	0 days	100%	Sun 6/10/24	Sun 20/10/24	Sun 6/10/24	Sun 20/10/24	0 days	0 days	767	780														
772	CON-3.8-54700	Backfill to Formation for Cement Solidification Location (Site 3-8 CIF)	15 days	0 days	100%	Sat 28/10/23	Sat 11/11/23	Sat 28/10/23	Sat 11/11/23	0 days	0 days	768FS-14 days	1273														
773	CON-3.8-60000	Site Formation	909 days	0 days	100%	Sat 1/10/22	Thu 27/3/25	Sat 1/10/22	Thu 27/3/25	0 days	0 days		Site Formation														
Task Critical Task Milestone Summary																											

Task Critical Task Milestone Summary

Page 17

*E=Excavator L=Lorry W=Worker D=Drill plant C=Crane Lorry R=Rotter

ID	Activity ID	Task Name	Duration	Remaining Duration	% Work Complete	Start	Finish	Late Start	Late Finish	Free Slack	Total Slack	Predecessors	Successors
817	CON-3.8-60250	Excavation to Formation and U-Channel (Site 3-8 Current Access to CIF)	8 days	0 days	100%	Wed 12/3/25	Wed 19/3/25	Wed 12/3/25	Wed 19/3/25	0 days	0 days	806	824
818	CON-3.8-60300	Concrete Access	60 days	0 days	100%	Mon 27/1/25	Thu 27/3/25	Mon 27/1/...	Thu 27/3/...	0 days	0 days		
819	CON-3.8-60330	Stairway above Formation Level	10 days	0 days	100%	Tue 18/3/25	Thu 27/3/25	Tue 18/3/25	Thu 27/3/...	0 days	0 days	811,810	824
820	CON-3.8-60340	Maintenance Access (Site 3-8 CIF)	30 days	0 days	100%	Mon 27/1/25	Tue 25/2/25	Mon 27/1/25	Tue 25/2/...	0 days	0 days	804SS+14 days	821,812FS-5 days,785SS+
821	CON-3.8-60360	Stairway above Formation Level (Site 3-8 CIF)	16 days	0 days	100%	Wed 12/3/25	Thu 27/3/25	Wed 12/3/...	Thu 27/3/...	0 days	0 days	815FS-3 days,820	824
822	CON-3.8-60370	Maintenance Access (Site 3-8 Current Kai Pak Ling Road)	20 days	0 days	100%	Sat 8/3/25	Thu 27/3/25	Sat 8/3/25	Thu 27/3/25	0 days	0 days	816	824
823	CON-3.8-60380	Maintenance Access (Site 3-8 Current Access)	16 days	0 days	100%	Wed 12/3/25	Thu 27/3/25	Wed 12/3/...	Thu 27/3/...	0 days	0 days	806	824
824	CON-3.8-70000	Planned Completion of Section 1A3	0 days	0 days	100%	Thu 27/3/25	Thu 27/3/25	Thu 27/3/25	Thu 27/3/...	0 days	0 days	819,821,804,814,815,122	
825		Section 1A4	1030 days	0 days	100%	Fri 28/1/22	Fri 22/11/24	Fri 28/1/22	Fri 22/11/...	0 days	0 days		
826		Site 2-18 (Portion B11)	1030 days	0 days	100%	Fri 28/1/22	Fri 22/11/24	Fri 28/1/22	Fri 22/11/...	0 days	0 days		
827	CON-2.18-10000	Site Clearance	5 days	0 days	100%	Fri 28/1/22	Tue 1/2/22	Fri 28/1/22	Tue 1/2/22	0 days	45	829,830,831,832,834,835,	
828	CON-2.18-20000	Establishment	28 days	0 days	100%	Wed 2/2/22	Tue 1/3/22	Wed 2/2/22	Tue 1/3/22	0 days	0 days		
829	CON-2.18-20100	Condition Survey for Existing Structures to be Demolished	28 days	0 days	100%	Wed 2/2/22	Tue 1/3/22	Wed 2/2/22	Tue 1/3/22	0 days	0 days	827	843
830	CON-2.18-20200	Tree Survey	28 days	0 days	100%	Wed 2/2/22	Tue 1/3/22	Wed 2/2/22	Tue 1/3/22	0 days	0 days	827	838,839
831	CON-2.18-20300	Initial Survey	28 days	0 days	100%	Wed 2/2/22	Tue 1/3/22	Wed 2/2/22	Tue 1/3/22	0 days	0 days	827	838,839
832	CON-2.18-20400	Site Haul Road	7 days	0 days	100%	Wed 2/2/22	Tue 8/2/22	Wed 2/2/22	Tue 8/2/22	0 days	0 days	827	838,839
833	CON-2.18-20500	Health & Hygiene Facilities	14 days	0 days	100%	Wed 2/2/22	Tue 15/2/22	Wed 2/2/22	Tue 15/2/...	0 days	0 days	827	838,839
834	CON-2.18-20600	Fence Work	14 days	0 days	100%	Wed 2/2/22	Tue 15/2/22	Wed 2/2/22	Tue 15/2/...	0 days	0 days	827	838,839,836
835	CON-2.18-20700	Underground Utilities Detection	14 days	0 days	100%	Wed 2/2/22	Tue 15/2/22	Wed 2/2/22	Tue 15/2/...	0 days	0 days	827	838,839
836	CON-2.18-20800	Install Monitoring Points	10 days	0 days	100%	Wed 16/2/22	Fri 25/2/22	Wed 16/2/...	Fri 25/2/22	0 days	0 days	834	849,850
837	CON-2.18-30000	Tree Treatment	298 days	0 days	100%	Wed 2/3/22	Sat 24/12/21	Wed 2/3/22	Sat 24/12/...	0 days	0 days		
838	CON-2.18-30100	Tree Felling (part 1)	16 days	0 days	100%	Wed 2/3/22	Thu 17/3/22	Wed 2/3/22	Thu 17/3/...	0 days	0 days	830,831,832,834,835,152	
839	CON-2.18-30200	Tree Protection (part 1)	16 days	0 days	100%	Wed 2/3/22	Thu 17/3/22	Wed 2/3/22	Thu 17/3/...	0 days	0 days	830,831,832,834,835,152	
840	CON-2.18-30300	Tree Felling (part 2)	71 days	0 days	100%	Sat 15/10/22	Sat 24/12/22	Sat 15/10/...	Sat 24/12/...	0 days	0 days	52FS+14 days	849,850,843
841	CON-2.18-30400	Tree Protection (part 2)	71 days	0 days	100%	Sat 15/10/22	Sat 24/12/22	Sat 15/10/...	Sat 24/12/...	0 days	0 days	52FS+14 days	843,849,850
842	CON-2.18-40000	Demolition work	85 days	0 days	100%	Sun 25/12/22	Sun 19/3/23	Sun 25/12/...	Sun 19/3/...	0 days	0 days		
843	CON-2.18-40100	Demolition of Existing Structures	85 days	0 days	100%	Sun 25/12/22	Sun 19/3/23	Sun 25/12/...	Sun 19/3/...	0 days	0 days	829,397,400,841,840	861,867,868
844	CON-2.18-50000	Decontamination (include Road L54, remediation of contaminated soil carried out at Detention Pond)	437 days	0 days	100%	Fri 29/4/22	Sun 9/7/23	Fri 29/4/22	Sun 9/7/23	0 days	0 days		
845	CON-2.18-51000	CAP	55 days	0 days	100%	Fri 29/4/22	Wed 22/6/22	Fri 29/4/22	Wed 22/6/...	0 days	0 days		
846	CON-2.18-51100	Site Appraisal& Preparation of CAP	8 days	0 days	100%	Fri 29/4/22	Fri 6/5/22	Fri 29/4/22	Fri 6/5/22	0 days	0 days	847,925SS,293SS	
847	CON-2.18-51200	Submission& Endorsement by EPD	28 days	0 days	100%	Thu 26/5/22	Wed 22/6/22	Thu 26/5/22	Wed 22/6/...	0 days	0 days	846,294FF	849,850
848	CON-2.18-52000	Ground Investigation (Trial Pit / Borehole)	21 days	0 days	100%	Sat 10/12/22	Fri 30/12/22	Sat 10/12/...	Fri 30/12/...	0 days	0 days		
849	CON-2.18-52100	Trial Pit Sampling& Testing	21 days	0 days	100%	Sat 10/12/22	Fri 30/12/22	Sat 10/12/...	Fri 30/12/...	0 days	0 days	836,393,847,841,840	852,296,299
850	CON-2.18-52200	Inspection Pit for installing Groundwater Wells	21 days	0 days	100%	Sat 10/12/22	Fri 30/12/22	Sat 10/12/...	Fri 30/12/...	0 days	0 days	836,847,841,840	852
851	CON-2.18-53000	CAR & RAP Submission	36 days	0 days	100%	Sat 31/12/22	Fri 3/2/23	Sat 31/12/...	Fri 3/2/23	0 days	0 days		
852	CON-2.18-53100	Preparation of CAR& rap	7 days	0 days	100%	Sat 31/12/22	Fri 6/1/23	Sat 31/12/...	Fri 6/1/23	0 days	0 days	850,849	853
853	CON-2.18-53200	Review and Accepted by EPD	28 days	0 days	100%	Sat 7/1/23	Fri 3/2/23	Sat 7/1/23	Fri 3/2/23	0 days	0 days	852	856
854	CON-2.18-54000	Decontamination Works	131 days	0 days	100%	Wed 1/3/23	Sun 9/7/23	Wed 1/3/23	Sun 9/7/23	0 days	0 days		
855	CON-2.18-54100	Treatability Test for Heavy Metal	24 days	0 days	100%	Wed 1/3/23	Fri 24/3/23	Wed 1/3/23	Fri 24/3/23	0 days	0 days		
856	CON-2.18-54110	Treatability Test for Heavy Metal	24 days	0 days	100%	Wed 1/3/23	Fri 24/3/23	Wed 1/3/23	Fri 24/3/23	0 days	0 days	853	858
857	CON-2.18-54200	Confirmation Test Sampling and Testing	28 days	0 days	100%	Sat 25/3/23	Fri 21/4/23	Sat 25/3/23	Fri 21/4/23	0 days	0 days		
858	CON-2.18-54210	Trial Pit	14 days	0 days	100%	Sat 25/3/23	Fri 7/4/23	Sat 25/3/23	Fri 7/4/23	0 days	0 days	856	859
859	CON-2.18-54220	Sampling and Testing	14 days	0 days	100%	Sat 8/4/23	Fri 21/4/23	Sat 8/4/23	Fri 21/4/23	0 days	0 days	858	861,862
860	CON-2.18-54300	Excavation of Contaminated Soil	70 days	0 days	100%	Sat 22/4/23	Fri 30/6/23	Sat 22/4/23	Fri 30/6/23	0 days	0 days		
861	CON-2.18-54310	To Biopile	70 days	0 days	100%	Sat 22/4/23	Fri 30/6/23	Sat 22/4/23	Fri 30/6/23	0 days	0 days	859,135,765SS,843	863SS+14 days,862SS,119
862	CON-2.18-54320	To Stockpile for Cement Solidification	70 days	0 days	100%	Sat 22/4/23	Fri 30/6/23	Sat 22/4/23	Fri 30/6/23	0 days	0 days	859,135,861SS	864SS+14 days,1179SS+6
863	CON-2.18-54400	Backfilling to Formation of Biopile Location	65 days	0 days	100%	Sat 6/5/23	Sun 9/7/23	Sat 6/5/23	Sun 9/7/23	0 days	0 days	861SS+14 days	935SS,867SS,868SS
864	CON-2.18-54500	Backfilling to Formation of Cement Solidification Location	65 days	0 days	100%	Sat 6/5/23	Sun 9/7/23	Sat 6/5/23	Sun 9/7/23	0 days	0 days	862SS+14 days	869
865	CON-2.18-60000	Site formation (include Road L53 and L54 adjacent to site 2-18)	509 days	0 days	100%	Sat 6/5/23	Wed 25/9/24	Sat 6/5/23	Wed 25/9/24	0 days	0 days		

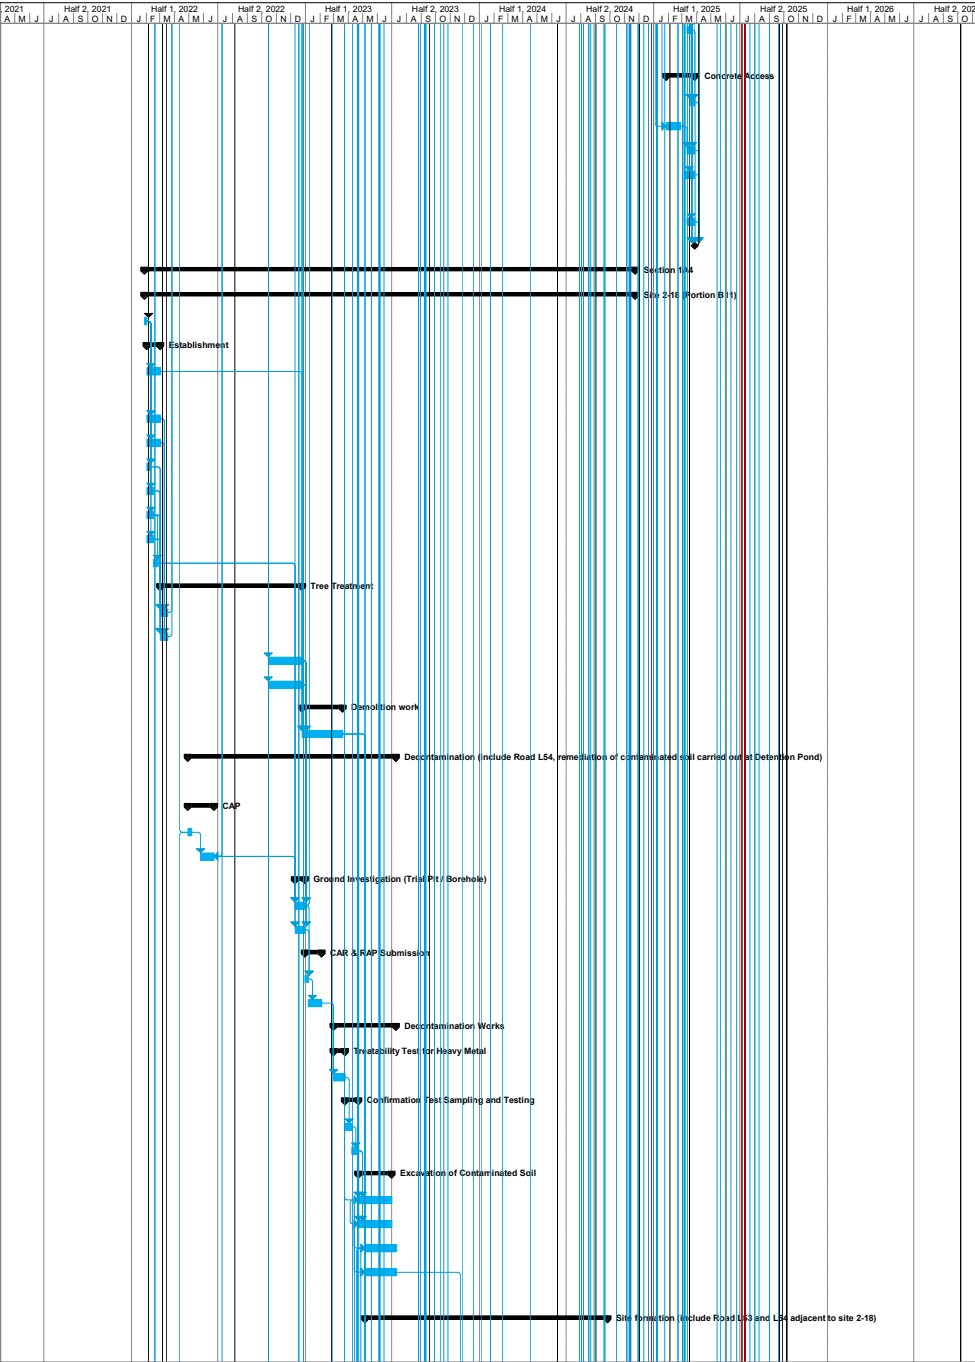

Activity ID	Task Name	Duration	Remaining Duration	% Work Complete	Start	Finish	Late Start	Late Finish	Free Slack	Total Slack	Predecessors	Successors	2021	Half 2, 2021	Half 1, 2022	Half 2, 2022	Half 1, 2023	Half 2, 2023	Half 1, 2024	Half 2, 2024	Half 1, 2025	Half 2, 2025	Half 1, 2026	Half 2, 2026
866	CON-2.18-60100	Earthwork	496 days	0 days	100%	Sat 6/5/23	Thu 12/9/24	Sat 6/5/23	Thu 12/9/24	0 days	0 days													
867	CON-2.18-60110	Breaking of Loading Bay Concrete Pavement	200 days	0 days	100%	Sat 6/5/23	Tue 21/11/23	Sat 6/5/23	Tue 21/1/24	0 days	0 days	429,843,863SS	869											
868	CON-2.18-60111	Breaking of Carpark Pavement and Decompo	200 days	0 days	100%	Sat 6/5/23	Tue 21/11/23	Sat 6/5/23	Tue 21/1/24	0 days	0 days	429,843,863SS	869,989SS+27 days											
869	CON-2.18-60120	Backfilling & Compaction to Formation +7.5mPD Portion 1 (South and East Portion of no retaining wall structure)	90 days	0 days	100%	Wed 22/11/23	Mon 19/2/24	Wed 22/11/23	Mon 19/2/24	0 days	0 days	864,868,867,871FF	875SS+14 days,883SS+40 days,886,890,990											
870	CON-2.18-60121	Backfilling & Compaction to Formation +7.5mPD Portion 2 (North and East Portion that backfilling after retaining wall structure completed)	90 days	0 days	100%	Sat 1/6/24	Thu 29/8/24	Sat 1/6/24	Thu 29/8/24	0 days	0 days	890	888FS-30 days,872,879SS-14 days											
871	CON-2.18-60130	Treatment of Contaminated Underground Wa	45 days	0 days	100%	Mon 25/9/23	Wed 8/11/23	Mon 25/9/23	Wed 8/11/24	0 days	0 days		869FF											
872	CON-2.18-60150	Trimming for Fill Slope	21 days	0 days	100%	Fri 23/8/24	Thu 12/9/24	Fri 23/8/24	Thu 12/9/24	0 days	0 days	870,877	895,1015FS+4 days											
873	CON-2.18-60200	Surface Drainage	261 days	0 days	100%	Wed 6/12/23	Thu 22/8/24	Wed 6/12/23	Thu 22/8/24	0 days	0 days													
874	CON-2.18-60210	At Slope Toe +4.6mPD	261 days	0 days	100%	Wed 6/12/23	Thu 22/8/24	Wed 6/12/23	Thu 22/8/24	0 days	0 days													
875	CON-2.18-60211	Excavation to Formation	200 days	0 days	100%	Wed 6/12/23	Sat 22/6/24	Wed 6/12/23	Sat 22/6/24	0 days	0 days	869SS+14 days	876SS+7 days,895											
876	CON-2.18-60212	Catchpit	200 days	0 days	100%	Wed 13/12/23	Sat 29/6/24	Wed 13/1/24	Sat 29/6/24	0 days	0 days	875SS+7 days	877SS+14 days,895											
877	CON-2.18-60213	U-channel	240 days	0 days	100%	Wed 27/12/23	Thu 22/8/24	Wed 27/1/24	Thu 22/8/24	0 days	0 days	876SS+14 days	895,872											
878	CON-2.18-60220	At Slope Crest +7.5mPD	91 days	0 days	100%	Sat 18/5/24	Fri 16/8/24	Sat 18/5/24	Fri 16/8/24	0 days	0 days													
879	CON-2.18-60221	Excavation to Formation	60 days	0 days	100%	Sat 18/5/24	Tue 16/7/24	Sat 18/5/24	Tue 16/7/24	0 days	0 days	870SS-14 days	880SS+7 days,895											
880	CON-2.18-60222	Catchpit	60 days	0 days	100%	Sat 25/5/24	Tue 23/7/24	Sat 25/5/24	Tue 23/7/24	0 days	0 days	879SS+7 days	881SS+14 days,895											
881	CON-2.18-60223	U-channel	70 days	0 days	100%	Sat 8/6/24	Fri 16/8/24	Sat 8/6/24	Fri 16/8/24	0 days	0 days	880SS+14 days	895,892											
882	CON-2.18-60230	At +7.5mPD Platform	211 days	0 days	100%	Mon 1/1/24	Mon 29/7/24	Mon 1/1/24	Mon 29/7/24	0 days	0 days													
883	CON-2.18-60231	Excavation to Formation	155 days	0 days	100%	Mon 1/1/24	Mon 3/6/24	Mon 1/1/24	Mon 3/6/24	0 days	0 days	869SS+40 days	884SS+14 days,895											
884	CON-2.18-60232	Catchpit	155 days	0 days	100%	Mon 15/1/24	Mon 17/6/24	Mon 15/1/24	Mon 17/6/24	0 days	0 days	883SS+14 days	885SS+20 days,895											
885	CON-2.18-60233	U-channel	177 days	0 days	100%	Sun 4/2/24	Mon 29/7/24	Sun 4/2/24	Mon 29/7/24	0 days	0 days	884SS+20 days	895,886SS+100 days,893											
886	CON-2.18-60300	Drainage Work at +7.5mPD Platform	80 days	0 days	100%	Tue 14/5/24	Thu 1/8/24	Tue 14/5/24	Thu 1/8/24	0 days	0 days	885SS+100 days,869	887SS+30 days,895											
887	CON-2.18-60400	Sewer Work at +7.5mPD Platform	90 days	0 days	100%	Thu 13/6/24	Tue 10/9/24	Thu 13/6/24	Tue 10/9/24	0 days	0 days	886SS+30 days,346	888SS+40 days,895											
888	CON-2.18-60500	Waterwork at +7.5mPD Platform	57 days	0 days	100%	Wed 31/7/24	Wed 25/9/24	Wed 31/7/24	Wed 25/9/24	0 days	0 days	870FS-30 days,887SS	895,892FS-10 days,891FF											
889	CON-2.18-70000	Additional Works	235 days	0 days	100%	Tue 2/4/24	Fri 22/11/24	Tue 2/4/24	Fri 22/11/24	0 days	0 days													
890	CON-2.18-70100	Retaining Wall Structures (PMI 084, PMI 088)	60 days	0 days	100%	Tue 2/4/24	Fri 31/5/24	Tue 2/4/24	Fri 31/5/24	0 days	0 days	869	870											
891	CON-2.18-70450	Laying CLP Cable Duct for future Connection PMI 206, PMI 207)	40 days	0 days	100%	Sat 17/8/24	Wed 25/9/24	Sat 17/8/24	Wed 25/9/24	0 days	0 days	888FF	892FS-10 days											
892	CON-2.18-70500	Concrete Pavement for Footpath (PMI 129,223)	50 days	0 days	100%	Mon 16/9/24	Mon 4/11/24	Mon 16/9/24	Mon 4/11/24	0 days	0 days	881,888FS-10 days,85	895,894,1029FS+100 days											
893	CON-2.18-70550	Concrete Pavement for EVA (PMI 128,223)	58 days	0 days	100%	Thu 26/9/24	Fri 22/11/24	Thu 26/9/24	Fri 22/11/24	0 days	0 days	885,888	895,1025											
894	CON-2.18-70800	Public Lighting (PMI 112)	18 days	0 days	100%	Tue 5/11/24	Fri 22/11/24	Tue 5/11/24	Fri 22/11/24	0 days	0 days	892,249	895											
895	CON-2.18-90000	Planned Completion of Section 1A4	0 days	0 days	100%	Fri 22/11/24	Fri 22/11/24	Fri 22/11/24	Fri 22/11/24	0 days	0 days	877,888,881,885,894,123,1080												
896		Section 1A5	939 days	0 days	100%	Fri 29/4/22	Fri 22/11/24	Fri 29/4/22	Fri 22/11/24	0 days	0 days													
897		Site 2-19 (Portion A5,B10)	939 days	0 days	100%	Fri 29/4/22	Fri 22/11/24	Fri 29/4/22	Fri 22/11/24	0 days	0 days													
898	CON-2.19-10000	Site Clearance	8 days	0 days	100%	Sat 15/10/23	Sat 22/10/23	Sat 15/10/23	Sat 22/10/23	0 days	0 days													
899	CON-2.19-10100	Site Clearance for Portion A5	8 days	0 days	100%	Sat 15/10/23	Sat 22/10/23	Sat 15/10/23	Sat 22/10/23	0 days	0 days	44,52FS+14 days	902,904,906,908,910,911,913											
900	CON-2.19-10200	Site Clearance for Portion B10	8 days	0 days	100%	Sat 15/10/23	Sat 22/10/23	Sat 15/10/23	Sat 22/10/23	0 days	0 days	44,52FS+14 days	903,905,907,909,912,914											
901	CON-2.19-20000	Establishment	56 days	0 days	100%	Sun 23/10/23	Sat 17/12/23	Sun 23/10/23	Sat 17/12/23	0 days	0 days													
902	CON-2.19-20100	Condition Survey for Existing Structures to be Demolished for Portion A5	28 days	0 days	100%	Sun 23/10/22	Sat 19/11/22	Sun 23/10/22	Sat 19/11/22	0 days	0 days	899	903											
903	CON-2.19-20200	Condition Survey for Existing Structures to be Demolished for Portion B10	28 days	0 days	100%	Sun 20/11/22	Sat 17/12/22	Sun 20/11/22	Sat 17/12/22	0 days	0 days	900,902	922											
904	CON-2.19-20300	Tree Survey for Portion A5	28 days	0 days	100%	Sun 23/10/23	Sat 19/11/23	Sun 23/10/23	Sat 19/11/23	0 days	0 days	899	917,919											
905	CON-2.19-20400	Tree Survey for Portion B10	28 days	0 days	100%	Sun 23/10/23	Sat 19/11/23	Sun 23/10/23	Sat 19/11/23	0 days	0 days	900	918,920											
906	CON-2.19-20500	Initial Survey for Portion A5	28 days	0 days	100%	Sun 23/10/23	Sat 19/11/23	Sun 23/10/23	Sat 19/11/23	0 days	0 days	899	917,919											
907	CON-2.19-20600	Initial Survey for Portion B10	28 days	0 days	100%	Sun 23/10/23	Sat 19/11/23	Sun 23/10/23	Sat 19/11/23	0 days	0 days	900	918,920											
908	CON-2.19-20700	Site Haul Road for Portion A5	28 days	0 days	100%	Sun 23/10/23	Sat 19/11/23	Sun 23/10/23	Sat 19/11/23	0 days	0 days	899	917,919											
909	CON-2.19-20800	Site Haul Road for Portion B10	28 days	0 days	100%	Sun 23/10/23	Sat 19/11/23	Sun 23/10/23	Sat 19/11/23	0 days	0 days	900	918,920											
910	CON-2.19-20900	Health & Hygiene Facilities	7 days	0 days	100%	Sun 23/10/23	Sat 29/10/23	Sun 23/10/23	Sat 29/10/23	0 days	0 days	899	917,919											
911	CON-2.19-21000	Fence Work & Gate for Portion A5	28 days	0 days	100%	Sun 23/10/23	Sat 19/11/23	Sun 23/10/23	Sat 19/11/23	0 days	0 days	899	917,919											
912	CON-2.19-21100	Fence Work for Portion B10	28 days	0 days	100%	Sun 23/10/23	Sat 19/11/23	Sun 23/10/23	Sat 19/11/23	0 days	0 days	900	918,915,920											
913	CON-2.19-21200	Underground Utilities Detection for Portion A5	28 days	0 days	100%	Sun 23/10/23	Sat 19/11/23	Sun 23/10/23	Sat 19/11/23	0 days	0 days	899	917,919											

ID	Activity ID	Task Name	Duration	Remaining Duration	% Work Complete	Start	Finish	Late Start	Late Finish	Free Slack	Total Slack	Predecessors	Successors	2021	Half 2, 2021	Half 1, 2022	Half 2, 2022	Half 1, 2023	Half 2, 2023	Half 1, 2024	Half 2, 2024	Half 1, 2025	Half 2, 2025	Half 1, 2026	Half 2, 2026
914	CON-2.19-21300	Underground Utilities Detection for Portion B10	28 days	0 days	100%	Sun 23/10/23	Sat 19/11/23	Sun 23/10/23	Sat 19/11/23	0 days	0 days	900	918,920												
915	CON-2.19-21400	Install Monitoring Points	10 days	0 days	100%	Sun 20/11/23	Tue 29/11/23	Sun 20/11/23	Tue 29/11/23	0 days	0 days	912	928,929												
916	CON-2.19-30000	Tree Treatment	56 days	0 days	100%	Sun 6/11/23	Sat 31/12/23	Sun 6/11/23	Sat 31/12/23	0 days	0 days														
917	CON-2.19-30100	Tree Felling for Portion A5	28 days	0 days	100%	Sun 20/11/23	Sat 17/12/23	Sun 20/11/23	Sat 17/12/23	0 days	0 days	904,906,908,910,911,918													
918	CON-2.19-30200	Tree Felling for Portion B10	28 days	0 days	100%	Sun 4/12/23	Sat 31/12/23	Sun 4/12/23	Sat 31/12/23	0 days	0 days	905,907,909,912,914,928,929													
919	CON-2.19-30300	Tree Protection for Portion A5	28 days	0 days	100%	Sun 6/11/23	Sat 3/12/22	Sun 6/11/23	Sat 3/12/22	0 days	0 days	904,906,908,910,911,920													
920	CON-2.19-30400	Tree Protection for Portion B10	28 days	0 days	100%	Sun 4/12/23	Sat 31/12/23	Sun 4/12/23	Sat 31/12/23	0 days	0 days	905,907,909,912,914,929													
921	CON-2.19-40000	Demolition work	85 days	0 days	100%	Sun 18/12/23	Sun 12/3/23	Sun 18/12/23	Sun 12/3/23	0 days	0 days														
922	CON-2.19-40100	Demolition of Existing Structures	85 days	0 days	100%	Sun 18/12/23	Sun 12/3/23	Sun 18/12/23	Sun 12/3/23	0 days	0 days	903,997,400	928,929,935												
923	CON-2.19-50000	Decontamination (Remediation of contaminated soil carried out at Detention Pond)	385 days	0 days	100%	Fri 29/4/22	Thu 18/5/23	Fri 29/4/22	Thu 18/5/23	0 days	0 days														
924	CON-2.19-51000	CAP	55 days	0 days	100%	Fri 29/4/22	Wed 22/6/22	Fri 29/4/22	Wed 22/6/22	0 days	0 days														
925	CON-2.19-51100	Site Appraisal for Portion B10& Preparation of	25 days	0 days	100%	Fri 29/4/22	Mon 23/5/22	Fri 29/4/22	Mon 23/5/22	0 days	0 days	846SS	926												
926	CON-2.19-51200	Submission& Endorsement by EPD	30 days	0 days	100%	Tue 24/5/22	Wed 22/6/22	Tue 24/5/22	Wed 22/6/22	0 days	0 days	925,294FF	928,929												
927	CON-2.19-52000	Ground Investigation (Trial Pit / Borehole)	40 days	0 days	100%	Sun 26/2/23	Thu 6/4/23	Sun 26/2/23	Thu 6/4/23	0 days	0 days														
928	CON-2.19-52100	Trial Pit Sampling& Testing	40 days	0 days	100%	Sun 26/2/23	Thu 6/4/23	Sun 26/2/23	Thu 6/4/23	0 days	0 days	922,393,915,918,926	931												
929	CON-2.19-52200	Inspection Pit for installing Groundwater Wells	40 days	0 days	100%	Sun 26/2/23	Thu 6/4/23	Sun 26/2/23	Thu 6/4/23	0 days	0 days	922,915,918,926,920	931												
930	CON-2.19-53000	CAR & RAP Submission	42 days	0 days	100%	Fri 7/4/23	Thu 18/5/23	Fri 7/4/23	Thu 18/5/23	0 days	0 days														
931	CON-2.19-53100	Preparation of CAR& RAP	14 days	0 days	100%	Fri 7/4/23	Thu 20/4/23	Fri 7/4/23	Thu 20/4/23	0 days	0 days	929,928	932												
932	CON-2.19-53200	Review& Accepted by EPD	28 days	0 days	100%	Fri 21/4/23	Thu 18/5/23	Fri 21/4/23	Thu 18/5/23	0 days	0 days	931	935												
933	CON-2.19-60000	Site Formation (include Road L53 and L54 adjacent to site 2-19)	529 days	0 days	100%	Sat 20/5/23	Tue 29/10/24	Sat 20/5/23	Tue 29/10/24	0 days	0 days														
934	CON-2.19-60100	Earthwork	488 days	0 days	100%	Sat 20/5/23	Wed 18/9/24	Sat 20/5/23	Wed 18/9/24	0 days	0 days														
935	CON-2.19-60110	Excavation to Formation of retaining wall EM3, EM4 and EM5 at platform +11.0mPD	15 days	0 days	100%	Sat 20/5/23	Sat 3/6/23	Sat 20/5/23	Sat 3/6/23	0 days	0 days	429,863SS,922,932	936SS,944												
936	CON-2.19-60120	Backfilling & Compaction to Formation (Contamination Area)	40 days	0 days	100%	Sat 20/5/23	Wed 28/6/23	Sat 20/5/23	Wed 28/6/23	0 days	0 days	935SS													
937	CON-2.19-60130	Backfilling & Compaction for +11.0mPD platfo	75 days	0 days	100%	Thu 2/5/24	Mon 15/7/24	Thu 2/5/24	Mon 15/7/24	0 days	0 days	946	949,939FS-30 days,953												
938	CON-2.19-60140	Excavation to Formation of EM2, IL2 and EM5 at platform +9.5mPD	15 days	0 days	100%	Wed 23/8/23	Wed 6/9/23	Wed 23/8/23	Wed 6/9/23	0 days	0 days	944	945												
939	CON-2.19-60150	Backfilling & Compaction for +9.50mPD platfo	60 days	0 days	100%	Sun 16/6/24	Wed 14/8/24	Sun 16/6/24	Wed 14/8/24	0 days	0 days	937FS-30 days	941FS-10 days,957,986												
940	CON-2.19-60160	Excavation to Formation of EM1, IL1, EL1 and EM5 at +7.5mPD platform	15 days	0 days	100%	Mon 25/12/23	Mon 8/1/24	Mon 25/12/23	Mon 8/1/24	0 days	0 days	945	946												
941	CON-2.19-60170	Backfilling & Compaction for +7.5m Platform	30 days	0 days	100%	Mon 5/8/24	Tue 3/9/24	Mon 5/8/24	Tue 3/9/24	0 days	0 days	939FS-10 days	942,961												
942	CON-2.19-60180	Cut Slope	15 days	0 days	100%	Wed 4/9/24	Wed 18/9/24	Wed 4/9/24	Wed 18/9/24	0 days	0 days	941	986												
943	CON-2.19-60200	Retaining Wall	333 days	0 days	100%	Sun 4/6/23	Wed 1/5/24	Sun 4/6/23	Wed 1/5/24	0 days	0 days														
944	CON-2.19-60210	Retaining wall EM3, EM4, and EM5 at Platform +11.0mPD	80 days	0 days	100%	Sun 4/6/23	Tue 22/8/23	Sun 4/6/23	Tue 22/8/23	0 days	0 days	935,420	938												
945	CON-2.19-60220	Retaining wall EM2, IL2 and EM5 at platform +	109 days	0 days	100%	Thu 7/9/23	Sun 24/12/23	Thu 7/9/23	Sun 24/12/23	0 days	0 days	938	1041,940												
946	CON-2.19-60230	Retaining wall EM1, EL1 and EM5 at platform +	114 days	0 days	100%	Tue 9/1/24	Wed 1/5/24	Tue 9/1/24	Wed 1/5/24	0 days	0 days	940	937,965												
947	CON-2.19-60300	Surface Drainage (U-channel)	106 days	0 days	100%	Tue 16/7/24	Tue 29/10/24	Tue 16/7/24	Tue 29/10/24	0 days	0 days														
948	CON-2.19-60310	At Slope Crest +12.14mPD	45 days	0 days	100%	Tue 16/7/24	Thu 29/8/24	Tue 16/7/24	Thu 29/8/24	0 days	0 days														
949	CON-2.19-60311	Excavation to Formation	15 days	0 days	100%	Tue 16/7/24	Tue 30/7/24	Tue 16/7/24	Tue 30/7/24	0 days	0 days	937	950												
950	CON-2.19-60312	Catchpit	15 days	0 days	100%	Wed 31/7/24	Wed 14/8/24	Wed 31/7/24	Wed 14/8/24	0 days	0 days	949	951												
951	CON-2.19-60313	U-channel	15 days	0 days	100%	Thu 15/8/24	Thu 29/8/24	Thu 15/8/24	Thu 29/8/24	0 days	0 days	950	965												
952	CON-2.19-60320	At Platform +11.0mPD	48 days	0 days	100%	Tue 16/7/24	Sun 1/9/24	Tue 16/7/24	Sun 1/9/24	0 days	0 days														
953	CON-2.19-60321	Excavation to Formation	30 days	0 days	100%	Tue 16/7/24	Wed 14/8/24	Tue 16/7/24	Wed 14/8/24	0 days	0 days	937	954SS+9 days												
954	CON-2.19-60322	Catchpit	30 days	0 days	100%	Thu 25/7/24	Fri 23/8/24	Thu 25/7/24	Fri 23/8/24	0 days	0 days	953SS+9 days	955SS+9 days												
955	CON-2.19-60323	U-channel	30 days	0 days	100%	Sat 3/8/24	Sun 1/9/24	Sat 3/8/24	Sun 1/9/24	0 days	0 days	954SS+9 days	969FS-10 days,981												
956	CON-2.19-60330	At Platform +9.5mPD	46 days	0 days	100%	Thu 15/8/24	Sun 29/9/24	Thu 15/8/24	Sun 29/9/24	0 days	0 days														
957	CON-2.19-60331	Excavation to Formation	26 days	0 days	100%	Thu 15/8/24	Mon 9/9/24	Thu 15/8/24	Mon 9/9/24	0 days	0 days	939	958SS+10 days,986												
958	CON-2.19-60332	Catchpit	26 days	0 days	100%	Sun 25/8/24	Thu 19/9/24	Sun 25/8/24	Thu 19/9/24	0 days	0 days	957SS+10 days	959SS+10 days,986												
959	CON-2.19-60333	U-channel	26 days	0 days	100%	Wed 4/9/24	Sun 29/9/24	Wed 4/9/24	Sun 29/9/24	0 days	0 days	958SS+10 days	970FS-10 days,982												
960	CON-2.19-60340	At Platform +7.5mPD	32 days	0 days	100%	Wed 4/9/24	Sat 5/10/24	Wed 4/9/24	Sat 5/10/24	0 days	0 days														
961	CON-2.19-60341	Excavation to Formation	14 days	0 days	100%	Wed 4/9/24	Tue 17/9/24	Wed 4/9/24	Tue 17/9/24	0 days	0 days	941	962SS+9 days,986												

Contract No. YL/2020/03 Hung Shui Kiu/Ha Tsuen New Development Area Stage 1 Works - Site Formation and Engineering Infrastructure														Revised Programme Rev.13 (May 2025)																																																													
ID	Activity ID	Task Name	Duration	Remaining Duration	% Work Complete	Start	Finish	Late Start	Late Finish	Free Slack	Total Slack	Predecessors	Successors	2021	Half 2, 2021	Half 1, 2022	Half 2, 2022	Half 1, 2023	Half 2, 2023	Half 1, 2024	Half 2, 2024	Half 1, 2025	Half 2, 2025	Half 1, 2026	Half 2, 2026																																																		
962	CON-2.19-60342	Catchpit	14 days	0 days	100%	Fri 13/9/24	Thu 26/9/24	Fri 13/9/24	Thu 26/9/...	0 days	0 days	961SS+9 days	963SS+9 days,966																																																														
963	CON-2.19-60343	U-channel	14 days	0 days	100%	Sun 22/9/24	Sat 5/10/24	Sun 22/9/24	Sat 5/10/24	0 days	0 days	962SS+9 days	971FS-10 days,983																																																														
964	CON-2.19-60350	Boundary U-Channel	61 days	0 days	100%	Fri 30/8/24	Tue 29/10/24	Fri 30/8/24	Tue 29/10/...	0 days	0 days																																																																
965	CON-2.19-60351	Excavation to Formation	20 days	0 days	100%	Fri 30/8/24	Wed 18/9/24	Fri 30/8/24	Wed 18/9/...	0 days	0 days	946,951	966																																																														
966	CON-2.19-60352	Catchpit	20 days	0 days	100%	Thu 19/9/24	Tue 8/10/24	Thu 19/9/24	Tue 8/10/...	0 days	0 days	965	967																																																														
967	CON-2.19-60353	U-channel	21 days	0 days	100%	Wed 9/10/24	Tue 29/10/24	Wed 9/10/...	Tue 29/10/...	0 days	0 days	966	986																																																														
968	CON-2.19-60400	Drainage Work within Village	45 days	0 days	100%	Fri 23/8/24	Sun 6/10/24	Fri 23/8/24	Sun 6/10/...	0 days	0 days																																																																
969	CON-2.19-60410	Drainage Work at Platform +11.0mPD	20 days	0 days	100%	Fri 23/8/24	Wed 11/9/24	Fri 23/8/24	Wed 11/9/...	0 days	0 days	955FS-10 days	973SS+10 days,981																																																														
970	CON-2.19-60420	Drainage Work at Platform +9.5mPD	15 days	0 days	100%	Fri 20/9/24	Fri 4/10/24	Fri 20/9/24	Fri 4/10/24	0 days	0 days	959FS-10 days	974SS+10 days,982																																																														
971	CON-2.19-60430	Drainage Work at Platform +7.5mPD	11 days	0 days	100%	Thu 26/9/24	Sun 6/10/24	Thu 26/9/24	Sun 6/10/...	0 days	0 days	963FS-10 days	975SS+10 days,984,1041F																																																														
972	CON-2.19-60500	Sewer Work within Village	45 days	0 days	100%	Mon 2/9/24	Wed 16/10/24	Mon 2/9/24	Wed 16/10/...	0 days	0 days																																																																
973	CON-2.19-60510	Sewer Work at Platform +11.0mPD	14 days	0 days	100%	Mon 2/9/24	Sun 15/9/24	Mon 2/9/24	Sun 15/9/...	0 days	0 days	969SS+10 days	977SS+13 days,981																																																														
974	CON-2.19-60520	Sewer Work at Platform +9.5mPD	11 days	0 days	100%	Mon 30/9/24	Thu 10/10/24	Mon 30/9/24	Thu 10/10/...	0 days	0 days	970SS+10 days	978SS+7 days,982																																																														
975	CON-2.19-60530	Sewer Work at Platform +7.5mPD	11 days	0 days	100%	Sun 6/10/24	Wed 16/10/24	Sun 6/10/24	Wed 16/10/...	0 days	0 days	971SS+10 days	979SS+8 days,983																																																														
976	CON-2.19-60600	Waterwork within Village	43 days	0 days	100%	Sun 15/9/24	Mon 27/10/24	Sun 15/9/24	Sun 27/10/...	0 days	0 days																																																																
977	CON-2.19-60610	Waterwork at Platform +11.0mPD	16 days	0 days	100%	Sun 15/9/24	Mon 30/9/24	Sun 15/9/24	Mon 30/9/...	0 days	0 days	973SS+13 days	978,981																																																														
978	CON-2.19-60620	Waterwork at Platform +9.5mPD	12 days	0 days	100%	Mon 7/10/24	Fri 18/10/24	Mon 7/10/24	Fri 18/10/...	0 days	0 days	974SS+7 days,977	979,982																																																														
979	CON-2.19-60630	Waterwork at Platform +7.5mPD	14 days	0 days	100%	Mon 14/10/24	Sun 27/10/24	Mon 14/10/...	Sun 27/10/...	0 days	0 days	975SS+8 days,978	986,984,983																																																														
980	CON-2.19-70000	Additional Works	53 days	0 days	100%	Tue 1/10/24	Fri 22/11/24	Tue 1/10/24	Fri 22/11/...	0 days	0 days																																																																
981	CON-2.19-70110	Concrete Pavement for Footpath at Platform +11.0mPD (PMI 127,223)	14 days	0 days	100%	Tue 1/10/24	Mon 14/10/24	Tue 1/10/24	Mon 14/10/24	0 days	0 days	955,977,973,969	985,982																																																														
982	CON-2.19-70120	Concrete Pavement for Footpath at Platform +9.5mPD (PMI 127,223)	12 days	0 days	100%	Sat 19/10/24	Wed 30/10/24	Sat 19/10/24	Wed 30/10/24	0 days	0 days	959,978,981,974,970	985,983																																																														
983	CON-2.19-70130	Concrete Pavement for Footpath at Platform +7.5mPD (PMI 127,223)	14 days	0 days	100%	Thu 31/10/24	Wed 13/11/24	Thu 31/10/24	Wed 13/11/24	0 days	0 days	963,979,982,975	986,985,1033FS+90 days																																																														
984	CON-2.19-70200	Hydroseeding at Village House (PMI 096) (omitted)	0 days	0 days	100%	Sun 27/10/24	Sun 27/10/24	Sun 27/10/24	Sun 27/10/...	0 days	0 days	979,971	986																																																														
985	CON-2.19-70500	Public Lighting (PMI 112)	9 days	0 days	100%	Thu 14/11/24	Fri 22/11/24	Thu 14/11/...	Fri 22/11/...	0 days	0 days	983,981,982,249	986																																																														
986	CON-2.19-90000	Planned Completion of Section 1A5	0 days	0 days	100%	Fri 22/11/24	Fri 22/11/24	Fri 22/11/24	Fri 22/11/...	0 days	0 days	967,979,985,984,983,124,1080																																																															
987		Section 1A6	892 days	218.72 d...	89%	Thu 20/4/23	Sat 27/9/25	Thu 20/4/23	Mon 28/9/...	366 days	366 days																																																																
988	CON-1A6-10000	Road L54 (Site formation works refer to Section 1A4 and Section 1A5)	768 days	189.7 days	0%	Fri 4/8/23	Tue 9/9/25	Fri 4/8/23	Mon 28/9/26	384 days	384 days																																																																
989	CON-1A6-10100	Drainage Work (manhole 6nos)	55 days	0 days	100%	Wed 30/8/24	Mon 23/10/24	Wed 30/8/...	Mon 23/10/...	0 days	0 days	478,163,407,868SS+2991SS+30 days,990																																																															
990	CON-1A6-10110	Drainage Work (manhole 8nos)	45 days	0 days	100%	Tue 20/2/24	Thu 4/4/24	Tue 20/2/24	Thu 4/4/24	0 days	0 days	994,993,989,869	997																																																														
991	CON-1A6-10200	Sewer Work (manhole 2nos)	55 days	0 days	100%	Fri 29/9/23	Wed 22/11/24	Fri 29/9/23	Wed 22/11/...	0 days	0 days	989SS+30 days,410	992																																																														
992	CON-1A6-10210	Sewer Work (manhole 1nos)	20 days	0 days	100%	Mon 22/4/24	Sat 11/5/24	Mon 22/4/24	Sat 11/5/24	0 days	0 days	994,991,995SS	997																																																														
993	CON-1A6-10300	Removal of Existing CLP Pylons	107 days	0 days	100%	Fri 4/8/23	Sat 18/11/23	Fri 4/8/23	Sat 18/11/...	0 days	0 days		990																																																														
994	CON-1A6-10400	Treatment of Contaminated Underground Water	130 days	0 days	100%	Thu 28/9/23	Sun 4/2/24	Thu 28/9/23	Sun 4/2/24	0 days	0 days		990,992																																																														
995	CON-1A6-10500	Subsoil Drain (PMI 086)	60 days	0 days	100%	Mon 22/4/24	Thu 20/6/24	Mon 22/4/24	Thu 20/6/...	0 days	0 days		997FS+200 days,992SS																																																														
996	CON-1A6-10600	Water Work	189 days	70.88 days	0%	Tue 7/1/25	Mon 14/7/25	Tue 7/1/25	Mon 14/7/...	0 days	0 days																																																																
997	CON-1A6-10610	Water Pipe Installation (100m)	50 days	0 days	100%	Tue 7/1/25	Tue 25/2/25	Tue 7/1/25	Tue 25/2/...	0 days	0 days	404,992,995FS+200 d	999,1051,1003FS+80 days																																																														
998	CON-1A6-10620	Water Connection	30 days	30 days	0%	Sun 15/6/25	Mon 14/7/25	Sun 15/6/25	Mon 14/7/...	0 days	0 days																																																																
999	CON-1A6-10621	Testing and Submission	24 days	24 days	0%	Sun 15/6/25	Tue 8/7/25	Sun 15/6/25	Tue 8/7/25	0 days	0 days	997,1057FS+14 days	1000,167SS																																																														
1000	CON-1A6-10622	Approval from WSD	1 day	1 day	0%	Wed 9/7/25	Wed 9/7/25	Wed 9/7/25	Wed 9/7/25	0 days	0 days	999	1001																																																														
1001	CON-1A6-10623	Water Connection	1 day	1 day	0%	Thu 10/7/25	Thu 10/7/25	Thu 10/7/25	Thu 10/7/...	0 days	0 days	1000	1002																																																														
1002	CON-1A6-10624	Reinstatement Works	4 days	4 days	0%	Fri 11/7/25	Mon 14/7/25	Fri 11/7/25	Mon 14/7/...	0 days	0 days	1001	1011,1037,1007FF+10 day																																																														
1003	CON-1A6-10700	Utilities	110 days	11 days	90%	Sat 8/3/25	Wed 25/6/25	Sat 8/3/25	Wed 25/6/...	0 days	0 days	426,997FS+80 days	174FF,177FF,1005SS+60																																																														
1004	CON-1A6-10800	Road Works (L54+00 to L54+142)	274 days	91.33 days	0%	Fri 8/11/24	Fri 8/8/25	Fri 8/11/24	Mon 28/9/...	416 days	416 days																																																																
1005	CON-1A6-10810	Gully and Associated Pipe	70 days	0 days	100%	Fri 8/11/24	Thu 16/1/25	Fri 8/11/24	Thu 16/1/...	0 days	0 days	1003SS+60 days,426	1006FS-5 days,1009																																																														
1006	CON-1A6-10820	Pavement	110 days	0 days	100%	Sun 12/1/25	Thu 1/5/25	Sun 12/1/25	Thu 1/5/25	0 days	0 days	1005FS-5 days,1009F	1007																																																														
1007	CON-1A6-10830	Footpath	60 days	60 days	0%	Mon 2/6/25	Thu 31/7/25	Mon 2/6/25	Thu 31/7/...	0 days	0 days	1006,221,1002FF+10	1010																																																														
1008	CON-1A6-10840	Street Furniture / Traffic Sign	25 days	25 days	0%	Tue 15/7/25	Fri 8/8/25	Tue 15/7/25	Fri 8/8/25	0 days	0 days	1002	1011FS-8 days,1010FS-8																																																														
1009	CON-1A6-10845	Laying of Rock Fill for the Formation of Road base for Part of Portion of the Proposed Road L54 (PMI 263)	5 days	5 days	0%	Wed 16/4/25	Sun 20/4/25	Thu 24/9/26	Mon 28/9/26	526 days	526 days	1005	1006FF-15 days																																																														
1010	CON-1A6-10850	Road Lighting (Smart Lamp Post) (PMI 190, PMI 200)	40 days	40 days	0%	Fri 1/8/25	Tue 9/9/25	Fri 1/8/25	Tue 9/9/25	0 days	0 days	458,1007,1008FS-8 d	1037																																																														
1011	CON-1A6-10900	Landscaping Work	40 days	40 days	0%	Fri 1/8/25	Tue 9/9/25	Fri 1/8/25	Tue 9/9/25	0 days	0 days	462,1002,1008FS-8 d	1037																																																														

Task ■ Critical Task ■ Milestone ◆ Summary ▬ Page 22 *E=Excavator L=Lorry W=Worker D=Drill plant C=Crane Lorry R=Rotter


ID	Activity ID	Task Name	Duration	Remaining Duration	% Work Complete	Start	Finish	Late Start	Late Finish	Free Slack	Total Slack	Predecessors	Successors	2021	Half 2, 2021	Half 1, 2022	Half 2, 2022	Half 1, 2023	Half 2, 2023	Half 1, 2024	Half 2, 2024	Half 1, 2025	Half 2, 2025	Half 1, 2026	Half 2, 2026
1058	CON-1A6-20802	Temporary Traffic Ddiversion Stage 2	14 days	14 days	0%	Mon 11/8/25	Sun 24/8/25	Mon 11/8/25	Sun 24/8/...	0 days	0 days	1062,1060	1063												
1059	CON-1A6-20810	Gully and Associated Pipe	21 days	21 days	0%	Tue 24/6/25	Mon 14/7/25	Tue 24/6/25	Mon 14/7/...	0 days	0 days	1055FS-9 days,426,1060													
1060	CON-1A6-20820	Footpath near Fung Kong Tusen	14 days	14 days	0%	Tue 15/7/25	Mon 28/7/25	Tue 15/7/25	Mon 28/7/...	0 days	0 days	1059,1054FS-9 days	1062FS-7 days,1058												
1061	CON-1A6-20821	Footpath near Site 2-18	14 days	14 days	0%	Sun 14/9/25	Sat 27/9/25	Sun 14/9/25	Sat 27/9/25	0 days	0 days	1063	1068												
1062	CON-1A6-12830	Pavement stage 1 (near Fung Kong Tsuen)	20 days	20 days	0%	Tue 22/7/25	Sun 10/8/25	Tue 22/7/25	Sun 10/8/...	0 days	0 days	1060FS-7 days,221	1064,1058												
1063	CON-1A6-12831	Pavement stage 2 (near site 2-18)	20 days	20 days	0%	Mon 25/8/25	Sat 13/9/25	Mon 25/8/25	Sat 13/9/25	0 days	0 days	1058,1055	1068,1061												
1064	CON-1A6-20840	Street Furniture / Traffic Sign	24 days	24 days	0%	Mon 11/8/25	Wed 3/9/25	Mon 11/8/25	Wed 3/9/25	0 days	0 days	1062	1066FS-3 days,1067FS-3												
1065	CON-1A6-20845	Laying of Rock Dill Material for the formation of Roadbase along the Proposed Road L53 (PMI 254)	7 days	7 days	0%	Fri 21/2/25	Thu 27/2/25	Mon 19/5/25	Sun 25/5/25	63 days	87 days		1057												
1066	CON-1A6-20850	Road Lighting (Smart Lamp Post) (PMI 191, PMI 2	27 days	27 days	0%	Mon 1/9/25	Sat 27/9/25	Mon 1/9/25	Sat 27/9/25	0 days	0 days	458,1064FS-3 days	171FF,1068												
1067	CON-1A6-20900	Landscaping Work	27 days	27 days	0%	Mon 1/9/25	Sat 27/9/25	Mon 1/9/25	Sat 27/9/25	0 days	0 days	462,1064FS-3 days	1068												
1068	CON-1A6-21000	Planned Road L53 Completion Date (Road L53 + Rce	0 days	0 days	0%	Sat 27/9/25	Sat 27/9/25	Sat 27/9/25	Sat 27/9/25	0 days	0 days	1067,1066,171,174,17	1078												
1069	CON-1A6-30000	Boost-Up Transformer Room (at footpath of Road	339 days	0 days	100%	Mon 19/2/24	Wed 22/1/25	Mon 19/2/...	Wed 22/1/...	0 days	0 days														
1070	CON-1A6-30100	Excavation to Formation Level	10 days	0 days	100%	Mon 19/2/24	Wed 28/2/24	Mon 19/2/24	Wed 28/2/...	0 days	0 days	442,1262FS+90 days	1071												
1071	CON-1A6-30200	Construction of Footing & Trench	10 days	0 days	100%	Thu 29/2/24	Sat 9/3/24	Thu 29/2/24	Sat 9/3/24	0 days	0 days	1070	1072												
1072	CON-1A6-30300	Construction of RC Structures	30 days	0 days	100%	Sun 10/3/24	Mon 8/4/24	Sun 10/3/24	Mon 8/4/24	0 days	0 days	1071	1073												
1073	CON-1A6-30400	Waterproofing, Finishing & Painting Works	25 days	0 days	100%	Mon 5/8/24	Thu 29/8/24	Mon 5/8/24	Thu 29/8/...	0 days	0 days	1072	1074												
1074	CON-1A6-30500	Hardware	20 days	0 days	100%	Fri 30/8/24	Wed 18/9/24	Fri 30/8/24	Wed 18/9/...	0 days	0 days	1073	1075												
1075	CON-1A6-30600	E&M Works	30 days	0 days	100%	Thu 19/9/24	Fri 18/10/24	Thu 19/9/24	Fri 18/10/...	0 days	0 days	1074,247,230	1076FS+60 days												
1076	CON-1A6-30700	Testing & Commissioning	20 days	0 days	100%	Wed 18/12/24	Mon 6/1/25	Wed 18/1/...	Mon 6/1/25	0 days	0 days	1075FS+60 days	1077												
1077	CON-1A6-30800	Handover to CLP	10 days	0 days	100%	Mon 13/1/25	Wed 22/1/25	Mon 13/1/25	Wed 22/1/...	0 days	0 days	1076,1268	1334,1286,1269												
1078	CON-1A6-40000	Planned Completion of Section 1A6	0 days	0 days	0%	Sat 27/9/25	Sat 27/9/25	Sat 27/9/25	Sat 27/9/25	0 days	0 days	1037,1068,1033,1035,25,1080													
1079		Section 1B	365 days	365 days	0%	Sun 28/9/25	Sun 27/9/26	Sun 28/9/25	Sun 27/9/...	0 days	0 days														
1080	CON-1B-10000	Establishment works of Sections 1A4, 1A5, 1A6	365 days	365 days	0%	Sun 28/9/25	Sun 27/9/26	Sun 28/9/25	Sun 27/9/...	0 days	0 days	895,986,1078	1081												
1081	CON-1B-20000	Planned Completion of Section 1B	0 days	0 days	0%	Sun 27/9/26	Sun 27/9/26	Sun 27/9/26	Sun 27/9/...	0 days	0 days	1080	26												
1082		Section 2A	1340 days	168.3 days	96%	Fri 28/1/22	Sun 28/9/25	Fri 28/1/22	Sun 28/9/...	0 days	0 days														
1083	CON-2A-10000	Ping Ha Road (Portion C1)	997 days	110.08 d...	89%	Mon 19/12/24	Wed 10/9/25	Mon 19/1/...	Wed 10/9/...	0 days	0 days														
1084	CON-2A-10200	Pipe Jacking	964 days	75.61 days	90%	Mon 19/12/24	Fri 8/8/25	Mon 19/1/...	Fri 8/8/25	0 days	0 days														
1085	CON-2A-10201	Site Clearance	3 days	0 days	100%	Mon 19/12/24	Wed 21/1/25	Mon 19/12/...	Wed 21/1/...	0 days	0 days	468	1086,1087,1088												
1086	CON-2A-10202	Initial Survey	7 days	0 days	100%	Thu 22/12/24	Wed 28/1/25	Thu 22/12/...	Wed 28/1/...	0 days	0 days	1085	1090												
1087	CON-2A-10203	Tree Survey	7 days	0 days	100%	Thu 22/12/24	Wed 28/1/25	Thu 22/12/...	Wed 28/1/...	0 days	0 days	1085	1090												
1088	CON-2A-10204	Fence Work	7 days	0 days	100%	Thu 22/12/24	Wed 28/1/25	Thu 22/12/...	Wed 28/1/...	0 days	0 days	1085	1090,1089												
1089	CON-2A-10205	Underground Utilities Detection and Protection	90 days	0 days	100%	Thu 29/12/24	Tue 28/3/25	Thu 29/12/...	Tue 28/3/...	0 days	0 days	1088	1090												
1090	CON-2A-10206	Install Monitoring Points	7 days	0 days	100%	Mon 3/4/23	Sun 9/4/23	Mon 3/4/23	Sun 9/4/23	0 days	0 days	1086,1087,1088,1089	1091												
1091	CON-2A-10207	ELS for Jacking Pits & Receiving Pits	550 days	0 days	100%	Mon 10/4/23	Thu 10/10/24	Mon 10/4/23	Thu 10/1/...	0 days	0 days	1090,455	1099SS+20 days,1095,109												
1092	CON-2A-10210	Pipe Jacking Works	130 days	0 days	100%	Fri 11/10/24	Mon 17/2/25	Fri 11/10/24	Mon 17/2/...	0 days	0 days														
1093	CON-2A-10211	Preparation works for Pipe Jacking, including Supporting Frame, Thrust Wall, Entrance Ring and set up of Jacking Equipment etc.	60 days	0 days	100%	Fri 11/10/24	Mon 9/12/24	Fri 11/10/24	Mon 9/12/24	0 days	0 days	1091	1095,1094												
1094	CON-2A-10212	Pipe Jacking	70 days	0 days	100%	Tue 10/12/24	Mon 17/2/25	Tue 10/12/...	Mon 17/2/...	0 days	0 days	1093	1095FS+55 days												
1095	CON-2A-10213	Pipe Installation within Sleeve Pipes	50 days	5 days	90%	Mon 14/4/25	Mon 2/6/25	Mon 14/4/25	Mon 2/6/25	0 days	0 days	1091,1093,1094FS+55	1096												
1096	CON-2A-10214	Construct Chambers & Main Connections ; Revised Design of WSD Inspection Chamber and Pipe Jacking Works(PMI 203)	60 days	60 days	0%	Tue 3/6/25	Fri 1/8/25	Tue 3/6/25	Fri 1/8/25	0 days	0 days	1095	1097												
1097	CON-2A-10215	Backfilling & Reinstatement	7 days	7 days	0%	Sat 2/8/25	Fri 8/8/25	Sat 2/8/25	Fri 8/8/25	0 days	0 days	1096	1101												
1098	CON-2A-10300	Water Work	865 days	865 days	0%	Sun 30/4/23	Wed 10/9/25	Sun 30/4/23	Wed 10/9/...	0 days	0 days														
1099	CON-2A-10310	Water Pipe Installation at Ping Ha Road (Omitted)	0 days	0 days	100%	Sun 30/4/23	Sun 30/4/23	Sun 30/4/23	Sun 30/4/...	0 days	0 days	404,1091SS+20 days	1101												
1100	CON-2A-10320	Water Connection	33 days	33 days	0%	Sat 9/8/25	Wed 10/9/25	Sat 9/8/25	Wed 10/9/...	0 days	0 days														
1101	CON-2A-10321	Testing and Submission	26 days	26 days	0%	Sat 9/8/25	Wed 3/9/25	Sat 9/8/25	Wed 3/9/25	0 days	0 days	1099,1097	1102,168SS												
1102	CON-2A-10322	Approval from WSD	1 day	1 day	0%	Thu 4/9/25	Thu 4/9/25	Thu 4/9/25	Thu 4/9/25	0 days	0 days	1101	1103												
1103	CON-2A-10323	Water Connection	1 day	1 day	0%	Fri 5/9/25	Fri 5/9/25	Fri 5/9/25	Fri 5/9/25	0 days	0 days	1102	1104												
1104	CON-2A-10324	Reinstatement Works	5 days	5 days	0%	Sat 6/9/25	Wed 10/9/25	Sat 6/9/25	Wed 10/9/...	0 days	0 days	1103,168FF	1105												
1105		Planned Ping Ha Road Completion Date	0 days	0 days	0%	Wed 10/9/25	Wed 10/9/25	Wed 10/9/25	Wed 10/9/...	0 days	0 days	1104	1334												
1106	CON-2A-20000	Ha Tsuen Road (Portion A3,A6,A7,A8,D1,D2)	946 days	0 days	100%	Thu 28/7/22	Fri 28/2/25	Thu 28/7/22	Fri 28/2/25	0 days	0 days														
1107	CON-2A-20100	Water Work and Sewerage Work (Omitted)	545 days	0 days	100%	Fri 1/9/23	Fri 28/2/25	Fri 1/9/23	Fri 28/2/25	0 days	0 days														

ID	Activity ID	Task Name	Duration	Remaining Duration	% Work Complete	Start	Finish	Late Start	Late Finish	Free Slack	Total Slack	Predecessors	Successors	2021	Half 2, 2021	Half 1, 2022	Half 2, 2022	Half 1, 2023	Half 2, 2023	Half 1, 2024	Half 2, 2024	Half 1, 2025	Half 2, 2025	Half 1, 2026	Half 2, 2026
1108	CON-2A-20110	Water Pipe Installation (Ha Tsuen Road to Road D1) (Omitted)	0 days	0 days	100%	Fri 1/9/23	Fri 1/9/23	Fri 1/9/23	Fri 1/9/23	0 days	0 days	32,35,36,37,473,404	1111,1130												
1109	CON-2A-20120	Sewer pipe and manhole installation (Ha Tsuen Road to Road D1) (Omitted)	0 days	0 days	100%	Fri 1/9/23	Fri 1/9/23	Fri 1/9/23	Fri 1/9/23	0 days	0 days	32,35,36,37,473,404	1111,1130												
1110	CON-2A-20120	Water Connection (Omitted)	0 days	0 days	100%	Fri 28/2/25	Fri 28/2/25	Fri 28/2/25	Fri 28/2/25	0 days	0 days														
1111	CON-2A-20121	Testing and Submission (Omitted)	0 days	0 days	100%	Fri 28/2/25	Fri 28/2/25	Fri 28/2/25	Fri 28/2/25	0 days	0 days	1108,1264,1109	1112,166SS												
1112	CON-2A-20122	Approval from WSD (Omitted)	0 days	0 days	100%	Fri 28/2/25	Fri 28/2/25	Fri 28/2/25	Fri 28/2/25	0 days	0 days	1111	1113												
1113	CON-2A-20123	Water Connection (Omitted)	0 days	0 days	100%	Fri 28/2/25	Fri 28/2/25	Fri 28/2/25	Fri 28/2/25	0 days	0 days	1112	1114												
1114	CON-2A-20124	Reinstatement Works (Omitted)	0 days	0 days	100%	Fri 28/2/25	Fri 28/2/25	Fri 28/2/25	Fri 28/2/25	0 days	0 days	1113,166FF	1131												
1115	CON-2A-20200	Sewage Pumping Station (Omitted)	553 days	0 days	100%	Thu 28/7/22	Thu 1/2/24	Thu 28/7/22	Thu 1/2/24	0 days	0 days														
1116	CON-2A-20210	Sewage Work (Omitted)	553 days	0 days	100%	Thu 28/7/22	Thu 1/2/24	Thu 28/7/22	Thu 1/2/24	0 days	0 days														
1117	CON-2A-20211	Access day 456	0 days	0 days	100%	Thu 28/7/22	Thu 28/7/22	Thu 28/7/22	Thu 28/7/...	0 days	0 days	47	1118												
1118	CON-2A-20212	Site Clearance (Omitted)	0 days	0 days	100%	Thu 28/7/22	Thu 28/7/22	Thu 28/7/22	Thu 28/7/...	0 days	0 days	1117	1119,1120,1121,1122												
1119	CON-2A-20213	Initial Survey (Omitted)	0 days	0 days	100%	Thu 28/7/22	Thu 28/7/22	Thu 28/7/22	Thu 28/7/...	0 days	0 days	1118	1122												
1120	CON-2A-20214	Tree Survey (Omitted)	0 days	0 days	100%	Thu 28/7/22	Thu 28/7/22	Thu 28/7/22	Thu 28/7/...	0 days	0 days	1118	1122												
1121	CON-2A-20215	Fence Work (Omitted)	0 days	0 days	100%	Thu 28/7/22	Thu 28/7/22	Thu 28/7/22	Thu 28/7/...	0 days	0 days	1118	1122												
1122	CON-2A-20216	Underground Utilities Detection (Omitted)	0 days	0 days	100%	Thu 28/7/22	Thu 28/7/22	Thu 28/7/22	Thu 28/7/...	0 days	0 days	1118,1121,1119,1120	1123												
1123	CON-2A-20217	Install Monitoring Points (Omitted)	0 days	0 days	100%	Thu 1/2/24	Thu 1/2/24	Thu 1/2/24	Thu 1/2/24	0 days	0 days	1122	1124												
1124	CON-2A-20218	ELS (Omitted)	0 days	0 days	100%	Thu 1/2/24	Thu 1/2/24	Thu 1/2/24	Thu 1/2/24	0 days	0 days	1123,439,366	1125												
1125	CON-2A-20219	Construction of RC Structures (Omitted)	0 days	0 days	100%	Thu 1/2/24	Thu 1/2/24	Thu 1/2/24	Thu 1/2/24	0 days	0 days	1124	1128FS-20 days,1126,112												
1126	CON-2A-20220	Builder's Works and Finish (Omitted)	0 days	0 days	100%	Thu 1/2/24	Thu 1/2/24	Thu 1/2/24	Thu 1/2/24	0 days	0 days	1125	1130,1127												
1127	CON-2A-20221	E&M Works (Omitted)	0 days	0 days	100%	Thu 1/2/24	Thu 1/2/24	Thu 1/2/24	Thu 1/2/24	0 days	0 days	1125,1126	1130												
1128	CON-2A-20222	Rising Main (Omitted)	0 days	0 days	100%	Fri 12/1/24	Fri 12/1/24	Fri 12/1/24	Fri 12/1/24	0 days	0 days	1125FS-20 days,473	1130												
1129	CON-2A-20230	Setting Equipment	0 days	0 days	100%	Thu 1/2/24	Thu 1/2/24	Thu 1/2/24	Thu 1/2/24	0 days	0 days														
1130	CON-2A-20231	Test and Commissioning (Omitted)	0 days	0 days	100%	Thu 1/2/24	Thu 1/2/24	Thu 1/2/24	Thu 1/2/24	0 days	0 days	1128,1127,1126,1108,	1131												
1131		Planned Ha Tsuen Road completion Date	0 days	0 days	100%	Fri 28/2/25	Fri 28/2/25	Fri 28/2/25	Fri 28/2/25	0 days	0 days	1114,1130,154	1334												
1132	CON-2A-30000	Detention Pond (Portion B2)	1256 days	115.32 d...	100%	Fri 28/1/22	Tue 8/7/25	Fri 28/1/22	Sun 28/9/...	82 days	82 days														
1133	CON-2A-30100	Site Clearance	5 days	0 days	100%	Fri 28/1/22	Tue 1/2/22	Fri 28/1/22	Tue 1/12/22	0 days	0 days	39	1134,1135,1136,1137												
1134	CON-2A-30200	Initial Survey	7 days	0 days	100%	Wed 2/2/22	Tue 8/2/22	Wed 2/2/22	Tue 8/2/22	0 days	0 days	1133	1138												
1135	CON-2A-30300	Tree Survey	7 days	0 days	100%	Wed 2/2/22	Tue 8/2/22	Wed 2/2/22	Tue 8/2/22	0 days	0 days	1133	1138												
1136	CON-2A-30400	Fence Work	7 days	0 days	100%	Wed 2/2/22	Tue 8/2/22	Wed 2/2/22	Tue 8/2/22	0 days	0 days	1133	1138												
1137	CON-2A-30500	Underground Utilities Detection	7 days	0 days	100%	Wed 2/2/22	Tue 8/2/22	Wed 2/2/22	Tue 8/2/22	0 days	0 days	1133	1138												
1138	CON-2A-30600	Install Monitoring Points	14 days	0 days	100%	Wed 9/2/22	Tue 22/2/22	Wed 9/2/22	Tue 22/2/...	0 days	0 days	1134,1135,1136,1137	1139,1144												
1139	CON-2A-30700	Excavation to Bottom Level & Cut Slope (Heavy Metal Treatment Area) (Omitted)	0 days	0 days	100%	Tue 23/4/24	Tue 23/4/24	Tue 23/4/24	Tue 23/4/24	0 days	0 days	445,1138,1188	1140												
1140	CON-2A-30710	Excavation to Bottom Level & Cut Slope (Hydrocarbon Treatment Area) (Omitted)	0 days	0 days	100%	Tue 23/4/24	Tue 23/4/24	Tue 23/4/24	Tue 23/4/24	0 days	0 days	1139	1141												
1141	CON-2A-30800	Laying 1st Layer of Granular Material with Geotextile Filter (Omitted)	0 days	0 days	100%	Tue 23/4/24	Tue 23/4/24	Tue 23/4/24	Tue 23/4/24	0 days	0 days	1140	1142												
1142	CON-2A-30900	Laying 2nd Layer of Granular Material with Geotextile Filter (Omitted)	0 days	0 days	100%	Tue 23/4/24	Tue 23/4/24	Tue 23/4/24	Tue 23/4/24	0 days	0 days	1141	1143												
1143	CON-2A-31000	300 u-channel at +17.2mPD (Omitted)	0 days	0 days	100%	Tue 23/4/24	Tue 23/4/24	Tue 23/4/24	Tue 23/4/...	0 days	0 days	1142	1148,1145												
1144	CON-2A-31100	Construction of Toe Block & Outlet Chamber	150 days	0 days	100%	Mon 20/2/23	Wed 19/7/23	Mon 20/2/23	Wed 19/7/...	0 days	0 days	1159,1138	1149												
1145	CON-2A-31200	Laying Granular Material with Geotextile Filter on Slope (Omitted)	0 days	0 days	100%	Tue 23/4/24	Tue 23/4/24	Tue 23/4/24	Tue 23/4/24	0 days	0 days	1143	1146												
1146	CON-2A-31300	Laying 150mm thk. Cast In-situ Cellular Reinforced Paving (Omitted)	0 days	0 days	100%	Tue 23/4/24	Tue 23/4/24	Tue 23/4/24	Tue 23/4/24	0 days	0 days	1145	1334,1147												
1147	CON-2A-31400	Install Drainage Trunk Main No.1 & No.2 (Omitted)	0 days	0 days	100%	Tue 23/4/24	Tue 23/4/24	Tue 23/4/24	Tue 23/4/...	0 days	0 days	1146	1148												
1148	CON-2A-31500	Access Road from +17.2mPD to Top (Omitted)	0 days	0 days	100%	Tue 23/4/24	Tue 23/4/24	Tue 23/4/24	Tue 23/4/...	0 days	0 days	1143,1147	1151												
1149	CON-2A-31600	Construction of 1650 drain pipe connecting to outlet chamber	100 days	0 days	100%	Thu 20/7/23	Fri 27/10/23	Thu 20/7/23	Fri 27/10/23	0 days	0 days	1144	1150FS+150 days												
1150	CON-2A-31700	Construction of 1650 drain pipe st downstream to detention pond	154 days	0 days	100%	Tue 26/3/24	Mon 26/8/24	Tue 26/3/24	Mon 26/8/24	0 days	0 days	1149FS+150 days	1196,1154												
1151	CON-2A-31800	150 U-channel & Concrete Slab on Top Level around the Pond (Omitted)	0 days	0 days	100%	Tue 23/4/24	Tue 23/4/24	Tue 23/4/24	Tue 23/4/24	0 days	0 days	1148	1196												

ID	Activity ID	Task Name	Duration	Remaining Duration	% Work Complete	Start	Finish	Late Start	Late Finish	Free Slack	Total Slack	Predecessors	Successors	2021	Half 2, 2021	Half 1, 2022	Half 2, 2022	Half 1, 2023	Half 2, 2023	Half 1, 2024	Half 2, 2024	Half 1, 2025	Half 2, 2025	Half 1, 2026	Half 2, 2026
1152	CON-2A-31810	Rehabilitation of the Existing Ditch at Downstream of Detention Pond (PMI 227)	150 days	0 days	100%	Thu 26/12/24	Sat 24/5/25	Thu 26/12/24	Sat 24/5/25	0 days	0 days		1196												
1153	CON-2A-31900	Demolition of the Existing Shelter and Formation of a Temporary Access for the Existing Business Undertakings near Detention Pond (PMI 224)	14 days	0 days	100%	Mon 4/11/24	Sun 17/11/24	Mon 4/11/24	Sun 17/11/24	0 days	0 days		603												
1154	CON-2A-31910	Trapezoidal Channel (2mx12mx1m D)	21 days	8.4 days	60%	Wed 21/5/25	Tue 10/6/25	Wed 21/5/...	Sun 31/8/...	0 days	82 days	1150,767FS+150 days	1155												
1155	CON-2A-31920	Desilting Pond (12mx12mx2.5m)	28 days	28 days	0%	Wed 11/6/25	Tue 8/7/25	Mon 1/9/25	Sun 28/9/...	0 days	82 days	1154	1196												
1156	CON-2A-32000	Remediation of Contaminated Soil	865 days	95.52 days	0%	Tue 14/2/23	Fri 27/6/25	Tue 14/2/23	Sun 28/9/...	0 days	93 days														
1157	CON-2A-33000	Biopile Works (Hydrocarbon Treatment)	805 days	97.96 days	0%	Tue 14/2/23	Mon 28/4/25	Tue 14/2/23	Sun 28/9/...	0 days	153 days														
1158	CON-2A-33100	Biopile System Setup	46 days	0 days	100%	Tue 14/2/23	Fri 31/3/23	Tue 14/2/23	Fri 31/3/23	0 days	0 days														
1159	CON-2A-33101	Formation of Concrete Slab	6 days	0 days	100%	Tue 14/2/23	Sun 19/2/23	Tue 14/2/23	Sun 19/2/...	0 days	0 days		1160,1144												
1160	CON-2A-33102	Waterproofing Works	9 days	0 days	100%	Mon 20/2/23	Tue 28/2/23	Mon 20/2/23	Tue 28/2/...	0 days	0 days	1159	1161												
1161	CON-2A-33103	Placing 1st Layer of contaminated soil & associated pipe	14 days	0 days	100%	Wed 1/3/23	Tue 14/3/23	Wed 1/3/23	Tue 14/3/23	0 days	0 days	1160	1162												
1162	CON-2A-33105	Placing 2nd Layer of contaminated soil & cover up the whole biopile	14 days	0 days	100%	Wed 15/3/23	Tue 28/3/23	Wed 15/3/23	Tue 28/3/23	0 days	0 days	1161	1163												
1163	CON-2A-33107	Connection & Commissioning of Biopile Sy	3 days	0 days	100%	Wed 29/3/23	Fri 31/3/23	Wed 29/3/...	Fri 31/3/23	0 days	0 days	1162	1166,1167,767,1165												
1164	CON-2A-33200	Biopile System Operation	587 days	0 days	100%	Thu 3/8/23	Tue 11/3/25	Thu 3/8/23	Tue 11/3/...	0 days	0 days														
1165	CON-2A-33201	Operation & Maintenance (for Site 2-18, 2-	180 days	0 days	100%	Thu 3/8/23	Mon 29/1/24	Thu 3/8/23	Mon 29/1/...	0 days	0 days	1163,861SS+12 days	1169												
1166	CON-2A-33211	Operation & Maintenance (for Site 3-8)	180 days	0 days	100%	Thu 3/8/23	Mon 29/1/24	Thu 3/8/23	Mon 29/1/...	0 days	0 days	1163,765SS+12 days	1170												
1167	CON-2A-33213	Operation & Maintenance (for Site 3-8 CIF)	157 days	0 days	100%	Sun 6/10/24	Tue 11/3/25	Sun 6/10/24	Tue 11/3/...	0 days	0 days	1163,767	1170,1194												
1168	CON-2A-33300	Completion of Biopile	437 days	437 days	0%	Tue 30/1/24	Thu 10/4/25	Sat 26/4/25	Sun 25/5/...	45 days	45 days														
1169	CON-2A-33301	Submission of Closure Assessment Report (for Site 2-18,2-19,L54)	30 days	30 days	0%	Tue 30/1/24	Wed 28/2/24	Sat 26/4/25	Sun 25/5/25	407 days	452 days	1165	1171,1190												
1170	CON-2A-33304	Submission of Closure Assessment Report (for Site 3-8)	30 days	30 days	0%	Wed 12/3/25	Thu 10/4/25	Sat 26/4/25	Sun 25/5/25	0 days	45 days	1167,1166	1171,1190,1194												
1171	CON-2A-33400	Removal of Facilities	18 days	18 days	0%	Fri 11/4/25	Mon 28/4/25	Thu 11/9/25	Sun 28/9/...	71 days	153 days	1170,1169	1196												
1172	CON-2A-34000	Cement Solidification Works (Heavy Metal Treatment)	429 days	0 days	100%	Mon 20/2/23	Tue 23/4/24	Mon 20/2/23	Tue 23/4/24	0 days	0 days														
1173	CON-2A-34100	Mixing Facilities Setup	171 days	0 days	100%	Mon 20/2/23	Wed 9/8/23	Mon 20/2/...	Wed 9/8/23	0 days	0 days														
1174	CON-2A-34101	Formation of Concrete Slab	6 days	0 days	100%	Mon 20/2/23	Sat 25/2/23	Mon 20/2/23	Sat 25/2/23	0 days	0 days		1175												
1175	CON-2A-34102	Placing Concrete Block Barrier	9 days	0 days	100%	Sun 26/2/23	Mon 6/3/23	Sun 26/2/23	Mon 6/3/23	0 days	0 days	1174	1176												
1176	CON-2A-34103	Waterproofing Works	6 days	0 days	100%	Tue 7/3/23	Sun 12/3/23	Tue 7/3/23	Sun 12/3/...	0 days	0 days	1175	1177												
1177	CON-2A-34104	Provision of Enclose Shelter	150 days	0 days	100%	Mon 13/3/23	Wed 9/8/23	Mon 13/3/23	Wed 9/8/23	0 days	0 days	1176	1181,1185,768,1179,1183												
1178	CON-2A-34200	Cement Solidification Operation	252 days	0 days	100%	Wed 9/8/23	Wed 17/4/24	Wed 9/8/23	Wed 17/4/...	0 days	0 days														
1179	CON-2A-34201	Mixing Operation (for Site 2-18,2-19, L54)	30 days	0 days	100%	Thu 10/8/23	Fri 8/9/23	Thu 10/8/23	Fri 8/9/23	0 days	0 days	1177,862SS+65 days	1180SS+7 days												
1180	CON-2A-34202	Confirmation Test (for Site 2-18,2-19,L54)	30 days	0 days	100%	Thu 17/8/23	Fri 15/9/23	Thu 17/8/23	Fri 15/9/23	0 days	0 days	1179SS+7 days	1190												
1181	CON-2A-34209	Mixing Operation (for Site 3-7 CIF)	0 days	0 days	100%	Wed 9/8/23	Wed 9/8/23	Wed 9/8/23	Wed 9/8/23	0 days	0 days	1177,667SS+45 days	1182SS+7 days												
1182	CON-2A-34210	Confirmation Test (for Site 3-7, CIF)	0 days	0 days	100%	Wed 16/8/23	Wed 16/8/23	Wed 16/8/...	Wed 16/8/...	0 days	0 days	1181SS+7 days	1188,1192												
1183	CON-2A-34211	Mixing Operation (for Site 3-8)	30 days	0 days	100%	Thu 10/8/23	Fri 8/9/23	Thu 10/8/23	Fri 8/9/23	0 days	0 days	1177,766SS+22 days	1184SS+7 days												
1184	CON-2A-34212	Confirmation Test (for Site 3-8)	30 days	0 days	100%	Thu 17/8/23	Fri 15/9/23	Thu 17/8/23	Fri 15/9/23	0 days	0 days	1183SS+7 days	1188												
1185	CON-2A-34213	Mixing Operation (for Site 3-8 CIF)	30 days	0 days	100%	Tue 21/11/23	Wed 20/12/23	Tue 21/11/...	Wed 20/1/...	0 days	0 days	1177,768SS+25 days	1186SS+7 days												
1186	CON-2A-34214	Confirmation Test (for Site 3-8, CIF)	30 days	0 days	100%	Tue 28/11/23	Wed 27/12/23	Tue 28/11/...	Wed 27/1/...	0 days	0 days	1185SS+7 days	1188,1194												
1187	CON-2A-34315	Temporary Storage at Site 3-6 Lower Platform (PMI 077)	150 days	0 days	100%	Mon 20/11/23	Wed 17/4/24	Mon 20/11/23	Wed 17/4/24	0 days	0 days		1188,523SS												
1188	CON-2A-34416	Decommission of Facilities	6 days	0 days	100%	Thu 18/4/24	Tue 23/4/24	Thu 18/4/24	Tue 23/4/...	0 days	0 days	1182,1184,1186,1187	1139												
1189	CON-2A-35000	Remediation Report Submission	681 days	288.12 d...	0%	Wed 16/8/23	Fri 27/6/25	Wed 16/8/...	Sun 28/9/...	93 days	93 days														
1190	CON-2A-35100	Preparation of Remediation Report (For Site 2-18,2-19,L54)	50 days	5 days	90%	Fri 11/4/25	Fri 30/5/25	Fri 11/4/25	Sun 31/8/25	0 days	93 days	1169,1180,1170	1191												
1191	CON-2A-35200	Review & Accepted by EPD (For Site 2-18,2-1	28 days	28 days	0%	Sat 31/5/25	Fri 27/6/25	Mon 1/9/25	Sun 28/9/...	11 days	93 days	1190	1196												
1192	CON-2A-35500	Preparation of Remediation Report (For Site 3	0 days	0 days	100%	Wed 16/8/23	Wed 16/8/23	Wed 16/8/...	Wed 16/8/...	0 days	0 days	1182	1193												
1193	CON-2A-35600	Review & Accepted by EPD (For Site 3-7)	0 days	0 days	100%	Wed 16/8/23	Wed 16/8/23	Wed 16/8/...	Wed 16/8/...	0 days	0 days	1192	1196												
1194	CON-2A-35700	Preparation of Remediation Report (For Site 3	50 days	5 days	90%	Fri 11/4/25	Fri 30/5/25	Fri 11/4/25	Sun 31/8/...	0 days	93 days	1186,1167,1170	1195												
1195	CON-2A-35800	Review & Accepted by EPD (For Site 3-8)	28 days	28 days	0%	Sat 31/5/25	Fri 27/6/25	Mon 1/9/25	Sun 28/9/...	11 days	93 days	1194	1196												
1196		Planned Completion Date of Detention Pond	0 days	0 days	0%	Tue 8/7/25	Tue 8/7/25	Sun 28/9/25	Sun 28/9/...	82 days	82 days	1150,1151,1195,1193,1334													

ID	Activity ID	Task Name	Duration	Remaining Duration	% Work Complete	Start	Finish	Late Start	Late Finish	Free Slack	Total Slack	Predecessors	Successors	2021	Half 2, 2021	Half 1, 2022	Half 2, 2022	Half 1, 2023	Half 2, 2023	Half 1, 2024	Half 2, 2024	Half 1, 2025	Half 2, 2025	Half 1, 2026	Half 2, 2026
1197	CON-2A-40000	Road D1 (Decontamination works refer to Site 3-6, 3-7 and 3-8)	931 days	60.94 days	100%	Thu 29/12/22	Wed 16/7/25	Thu 29/12/22	Sun 28/9/25	74 days	74 days														
1198	CON-2A-40100	Soldier Pile Wall (Omitted)	0 days	0 days	100%	Sat 24/8/24	Sat 24/8/24	Sat 24/8/24	Sat 24/8/24	0 days	0 days														
1199	CON-2A-40110	Working platform (Omitted)	0 days	0 days	100%	Sat 24/8/24	Sat 24/8/24	Sat 24/8/24	Sat 24/8/24	0 days	0 days	55	1200												
1200	CON-2A-40120	Pre-drilling (Omitted)	0 days	0 days	100%	Sat 24/8/24	Sat 24/8/24	Sat 24/8/24	Sat 24/8/24	0 days	0 days	1199	1201												
1201	CON-2A-40130	Soldier Pile (Omitted)	0 days	0 days	100%	Sat 24/8/24	Sat 24/8/24	Sat 24/8/24	Sat 24/8/24	0 days	0 days	1200	1202												
1202	CON-2A-40140	Lagging Wall & Capping Beam (Omitted)	0 days	0 days	100%	Sat 24/8/24	Sat 24/8/24	Sat 24/8/24	Sat 24/8/24	0 days	0 days	1201	1203												
1203	CON-2A-40150	Mass Concrete Retaining Wall (Omitted)	0 days	0 days	100%	Sat 24/8/24	Sat 24/8/24	Sat 24/8/24	Sat 24/8/24	0 days	0 days	1202	1204												
1204	CON-2A-40160	Remove Working platform and trim to Formation Level (Omitted)	0 days	0 days	100%	Sat 24/8/24	Sat 24/8/24	Sat 24/8/24	Sat 24/8/24	0 days	0 days	1203	1246												
1205	CON-2A-40170	Cut the existing slope Along Road D1 (PMI 234)	30 days	30 days	0%	Tue 3/6/25	Wed 2/7/25	Sat 30/8/25	Sun 28/9/...	88 days	88 days	1320FS+14 days,1246	1334												
1206	CON-2A-41000	Road D1 North Eastern Portion (Next to Site 3-7, D1+320 to D1+511)	342 days	0 days	100%	Sat 20/7/24	Thu 26/6/25	Sat 20/7/24	Thu 26/6/25	0 days	0 days														
1207	CON-2A-41100	Northbound	237 days	0 days	100%	Sat 20/7/24	Thu 13/3/25	Sat 20/7/24	Thu 13/3/...	0 days	0 days														
1208	CON-2A-41110	Earthwork	237 days	0 days	100%	Sat 20/7/24	Thu 13/3/25	Sat 20/7/24	Thu 13/3/...	0 days	0 days														
1209	CON-2A-41111	Removal of additional Concrete Pavement within HSK CIF	20 days	0 days	100%	Sat 20/7/24	Thu 8/8/24	Sat 20/7/24	Thu 8/8/24	0 days	0 days	518	1210,524												
1210	CON-2A-41113	Sewerage (Omitted)	0 days	0 days	100%	Thu 8/8/24	Thu 8/8/24	Thu 8/8/24	Thu 8/8/24	0 days	0 days	162,407,410,1209	1211												
1211	CON-2A-41114	Backfilling & Compaction to Formation	217 days	0 days	100%	Fri 9/8/24	Thu 13/3/25	Fri 9/8/24	Thu 13/3/...	0 days	0 days	1210	1212,1214,1228FS-30 day												
1212	CON-2A-41115	Drainage	0 days	0 days	100%	Thu 13/3/25	Thu 13/3/25	Thu 13/3/25	Thu 13/3/...	0 days	0 days	1211	1213,1214												
1213	CON-2A-41116	Waterpipe Installation (Omitted)	0 days	0 days	100%	Thu 13/3/25	Thu 13/3/25	Thu 13/3/25	Thu 13/3/...	0 days	0 days	404,1212	1222												
1214	CON-2A-41117	Surface Drainage (Omitted)	0 days	0 days	100%	Thu 13/3/25	Thu 13/3/25	Thu 13/3/25	Thu 13/3/...	0 days	0 days	1211,1212	1225												
1215	CON-2A-41200	Southbound	237 days	0 days	100%	Sat 20/7/24	Thu 13/3/25	Sat 20/7/24	Thu 13/3/...	0 days	0 days														
1216	CON-2A-41210	Earthwork	237 days	0 days	100%	Sat 20/7/24	Thu 13/3/25	Sat 20/7/24	Thu 13/3/...	0 days	0 days														
1217	CON-2A-41211	Removal of additional Concrete Pavement within HSK CIF	20 days	0 days	100%	Sat 20/7/24	Thu 8/8/24	Sat 20/7/24	Thu 8/8/24	0 days	0 days	518	524,1219,1218												
1218	CON-2A-41212	Demolition and Disposal of a CLP Transformer Room (PMI 073)	15 days	0 days	100%	Fri 9/8/24	Fri 23/8/24	Fri 9/8/24	Fri 23/8/24	0 days	0 days	1217	1229												
1219	CON-2A-41213	Backfilling & Compaction to Formation	217 days	0 days	100%	Fri 9/8/24	Thu 13/3/25	Fri 9/8/24	Thu 13/3/...	0 days	0 days	1217	1220,1221,1228FS-30 day												
1220	CON-2A-41214	Drainage (Omitted)	0 days	0 days	100%	Thu 13/3/25	Thu 13/3/25	Thu 13/3/25	Thu 13/3/...	0 days	0 days	1219	1222,1221												
1221	CON-2A-41215	Surface Drainage (Omitted)	0 days	0 days	100%	Thu 13/3/25	Thu 13/3/25	Thu 13/3/25	Thu 13/3/...	0 days	0 days	1219,1220	1225												
1222	CON-2A-41300	Utilities (Omitted)	0 days	0 days	100%	Thu 13/3/25	Thu 13/3/25	Thu 13/3/25	Thu 13/3/...	0 days	0 days	426,1213,1220	1223												
1223	CON-2A-41400	Road Work (Omitted)	0 days	0 days	100%	Thu 13/3/25	Thu 13/3/25	Thu 13/3/25	Thu 13/3/...	0 days	0 days	426,1222	1224,1225												
1224	CON-2A-41500	Road Lighting (Omitted)	0 days	0 days	100%	Thu 13/3/25	Thu 13/3/25	Thu 13/3/25	Thu 13/3/...	0 days	0 days	458,1223	1289												
1225	CON-2A-41600	Landscaping Work (Omitted)	0 days	0 days	100%	Thu 26/6/25	Thu 26/6/25	Thu 26/6/25	Thu 26/6/...	0 days	0 days	462,1223,1214,1221	1289												
1226	CON-2A-41710	Trapezoidal Channel	37 days	0 days	100%	Mon 14/4/25	Tue 20/5/25	Mon 14/4/25	Tue 20/5/...	0 days	0 days	1227	1289,1334,1154												
1227	CON-2A-41720	Surface U-channel	36 days	0 days	100%	Sun 9/3/25	Sun 13/4/25	Sun 9/3/25	Sun 13/4/...	0 days	0 days	1228	1289,1334,1226,1249												
1228	CON-2A-41730	Dia. 450mm Drain Pipe	25 days	0 days	100%	Wed 12/2/25	Sat 8/3/25	Wed 12/2/...	Sat 8/3/25	0 days	0 days	1211FS-30 days,1219	1227												
1229	CON-2A-41740	Dia. 1650mm Drain Pipe	28 days	0 days	100%	Jun 17/11/25	Sat 14/12/24	Sun 17/11/...	Sat 14/12/...	0 days	0 days	1211FS-117 days,121	1247,1228												
1230	CON-2A-42000	Road D1 Central Portion (Next to Site 3-8, D1+170 to D1+320)	219 days	0 days	100%	Wed 20/11/24	Thu 26/6/25	Wed 20/11/24	Thu 26/6/25	0 days	0 days														
1231	CON-2A-42100	Northbound	48 days	0 days	100%	Wed 20/11/24	Mon 6/1/25	Wed 20/1/...	Mon 6/1/25	0 days	0 days														
1232	CON-2A-42110	Earthwork	48 days	0 days	100%	Wed 20/11/24	Mon 6/1/25	Wed 20/1/...	Mon 6/1/25	0 days	0 days														
1233	CON-2A-42111	Removal of additional Concrete Pavement within HSK CIF	18 days	0 days	100%	Wed 20/11/24	Sat 7/12/24	Wed 20/11/24	Sat 7/12/24	0 days	0 days	780	1234,1240,1247												
1234	CON-2A-42112	Sewerage (Omitted)	0 days	0 days	100%	Sat 7/12/24	Sat 7/12/24	Sat 7/12/24	Sat 7/12/24	0 days	0 days	1233,162,407,410	1235,1237,1241SS+20 day												
1235	CON-2A-42113	Drainage (Omitted)	0 days	0 days	100%	Sat 7/12/24	Sat 7/12/24	Sat 7/12/24	Sat 7/12/24	0 days	0 days	1234	1236SS+30 days,1237												
1236	CON-2A-42114	Waterpipe Installation (Omitted)	0 days	0 days	100%	Mon 6/1/25	Mon 6/1/25	Mon 6/1/25	Mon 6/1/25	0 days	0 days	404,1235SS+30 days	1243,1244												
1237	CON-2A-42115	Surface Drainage (Omitted)	0 days	0 days	100%	Sat 7/12/24	Sat 7/12/24	Sat 7/12/24	Sat 7/12/24	0 days	0 days	1234,1235	1246												
1238	CON-2A-42200	Southbound	20 days	0 days	100%	Sun 8/12/24	Fri 27/12/24	Sun 8/12/24	Fri 27/12/...	0 days	0 days														
1239	CON-2A-42210	Earthwork	20 days	0 days	100%	Sun 8/12/24	Fri 27/12/24	Sun 8/12/24	Fri 27/12/...	0 days	0 days														
1240	CON-2A-42211	Removal of additional Concrete Pavement within HSK CIF	20 days	0 days	100%	Sun 8/12/24	Fri 27/12/24	Sun 8/12/24	Fri 27/12/24	0 days	0 days	1233	1241,1247												
1241	CON-2A-42221	Drainage (omitted)	0 days	0 days	100%	Fri 27/12/24	Fri 27/12/24	Fri 27/12/24	Fri 27/12/...	0 days	0 days	1240,162,407,410,123	1244,1242												
1242	CON-2A-42222	Surface Drainage (omitted)	0 days	0 days	100%	Fri 27/12/24	Fri 27/12/24	Fri 27/12/24	Fri 27/12/...	0 days	0 days	1241	1246												

Task Critical Task Milestone Summary Page 27

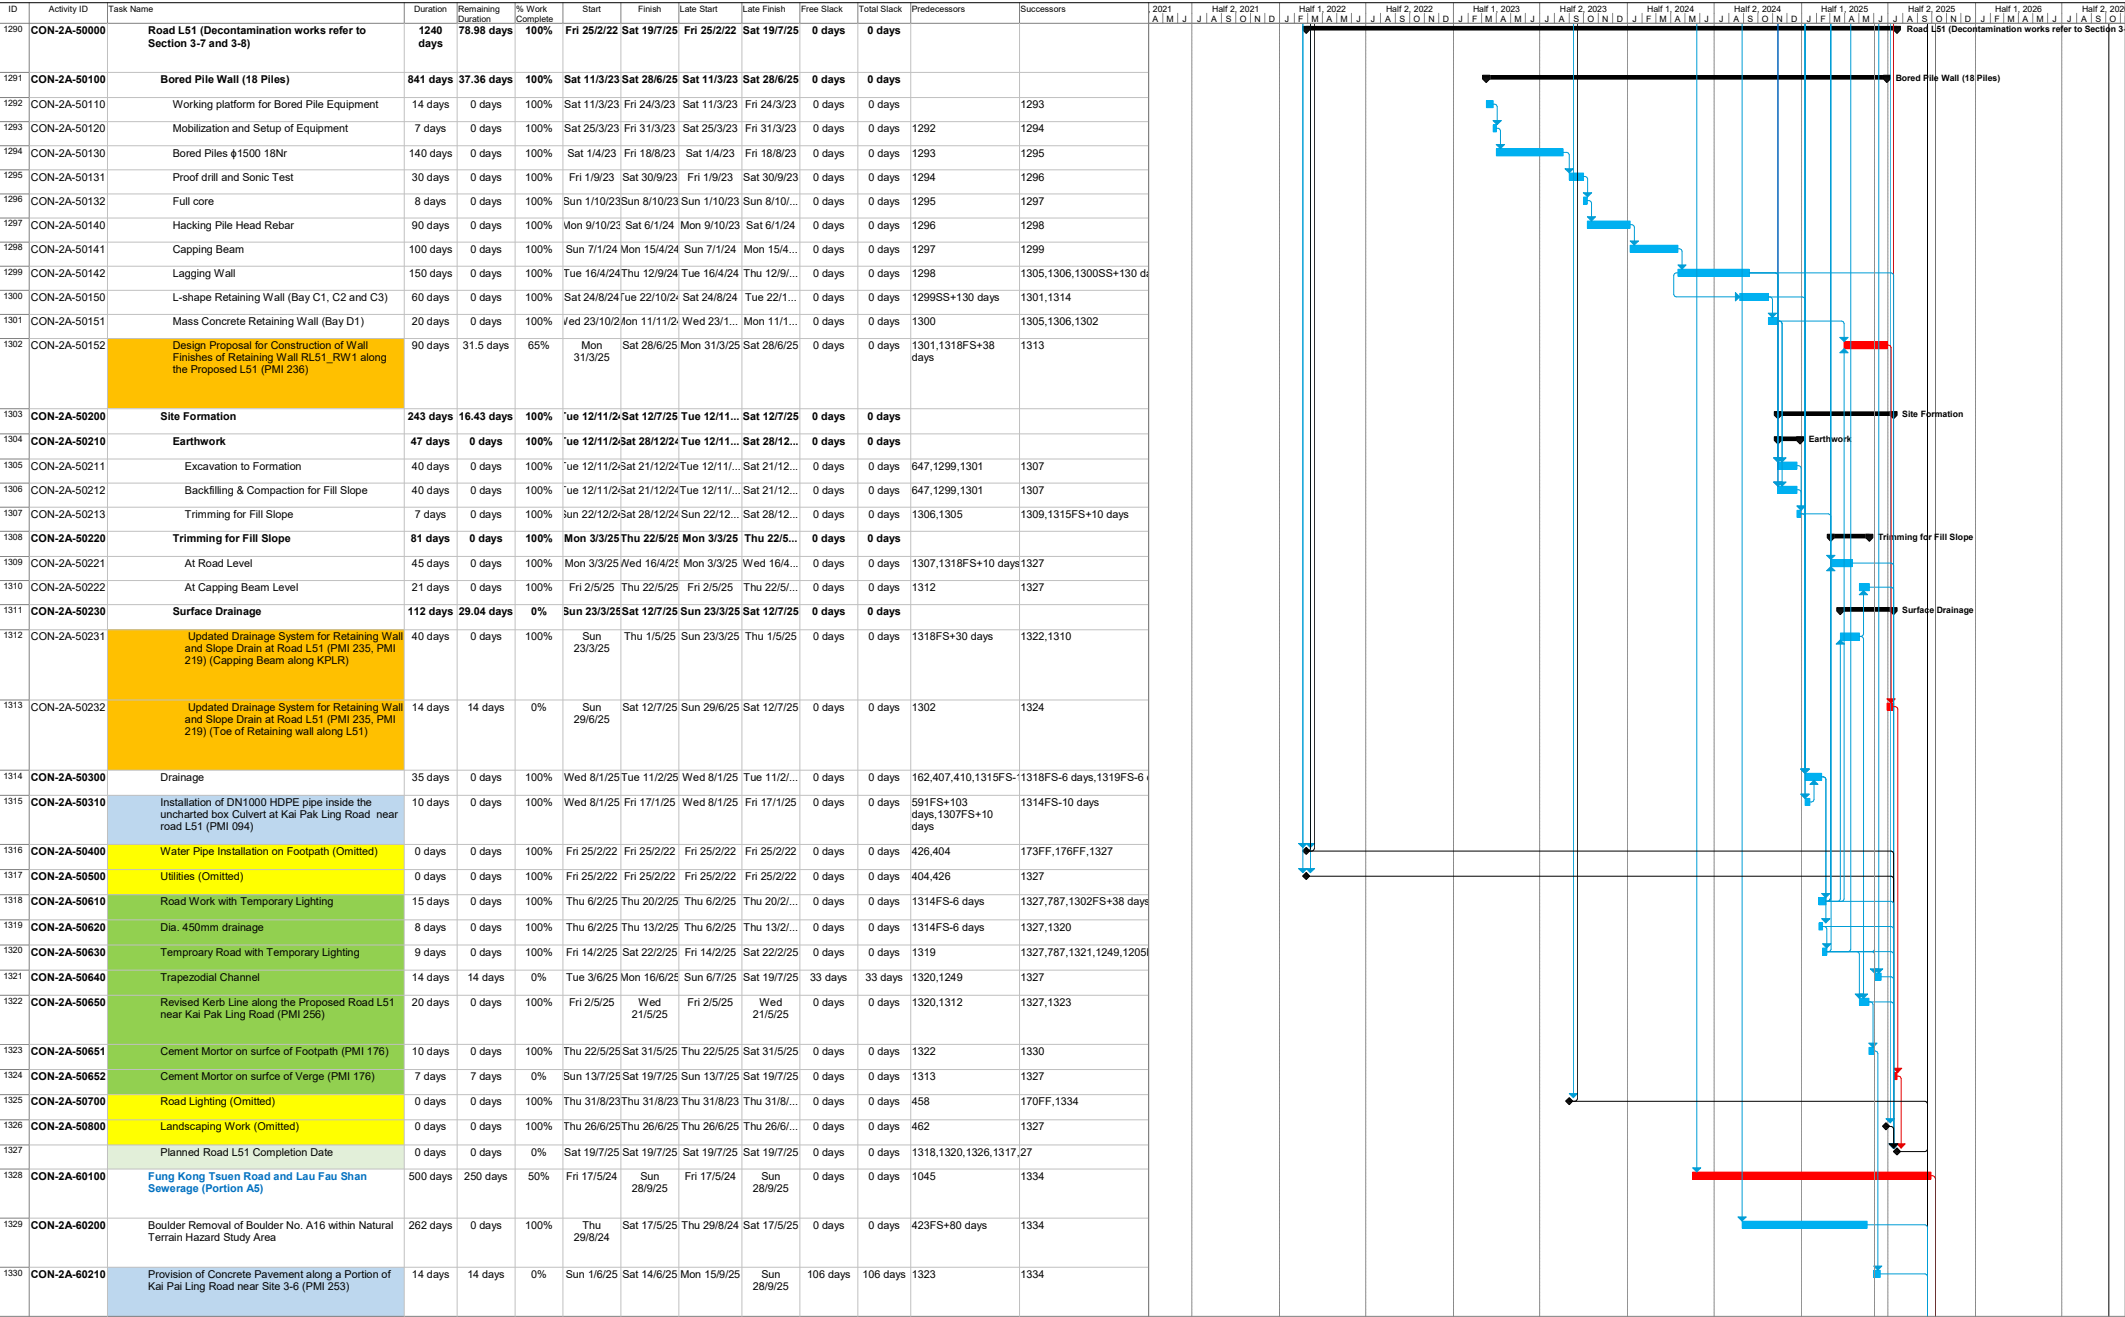

ID	Activity ID	Task Name	Duration	Remaining Duration	% Work Complete	Start	Finish	Late Start	Late Finish	Free Slack	Total Slack	Predecessors	Successors	2021	Half 2, 2021	Half 1, 2022	Half 2, 2022	Half 1, 2023	Half 2, 2023	Half 1, 2024	Half 2, 2024	Half 1, 2025	Half 2, 2025	Half 1, 2026	Half 2, 2026
1331	CON-2A-60300	Site Clearance within the Working Area near the Junction between Kai Pak Ling Road and Fung Kong Tsuen Road (PMI 208, 209, 216)	60 days	0 days	100%	Tue 15/10/24	Fri 13/12/24	Tue 15/10/24	Fri 13/12/24	0 days	0 days		1332												
1332	CON-2A-60350	Preparation of Asbestos Investigation Report and Asbestos Abatement Plan for Removal of Asbestos Containing Material at Fung Kong Tsuen Refuse Collection Point (PMI 270)	70 days	70 days	0%	Tue 1/4/25	Mon 9/6/25	Wed 11/6/25	Tue 19/8/25	0 days	71 days	1331	1333												
1333	CON-2A-60400	Site Formation Works for Refuse Collection Point at Fung Kong Tsuen (PMI 246)	40 days	40 days	0%	Tue 10/6/25	Sat 19/7/25	Wed 20/8/25	Sun 28/9/25	71 days	71 days	1332	1334												
1334	CON-2A-90000	Planned Completion of Section 2A	0 days	0 days	0%	Sun 28/9/25	Sun 28/9/25	Sun 28/9/25	Sun 28/9/...	0 days	0 days	1325,1146,1077,1131	1336,27												
1335		Section 2B	365 days	365 days	0%	Mon 29/9/25	Mon 28/9/26	Mon 29/9/25	Mon 28/9/...	0 days	0 days														
1336	CON-2B-10000	Landscape Softworks and Establishment works under this contract except the corresponding parts to be covered in section 1B of the works	365 days	365 days	0%	Mon 29/9/25	Mon 28/9/26	Mon 29/9/25	Mon 28/9/26	0 days	0 days	1334	1337												
1337	CON-2B-20000	Planned Completion of Section 2B	0 days	0 days	0%	Mon 28/9/26	Mon 28/9/26	Mon 28/9/26	Mon 28/9/...	0 days	0 days	1336	28												
