


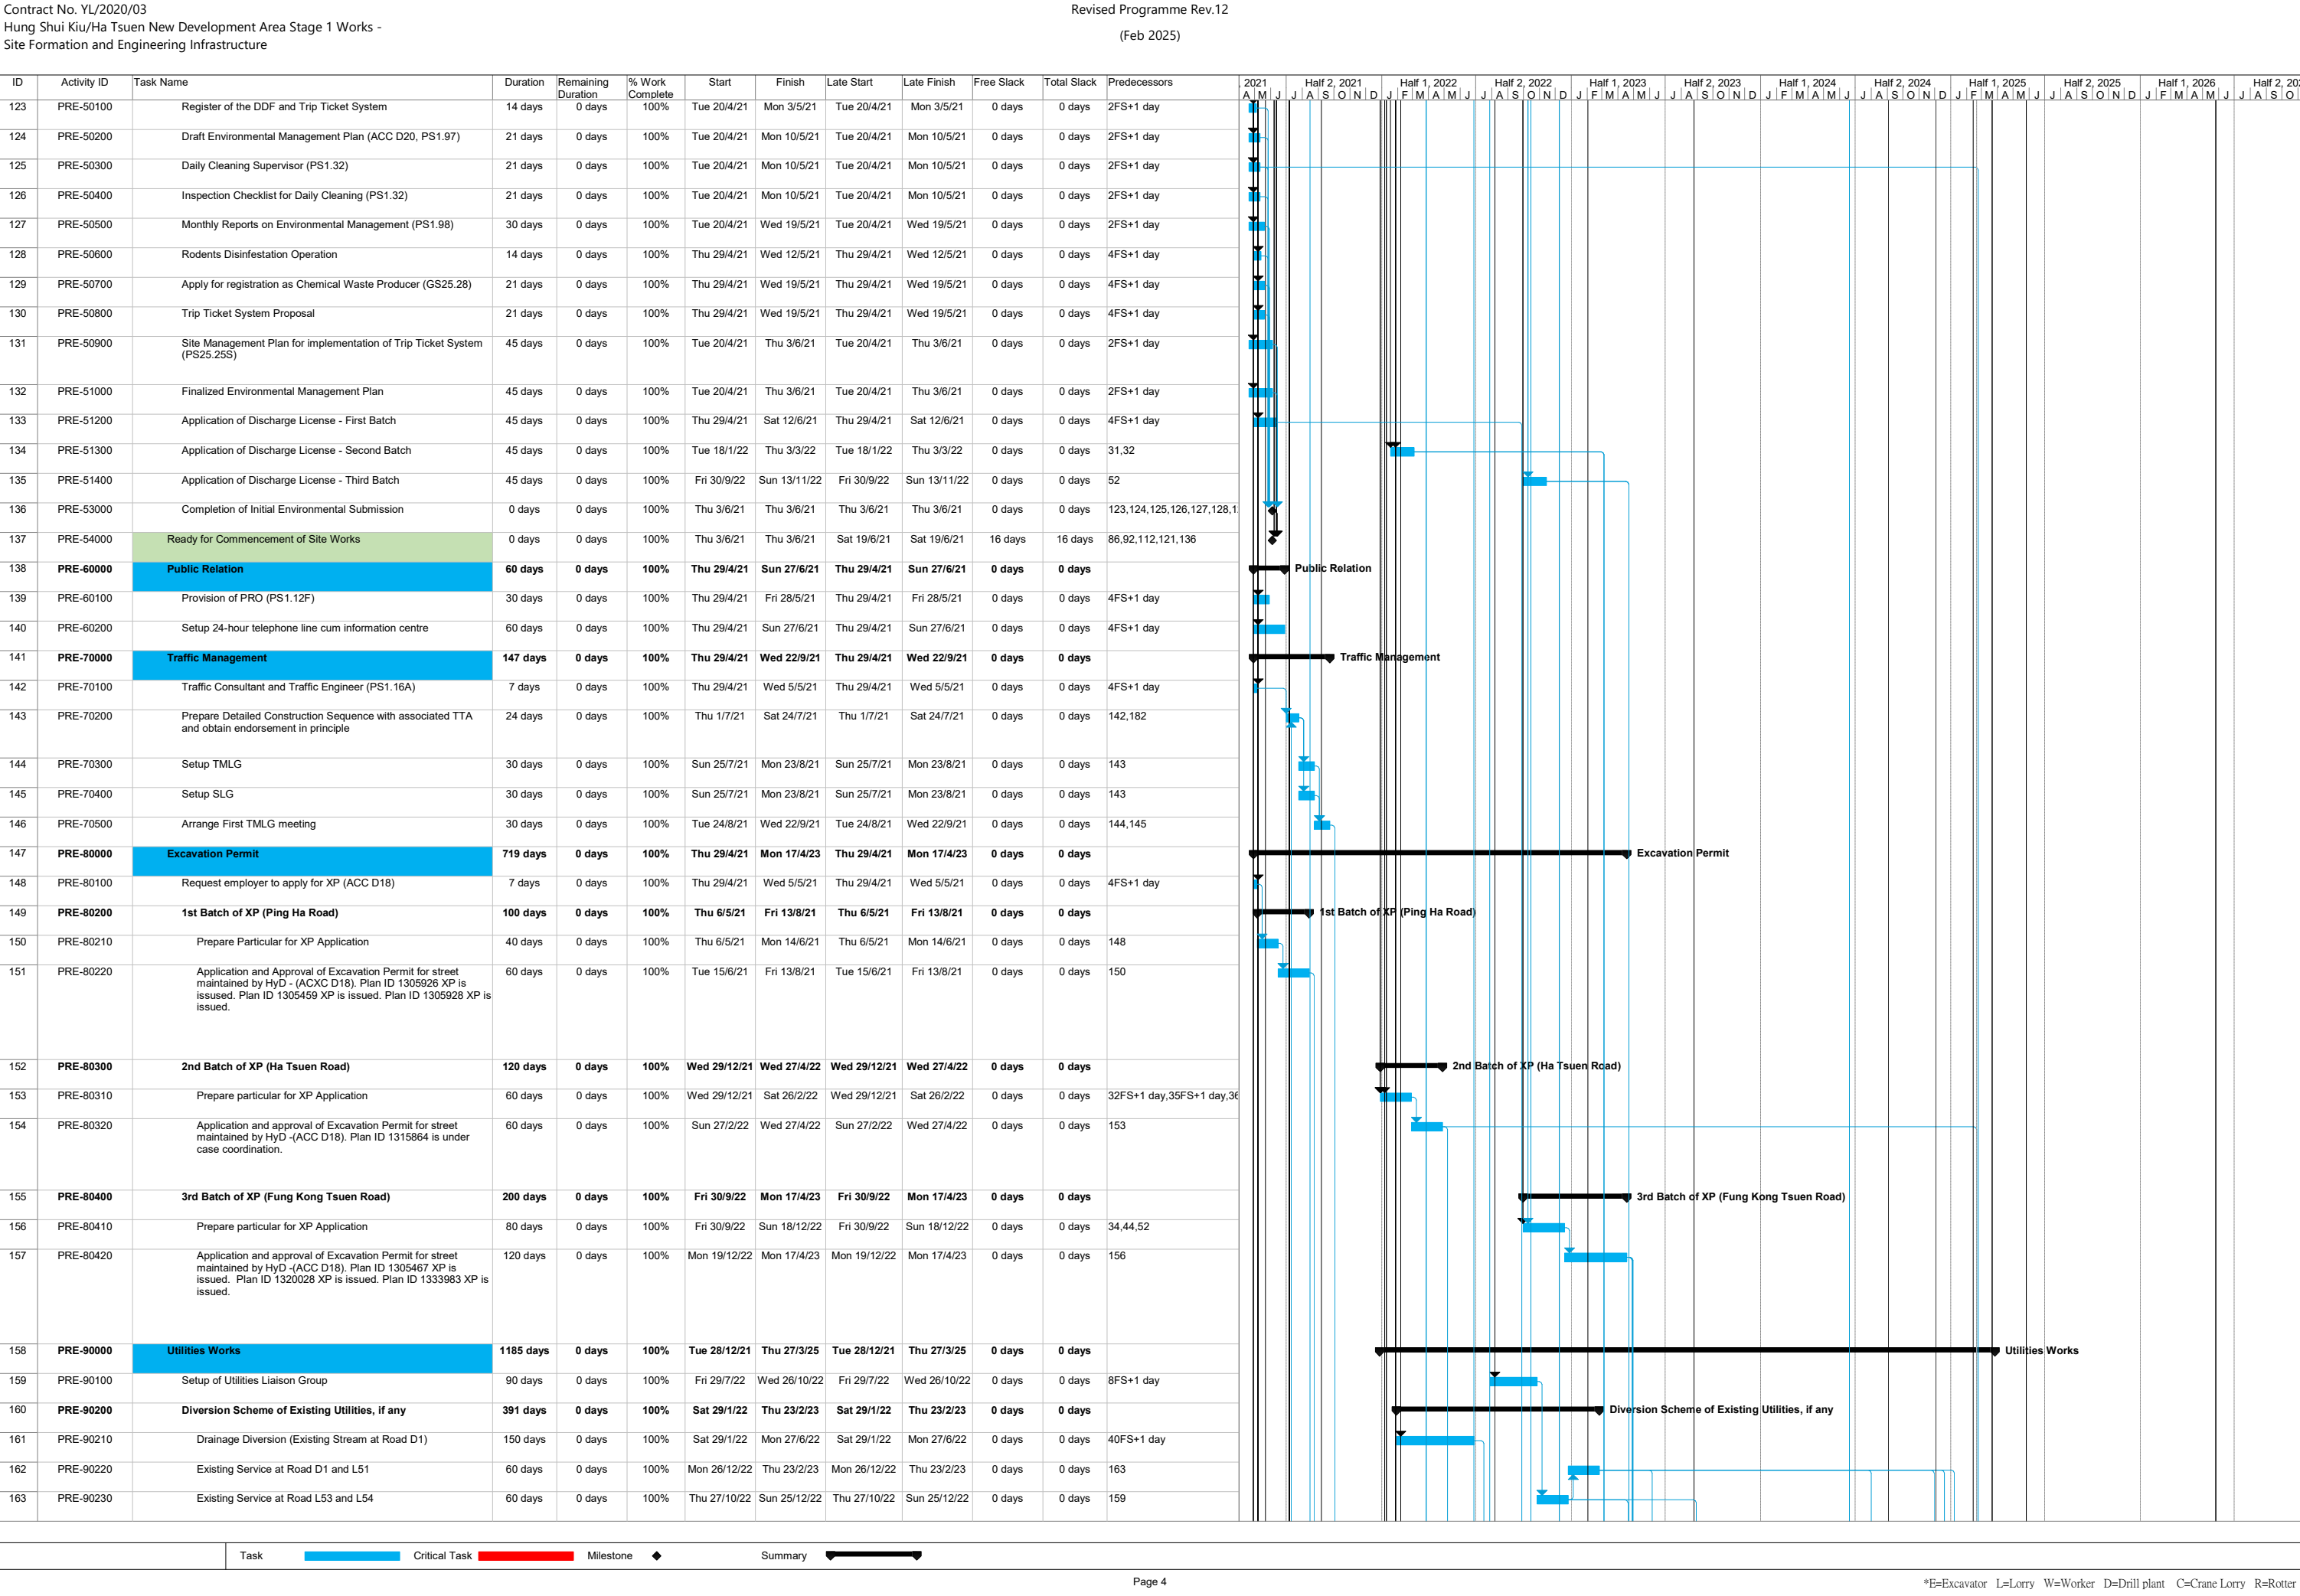

ID	Activity ID	Task Name	Duration	Remaining Duration	% Work Complete	Start	Finish	Late Start	Late Finish	Free Slack	Total Slack	Predecessors	2021 A M J	Half 2, 2021 J A S O N D	Half 1, 2022 J F M A M J	Half 2, 2022 J A S O N D	Half 1, 2023 J F M A M J	Half 2, 2023 J A S O N D	Half 1, 2024 J F M A M J	Half 2, 2024 J A S O N D	Half 1, 2025 J F M A M J	Half 2, 2025 J A S O N D	Half 1, 2026 J F M A M J	Half 2, 2026 J A S O N D
1320	CON-2A-60300	Site Clearance within the Working Area near the Junction between Kai Pak Ling Road and Fung Kong Tsuen Road (PMI 208, 209, 216)	60 days	60 days	0%	Tue 15/10/24	Fri 13/12/24	Mon 27/1/25	Thu 27/3/25	100 days	104 days													
1321	CON-2A-60400	Site Formation Works for Refuse Collection Point at Fung Kong Tsuen (PMI 246)	50 days	50 days	0%	Mon 24/3/25	Mon 12/5/25	Fri 28/3/25	Fri 16/5/25	4 days	4 days	1320												
1322	CON-2A-90000	Planned Completion of Section 2A	0 days	0 days	0%	Fri 16/5/25	Fri 16/5/25	Fri 16/5/25	Fri 16/5/25	0 days	0 days	1315,1140,1071,1125,1099												
1323		Section 2B	365 days	365 days	0%	Sat 17/5/25	Sat 16/5/26	Sat 17/5/25	Sat 16/5/26	0 days	0 days													
1324	CON-2B-10000	Landscape Softworks and Establishment works under this contract except the corresponding parts to be covered in section 1B of the works	365 days	365 days	0%	Sat 17/5/25	Sat 16/5/26	Sat 17/5/25	Sat 16/5/26	0 days	0 days	1322												
1325	CON-2B-20000	Planned Completion of Section 2B	0 days	0 days	0%	Sat 16/5/26	Sat 16/5/26	Sat 16/5/26	Sat 16/5/26	0 days	0 days	1324												
